GOVERNMENT OF PUNJAB

TOURISM, ARCHAEOLOGY & MUSEUMS DEPARTMENT

Priority Sites Progress

Presentation to the Hon'ble Senior Minister Punjab

Progress Overview — Priority Tourism & Heritage Sites

28
Priority Sites

ADP
2026-27 Financial Year

17
Projects completion CFY

Within 6 Months

Jun / Jul 2026 – Dec 2026 with Addl funds Req

12
SCHEMES

TDCP 9 schemes

Light and Sound Show	Completed
Water Sports & Parasailing (39 Mn)	30 Sep 2026
Eco Recreational Park, Kot addu (34 Mn)	30 Sep 2026
Derawar Fort Resort, Cholistan (49.9 Mn)	30 Oct 2026
Changa Manga Resort, Kasur (40 Mn)	30 Nov 2026
Dharabi Dam Resort, Chakwal (184 Mn)	30 Dec 2026
Dhanoi Rest House, KS (102 Mn)	30 Dec 2026
Dharabi Lake Resort (72 Mn)	30 Dec 2026
TDCP Patriata Resort (Component A) 317 Mn	30 Dec 2026

Archaeology 3 schemes

Sher Singh Baradari, Lahore (80 Mn)	15 Sep 2026
Kamran's Baradari, Lahore (43.5 Mn)	15 Sep 2026
St Andrew's Church, Lahore (32 Mn)	30 Oct 2026

Addl Funds Req
Sub Total: 951 Mn

Next 6 Months

Jan 2027 – Jun 2027 with Addl funds Req

5
SCHEMES

TDCP 4 schemes

- TDCP Patriata Chairlift (Component B) — 30 Jun 2027
- Paragliding Club, Chewra Hill Top (190 Mn) — 30 Jun 2027
- TDCP Resort, Jallo, Lahore (357 Mn) — 30 Jun 2027

Archaeology 2 schemes

- Dak Bungalows – Missa Kasowal / Tibbi Syedan (60 Mn) — 31 Mar 2027
- Umar Hayat Mahal, Chiniot (20 Mn) — 30 Jun 2027

Sub Total: 627 Mn

Following 6 Months

Jul 2027 – Dec 2027 with Addl funds Req

4
SCHEMES

- **Archaeology** 4 schemes

Bhera (250 Mn)	30 Sep 2027
Mouj Garh Fort (250 Mn)	31 Dec 2027
Din Garh Fort, Bahawalpur (300 Mn)	31 Dec 2027
Harappa Archaeological Park (400 Mn)	31 Dec 2027

Sub Total: 1,200 Mn

PHASE 4 · BEYOND 12 MONTHS

Uptil June 2028

Jan 2028 – Jun 2028 with Addl funds Req

7
SCHEMES

TDCP 3 schemes

- TDCP Resort, Kallar Kahar (241 Mn) — 30 Jun 2028
- Chairlift at Kotli Sattian (2,000 Mn) — 30 Jun 2028
- Sky Glass Bridge at Punjpeer Rocks (980 Mn) — 30 Jun 2027

Archaeology & LM 4 schemes

- Derawar Fort, Bahawalpur (800 Mn) — 31 Mar 2028
- World Heritage Site, Taxila (200 Mn) — 30 Jun 2028
- Lahore Museum New Block (500 Mn) — 30 Sep 2028
- Lahore Museum Existing Block (500 Mn) — 30 Sep 2028

Sub Total: 5,221 Mn

Procurement of Light and Sound Show Equipment System.

Responsibility: TAM / TDCP
Cost: PKR **150** million

Physical Progress 100%
Financial Progress 100%

Scope of work
1. 3D Mapping Projectors (04) 2. HD Lens (04) 3. Complete Sound System (02 set) 4. Generators 25kva (02) 5. Ups (06) 6. Shezore Vehicles (02) 7. Digital Mapping/ Programing visualization 8. Furniture (Chairs 400)

Progress so far
1. 3D Mapping Projectors (04) HD Lens (04) 2. Complete Sound System (02 set) 3. Generators 25kva (02) 4. Ups (06) 5. Shezore Vehicles (02) 6. Digital Mapping/ Programing visualization 7. Furniture (Chairs 400) **All above items procured & operational, Test Run successfully completed on 6th July 2026.**

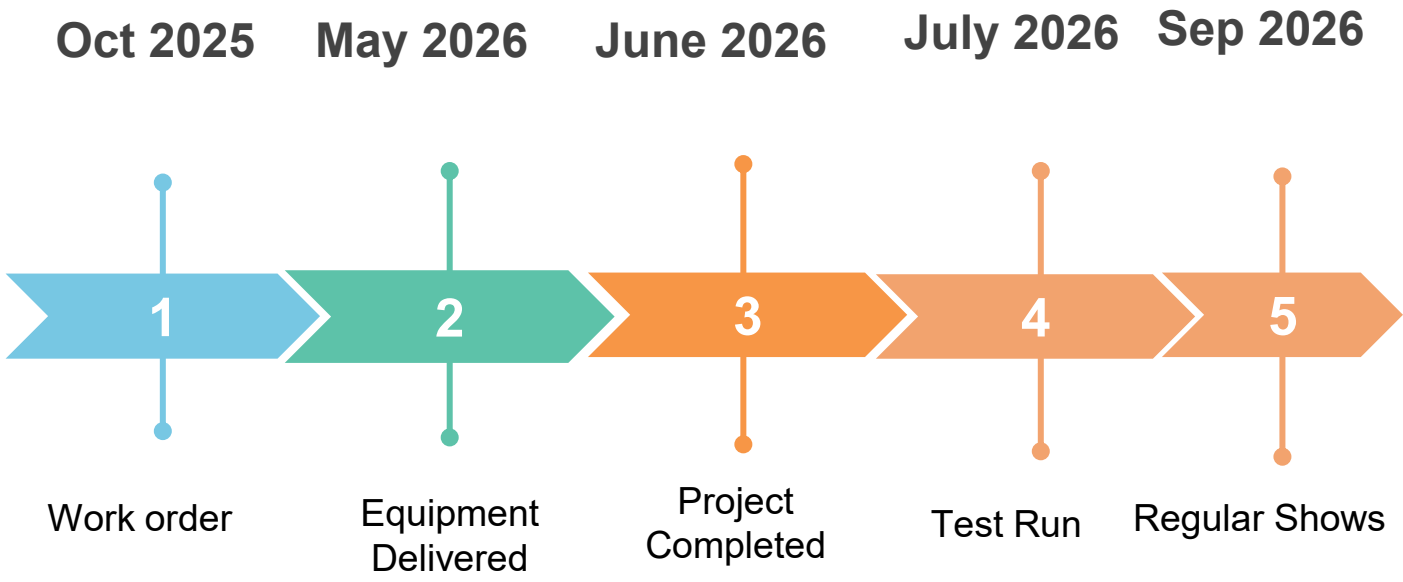

Project Start Date: **13 Oct 2025**
Completion Date: **30 Jun 2026**

Next Plans:
Events shall be started publicly with WCLA from September 2026 onward regularly

Procurement of Light and Sound Show Equipment System.

Procurement of Light and Sound Show Equipment System.

Physical Progress: 100%

Procurement of Light and Sound Show Equipment System.

13-14 August 2026 Show

Back

Provision of Water Sport, Parasailing and Speed Boats at Dharabi Lake, District Chakwal

Responsibility: TAM / TDCP
Cost: PKR **300.000** million

Scope of work
1. Jetski (08)
2. Floating Jetty (02)
3. Speed Boats (05)
4. Parasailing Boats (03)
5. PVC Tarpaulin towing Boats (15)

Progress so far
1. Jetski (All Procured & operational at site)
2. Floating Jetty (All Procured & operational at site)
3. Speed Boats (All Procured & operational at site)
4. Parasailing Boats procured
5. Inflatable towable Boats procured (pump delivery awaited)

Physical Progress	**98%**
Financial Progress	**80%**
Allocation CFY 2026-27:	**20M**
Additional Funds Req:	**38.758M**

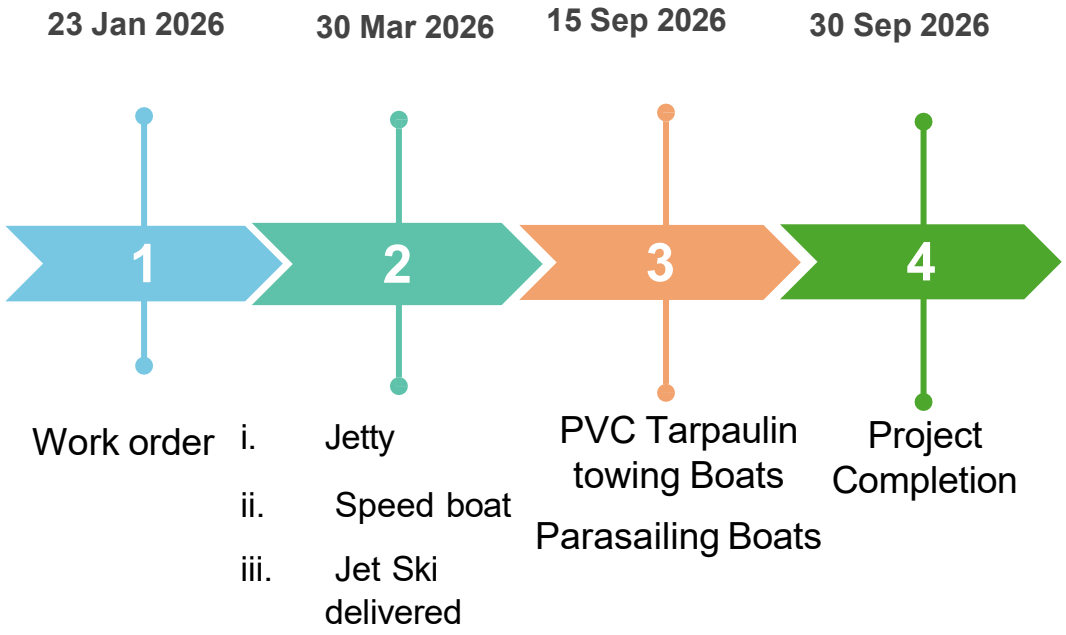

Project Start Date:	**21 Jul 2025**
Completion Date:	**30 June 2026**
Completion Date by TAM:	**30 Sep 2026**

Next 30 Days Plans:
Delivery of infalatable pump

Back

Components of the Project

Component Name	Physical Progress	Expected Completion	Status
Floating Jetty	100%	20-06-2026	On Track
Jetski	100%	20-06-2026	On Track
Speed Boat	100%	20-06-2026	On Track
Parasailing Boat	100%	30-09-2026	On Track
inflatable Towable Boats	98%	15-09-2026	On Track

On Track
Delayed
Critical

Provision of Water Sport, Parasailing and Speed Boats at Kallar Kahar Lake, District Chakwal.

Floating Jetty

Physical Progress: 100%

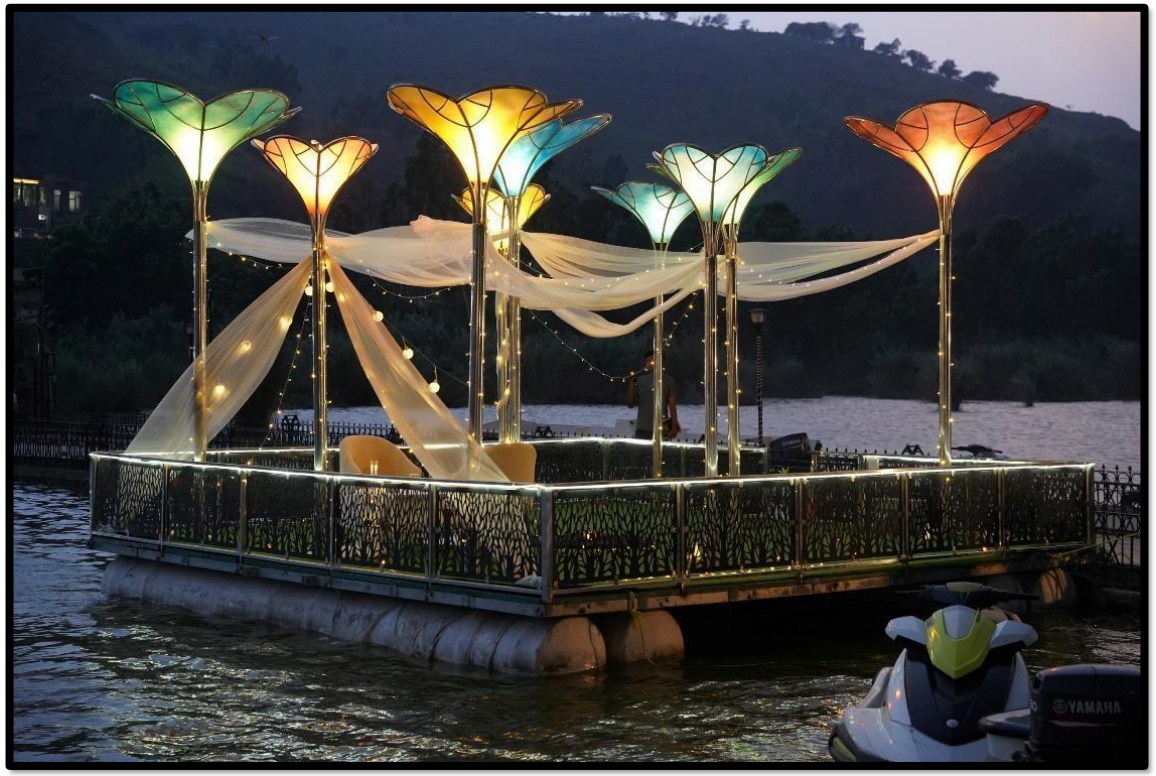

Provision of Water Sport, Parasailing and Speed Boats at Kallar Kahar Lake, District Chakwal.

Water Sports Kallar Kahar

TOURISM DEVELOPMENT CORPORATION OF PUNJAB
TOURISM, ARCHAEOLOGY AND MUSEUMS DEPARTMENT, GOVERNMENT OF THE PUNJAB

Provision of Water Sport, Parasailing and Speed Boats at Kallar Kahar Lake, District Chakwal.

Jetski & Speed boat

Physical Progress: 100%

Provision of Water Sport, Parasailing and Speed Boats at Kallar Kahar Lake, District Chakwal.

Parasailing and Inflatable Towable Boats

Completion Date: 30.09.2026

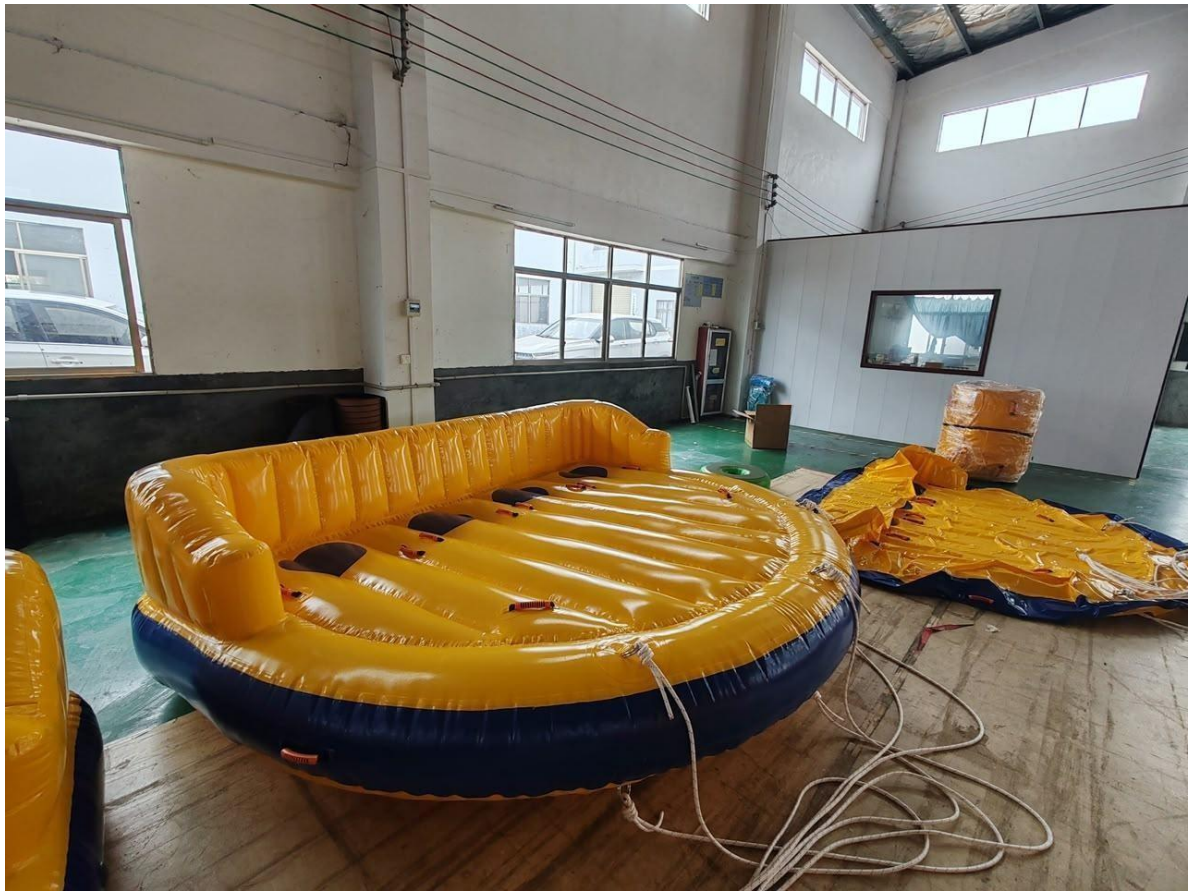

Improvement, Revitalization, and Upgradation of TDCP Tourist Resort Derawar Fort Cholistan, District Bahawalpur.

Responsibility: TAM / C&W / TDCP
Cost: PKR **126.440** million

Scope of work
1. Renovation of Restaurant
2. Renovation of Chalets (03)
3. Provision of Gazebo (04)
4. Construction of Toilet Block (04)
5. Parking
6. Tuff tiling
7. BBQ Area (01)
8. Construction of Fountain

Progress so far
1. Renovation of Restaurant (civil work in progress) 95%
2. Renovation of Chalets (civil in progress) 90%
3. Gazebo 04/04 installed 100%
4. Construction of Toilet Block (completed)100%
5. Parking (completed)100%
6. Tuff tiling (installation in progress) 98%
7. BBQ Area (civil work in progress) 80%
8. Construction of Fountain (civil work in progress) 70%

Physical Progress	**79%**
Financial Progress	**59%**
Allocation CFY 2026-27:	**20 Mn**
Additional Funds Demand	49.98Million

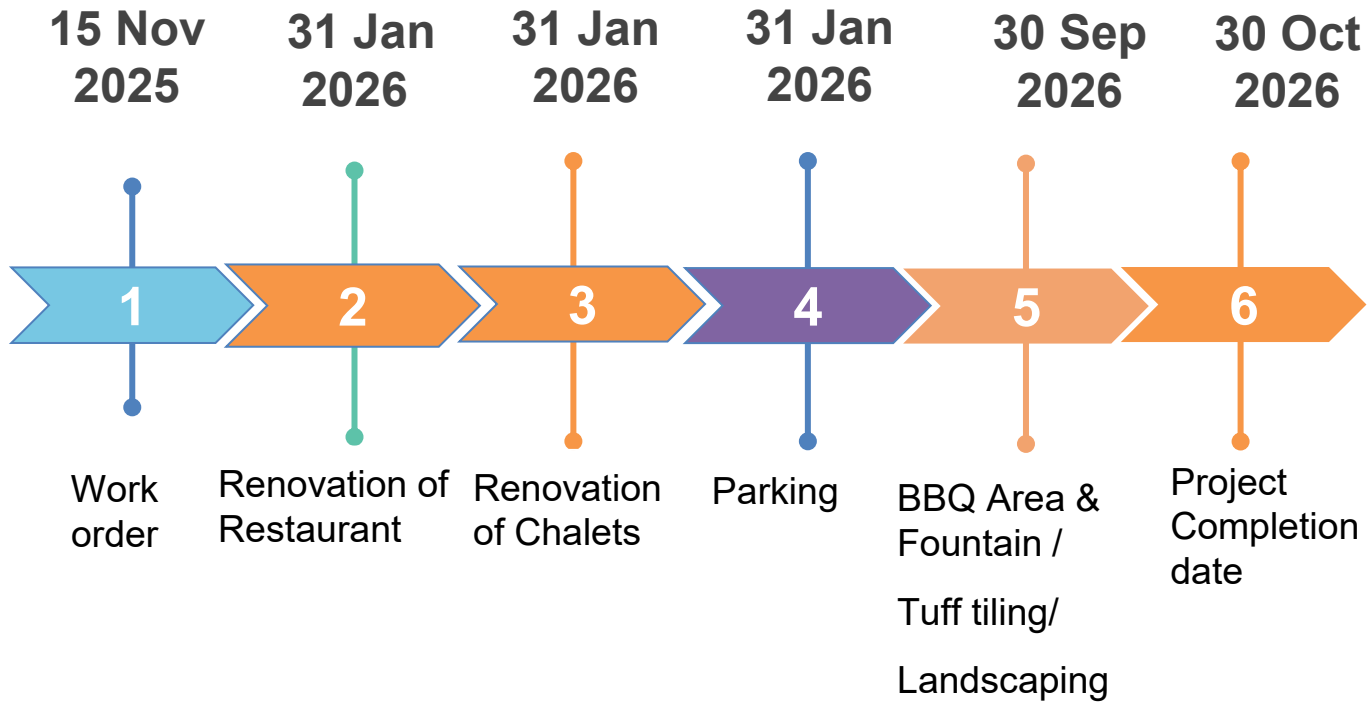

Project Start Date: **27 Jun 2025**
Completion Date by PC1: **31 Dec 2026**
Completion Date by TAM: **30 Oct 2026**

Next 30 Days Plans:
BBQ Area completed on 30 Sep 2026
Fountain completed on 30 Sep 2026

Back

Components of the Project

Component Name	Physical Progress	Expected Completion	Status
Renovation of Restaurant	95%	30-09-2026	On Track
Renovation of Chalets	90%	30-09-2026	On Track
Parking & tuff tiling	98%	30-09-2026	On Track
Gazebo	100%	30-09-2026	On Track
Construction of Toilet Block (04)	100%	30-09-2026	On Track
Landscaping	1%	30-10-2026	On Track
BBQ area	80%	30-09-2026	On Track
Fountain	70%	30-09-2026	On Track

- On Track
- Delayed
- Critical

Improvement, Revitalization, and Upgradation of TDCP Tourist Resort Derawar Fort Cholistan, District Bahawalpur.

Renovation of Restaurant

Physical Progress: 95%

Work in Progress

Improvement, Revitalization, and Upgradation of TDCP Tourist Resort Derawar Fort Cholistan, District Bahawalpur.

Renovation of Restaurant

Physical Progress: 95%

Work in Progress

Improvement, Revitalization, and Upgradation of TDCP Tourist Resort Derawar Fort Cholistan, District Bahawalpur.

Renovation of Chalets

Physical Progress: 90%

Work in Progress

Improvement, Revitalization, and Upgradation of TDCP Tourist Resort Derawar Fort Cholistan, District Bahawalpur.

Physical Progress: 90%

Renovation of Chalets

Work in Progress

Improvement, Revitalization, and Upgradation of TDCP Tourist Resort Derawar Fort Cholistan, District Bahawalpur.

Physical Progress: 90%

Renovation of Chalets

Work in Progress

Improvement, Revitalization, and Upgradation of TDCP Tourist Resort Derawar Fort Cholistan, District Bahawalpur.

Physical Progress: 90%

Renovation of Chalets

Work in Progress

Improvement, Revitalization, and Upgradation of TDCP Tourist Resort Derawar Fort Cholistan, District Bahawalpur.

Rooms

Physical Progress: 100%

Work Completed

Improvement, Revitalization, and Upgradation of TDCP Tourist Resort Derawar Fort Cholistan, District Bahawalpur.

Physical Progress: 70%
Completion Date: 30.9.2026

FOUNTAIN

Work In Progress

Back

Improvement, Revitalization, and Upgradation of TDCP Tourist Resort Derawar Fort Cholistan, District Bahawalpur.

Physical Progress: 80%
Completion Date: 30.9.2026

BBQ AREA

Work In Progress

Back

Improvement, Revitalization, and Upgradation of TDCP Tourist Resort Derawar Fort Cholistan, District Bahawalpur.

Derawar TDCP Resort

Project Status & Reasons for Delay

Dining Hall Washrooms: Floor tiles of **8 washrooms are still pending**; no labour was working today.
Fountain: Work has **not started**.
Bar-B-Q Setup: Welding work is in progress.
Chalets: Roof work is also pending on chalets.
Out of **14 rooms, only 9 are complete; 5 rooms remain pending**.
Green Work: Only **1% completed**; no significant green work has been carried out, except a small area of planting/landscaping.
Site Condition: Termite infestation, damaged ceiling, broken glass doors/windows, and damaged marble have been observed.
Fountain work is also pending.
Monitoring: CCTV is not installed, internet connectivity is an issue, and there is **no proper system for daily report/dashboard updates**.

Site Focal Person	Phone Number
Haider Shah	03025553132

Back

6.Up-Gradation of Kot Addu Eco Friendly Recreational Park Kot Addu-Taunsa

Responsibility: TAM / TDCP
Cost: PKR **52.470** million

Physical Progress 96%
Financial Progress 76%
Allocation CFY 2026-27: 10 Mn
Additional Funds Demand: 33.522 Mn

Scope of work

1. Guest House 08-Nos
2. Landscaping
3. Electric Work
4. Septic Tank
5. Development of Sitting Paragolas
6. Protective Bund
7. 2 Nos Main Gate

Progress so far

1. Construction of 08-Nos Guest House is 90%
2. Landscaping Nearing Complition
3. Electric work is in progress (street light or in 02 Guest House)
4. Septic Tank Completed
5. Landscape development is in progress
6. Development of sitting pergolas in progress
7. Gates Completed

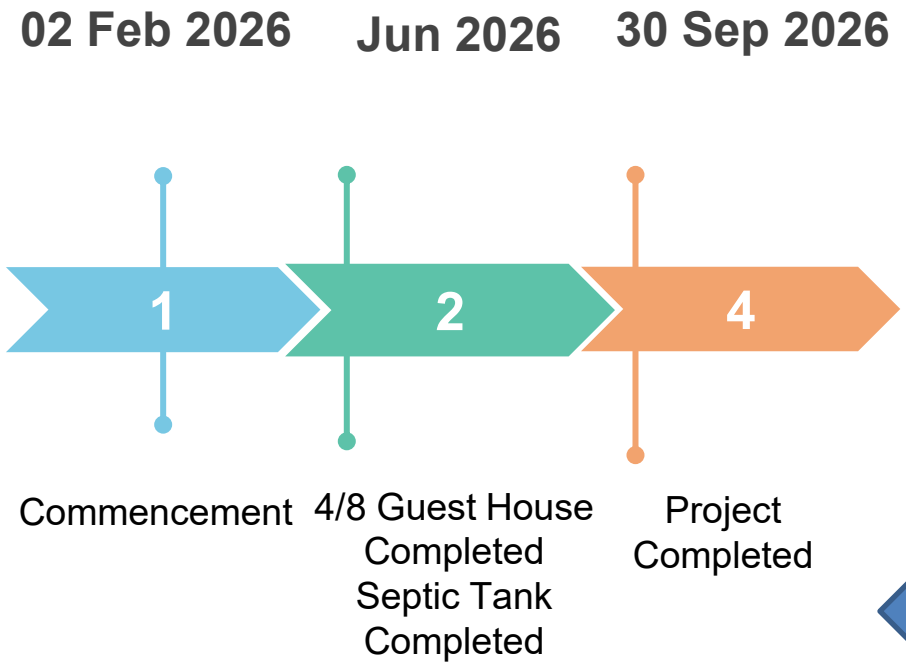

Back

Project Start Date: **02 February 2026**
Completion Date as per PC1: **15 September 2026**
Completion Date as TAM: **30 September 2026**

Next 30 Days Plans:

Remaining 2-Nos Guest House (Stone + Electrical Work + Finishing) will completed on	30 Sep 2026
Landscaping completed on	30 Sep 2026
Development of Sitting Paragolas completed on	30 Sep 2026

Components of the Project

Component Name	Physical Progress	Expected Completion	Status
Guest Houses	90%	30-09-2026	On Track
Electric Work	95%	30-09-2026	On Track
External Works (Main Gate, Protection Bund, Street Lights etc)	90%	30-09-2026	On Track
Landscaping	85%	30-09-2026	On Track

- On Track
- Delayed
- Critical

Up-Gradation of Kot Addu Eco Friendly Recreational Park Kot Addu-Taunsa

Construction of 08-Nos Guest House

Proposed

Work in Progress

Up-Gradation of Kot Addu Eco Friendly Recreational Park Kot Addu-Taunsa

Construction of 08-Nos Guest House (Internal)

Completed

Up-Gradation of Kot Addu Eco Friendly Recreational Park Kot Addu-Taunsa

Construction of 08-Nos Guest House (Internal)

Completed

Up-Gradation of Kot Addu Eco Friendly Recreational Park Kot Addu-Taunsa

Landscaping (Bamboo)

Proposed

Completed

Up-Gradation of Kot Addu Eco Friendly Recreational Park Kot Addu-Taunsa

Landscaping (Bamboo)

Proposed

Completed

Up-Gradation of Kot Addu Eco Friendly Recreational Park Kot Addu-Taunsa

Waterfall

Proposed

Work in Progress

Up-Gradation of Kot Addu Eco Friendly Recreational Park Kot Addu-Taunsa

Gate

Proposed

Completed

Up-Gradation of Kot Addu Eco Friendly Recreational Park Kot Addu-Taunsa

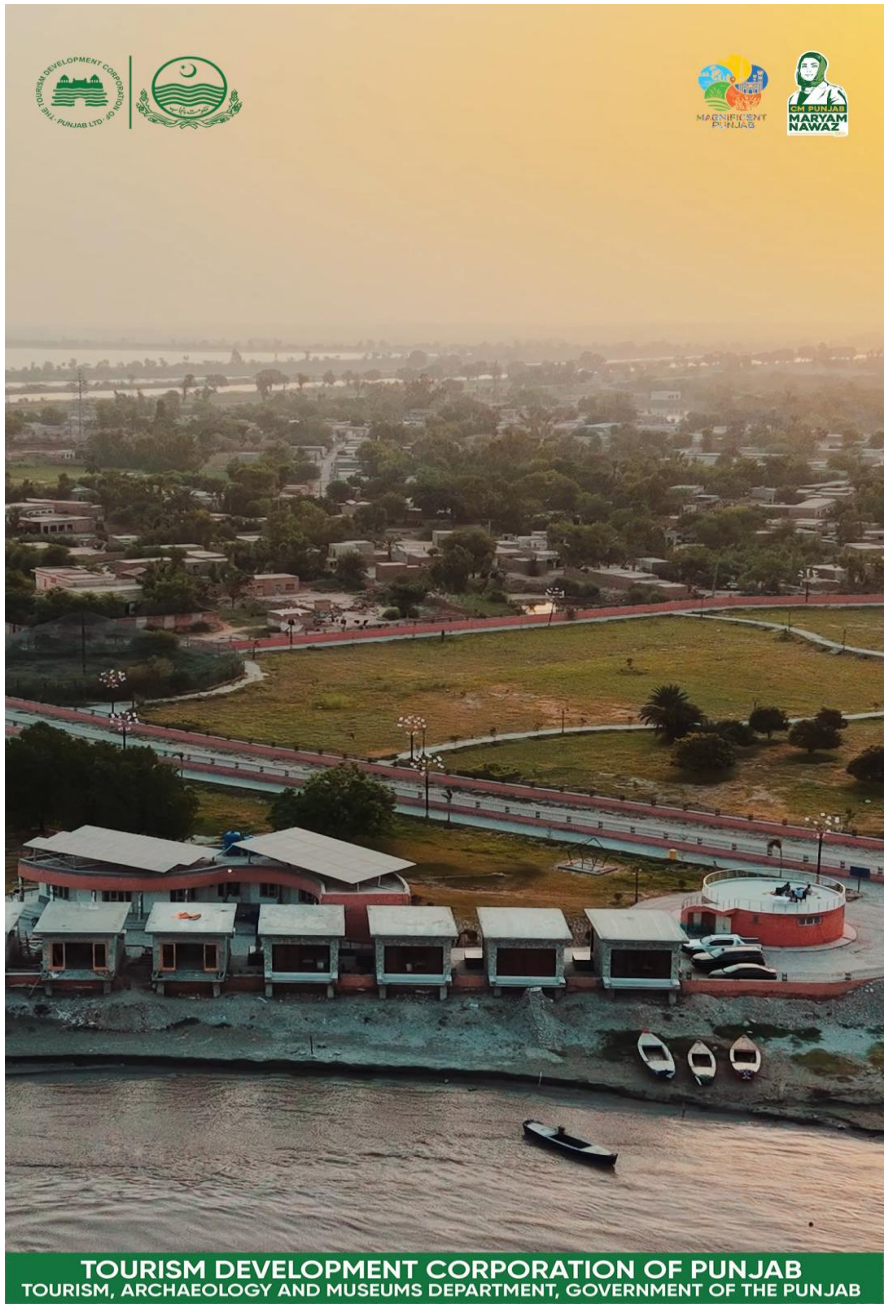

Up-Gradation of Kot Addu Eco Friendly Recreational Park Kot Addu-Taunsa

Project Status & Reasons for Delay

- MD Sir visited the site approximately two weeks ago and provided instructions regarding certain changes and finishing work.
- He also instructed to change the globes/light fixtures, due to which some additional work was required.
- Due to these changes and additional instructions, a slight delay has occurred.* Finishing work is still pending in four guest houses.
- There is a minor issue with the washroom lights in two guest houses, which is currently being rectified.
- Other electrical work is in progress at the site.* Globe/light fixture work is still pending.
- The protective band work is currently under process and has caused a slight delay.

Back

8.Improvement, Revitalization and Upgradation of TDCP Tourist Resort Changa Manga, District Kasur

Responsibility: TAM / TDCP

Cost: PKR **243.21** million

Scope of Work

1. Revamping of Guest Houses 3 Nos
2. Installation of Gazebos 8 Nos
3. Upgradation of Restaurant 1 Nos
4. Construction of Bonfire area 2 Nos
5. Construction of Bamboo Houses 4 Nos
6. Construction of Tree Houses 2 Nos
7. Car Parking & Main Gate 2 Nos
8. Landscaping & Outdoor Lighting

Progress so far

1. 02 std and deluxe complete; 01 VIP black stone, window and fixture remaining
2. 8 Gazebos installed, polish and sitting remaining
3. Restaurant area OT Tiles in progress & window & door polish and paint work is remaining
4. Sitting stone left; bonfire area left
5. 4 Construction of Bamboo Houses external cladding and Inner cladding completed & glass of windows & doors, & paint work left
6. Tree Houses woodwork completed & polish & paint remaining 2 Nos
7. Main Gate 2 Nos delivered to site and installation is in progress
8. Landscaping in progress & Outdoor Lighting in progress

Physical Progress 70%
Financial Progress70%
Allocation CFY 2026-27: 60.846 Mn
Additional Funds Demand: 40.016 Mn

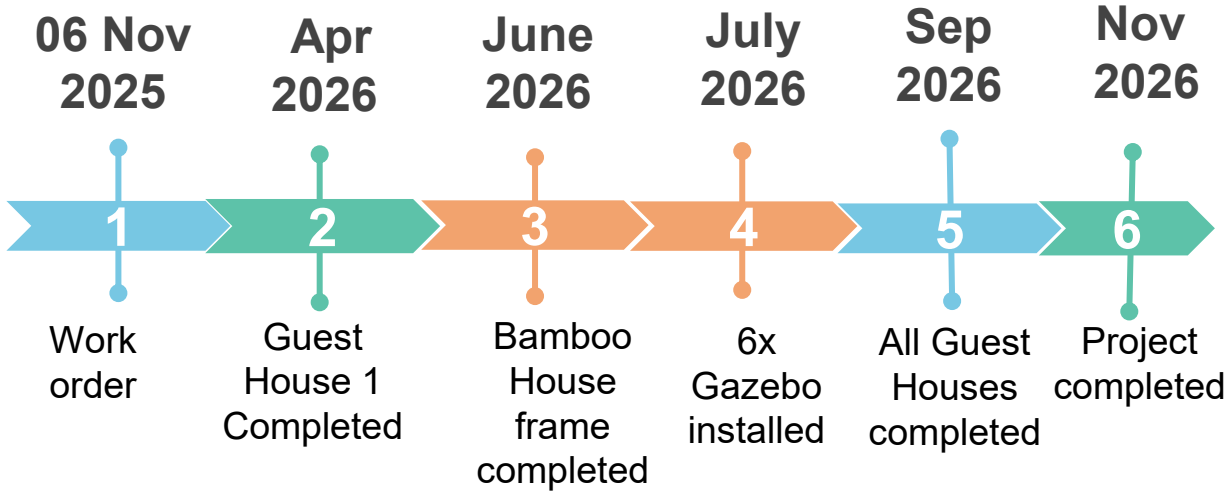

Project Start Date: **24 September 2025**
Completion as per PC-1: **30 June 2026**
Completion Date as per TAM: **30 November 2026**

Next 30 Days Plans:

All Guest Houses completion	20 Sep 2026
Main entrance & Gate completion	30 Sep 2026

Back

Components of the Project

Component Name	Physical Progress	Expected Completion	Status
Guest Houses 3 Nos	80%	20-09-2026	On Track
Gazebo 8 Nos	85%	20-09-2026	On Track
Restaurant	65%	30-09-2026	On Track
Bonfire Area 2 Nos	75%	30-09-2026	Delayed
Bamboo Houses 4 Nos	80%	20-09-2026	On Track
Tree Houses 2 Nos	65%	20-09-2026	On Track
Main Gate	65%	30-09-2026	On Track
Landscaping & Outdoor Lighting	50%	20-09-2026	On Track

● = On Track
● = Delayed
● = Critical

TDCP Resort **Changa Manga**

TDCP Resort **Changa Manga**

Physical Progress:80%
Completion Date: 20-09-2026

VIP Guest House

Proposed

Work in Progress

TDCP Resort **Changa Manga**

VIP Guest House

Physical Progress:80%
Completion Date:20-09-2026

Proposed

Work in Progress

TDCP Resort **Changa Manga**

VIP Guest House

Physical Progress:80%
Completion Date:20-09-2026

Proposed

Work in Progress

TDCP Resort **Changa Manga**

Physical Progress:80%
Completion Date:20-09-2026

VIP Guest House

Proposed

Work in Progress

TDCP Resort **Changa Manga**

Physical Progress: 95%
Completion Date: 20-09-2026

Standard Suite

Work in Progress

Work in Progress

TDCP Resort **Changa Manga**

Physical Progress:80%
Completion Date:20-09-2026

Deluxe Suite

Proposed

Work in Progress

TDCP Resort **Changa Manga**

Gazebos

Physical Progress:85%
Completion Date:20-09-2026

Work in Progress

Work in Progress

TDCP Resort **Changa Manga**

Restaurant

Physical Progress:65%
Completion Date:30-09-2026

Proposed

Work in Progress

TDCP Resort **Changa Manga**

Bonfire Area

Physical Progress:75%
Completion Date:30-09-2026

Proposed

Work in Progress

TDCP Resort **Changa Manga**

Bamboo House

Physical Progress:80%
Completion Date:20-09-2026

Proposed

Work in Progress

TDCP Resort **Changa Manga**

Tree House

Physical Progress:65%
Completion Date:20-09-2026

Proposed

Work in Progress

TDCP Resort **Changa Manga**

Main Entrance

Physical Progress:65%
Completion Date:30-09-2026

Proposed

Work in Progress

TDCP Resort **Changa Manga**

Physical Progress:50%
Completion Date:20-09-2026

Landscaping & Outdoor Lighting

Proposed

Work in Progress

TDCP Resort **Changa Manga**

Landscaping & Outdoor Lighting

Physical Progress:50%
Completion Date:20-09-2026

Proposed

Work in Progress

TDCP Resort **Changa Manga**

Landscaping & Outdoor Lighting

Physical Progress:50%
Completion Date:20-09-2026

Proposed

Work in Progress

TDCP Resort **Changa Manga**

Physical Progress:50%
Completion Date:20-09-2026

Landscaping & Outdoor Lighting

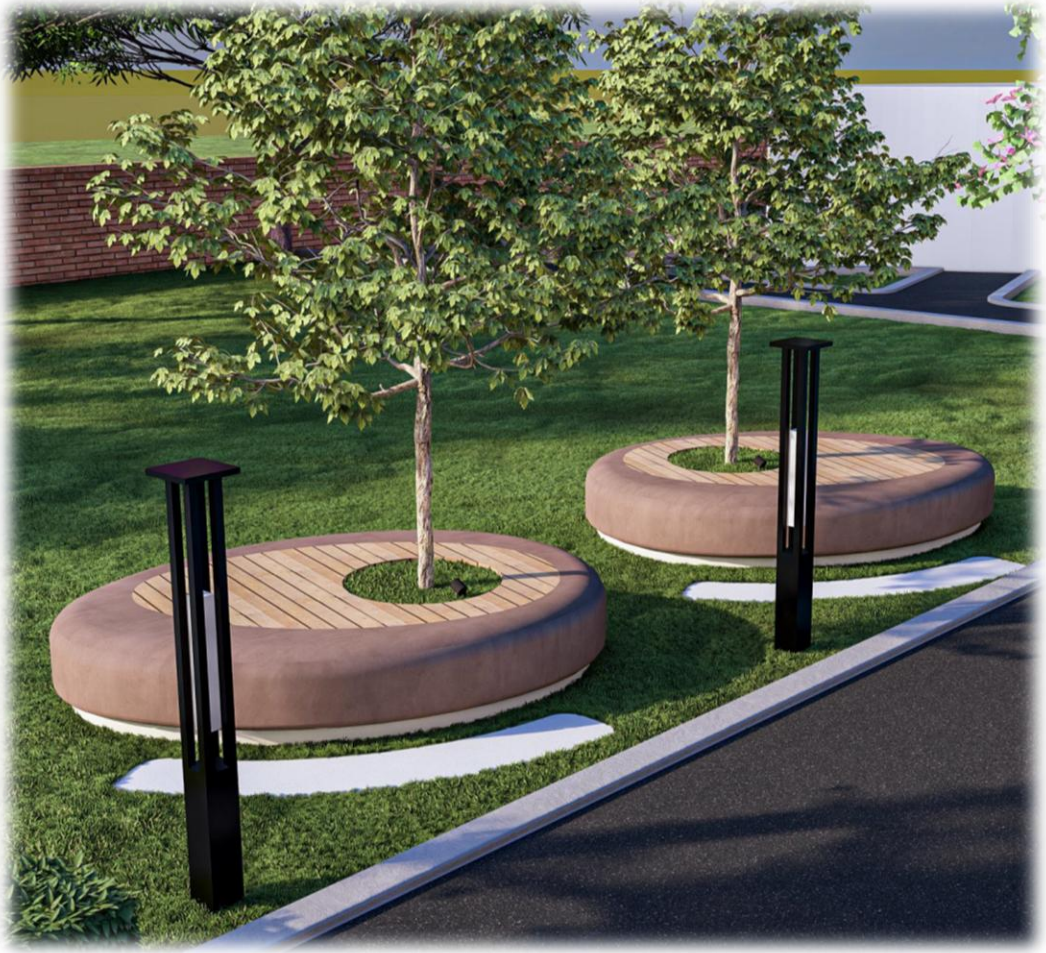

Proposed

Work in Progress

TDCP Resort **Changa Manga**

Landscaping & Outdoor Lighting

Physical Progress:50%
Completion Date:20-09-2026

Proposed

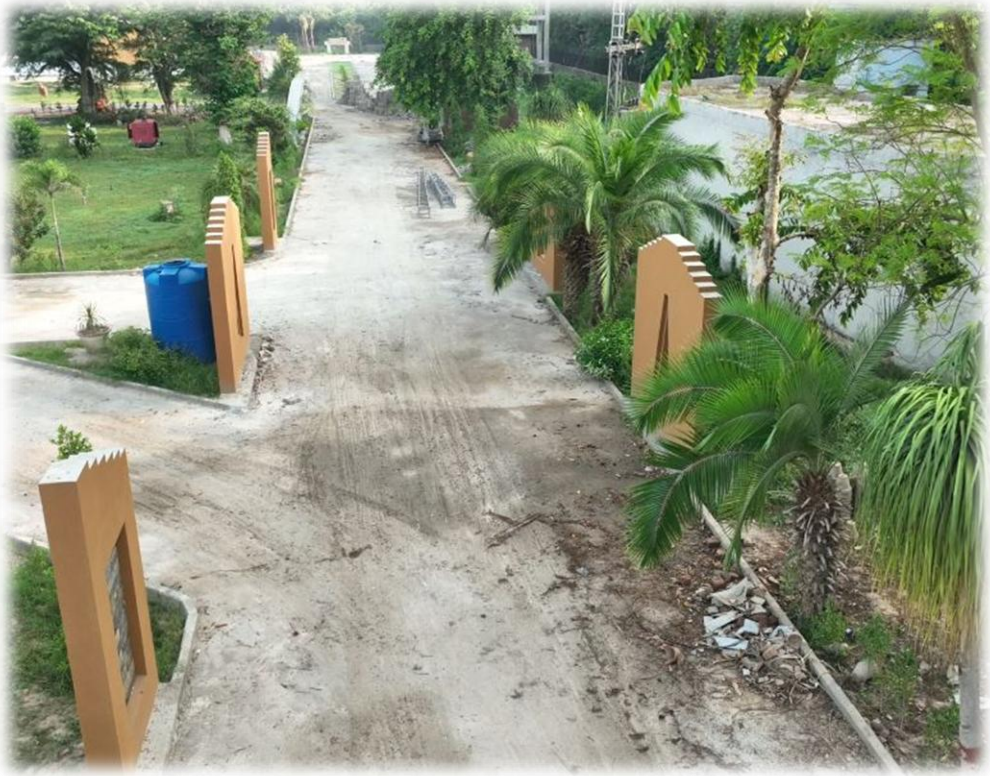

Work in Progress

Back

Remarks for Changa Manga Resort:

- The stone of sitting area of the Bonfire area (stone work) is pending and not started since July 25.
- Restaurant area work the paint and polish of doors, windows, and thatch roofing is pending as the pace is slow
- Gate stone work is also progressing very slowly.
- Overall the work progress is quite slow.

- Before the expected completion date was 30 October 2026 now it is 31st November 2026

Site Focal Person	Phone Number
Rizwan Tahir	+92 321 4149788

Back

Improvement, Revitalization and Upgradation of TDCP Tourist Resort Dharabi Dam, District Chakwal

Responsibility: TAM / TDCP

Cost: PKR **380.735 Million**

Scope of work

1. Renovation of main building (01 No)
2. Renovation of chalets (02 No)
3. Construction of chalets (01 Nos.)
4. Construction of rooms (08 Nos.)
5. 04 Nos. Suit
6. Restaurant development (01 No.)
7. Jetty area Viewing deck (01 No.)
8. External Development/ Parking tuff tiling (01 No.)
8. Gazebos (05 Nos.)
9. Fountain / viewing deck (01 No.)
10. Landscaping and site development

Progress so far

1. **Main Building:** Structure completed, Wash room tiles finishing is in progress.
2. **03 Nos. Chalets:** 02 Renovation near completion, one under construction.
3. **08 Nos. Rooms:** Finishing works in progress- paint, windows and Doors left.
4. **04 Nos. Suite** structure completed finishing left
5. **Restaurant:** Kitchen tiles in progress.
6. **Viewing Deck:** Base done structure left
7. **Parking:** Tuff tiling in progress.
8. **05 Gazebos:** 01 Bases completed, others leveling done .
9. **Fountain:** Development yet to start.
10. **Landscaping:** Site development in progress.

Physical Progress	50%
Financial Progress	40%
Allocation CFY 2026-27:	100 Mn
Additional Funds Demand:	183.901 Mn

29 Jan 2026 **30 Jun 2026** **15 Aug 2026** **30 Dec 2026**

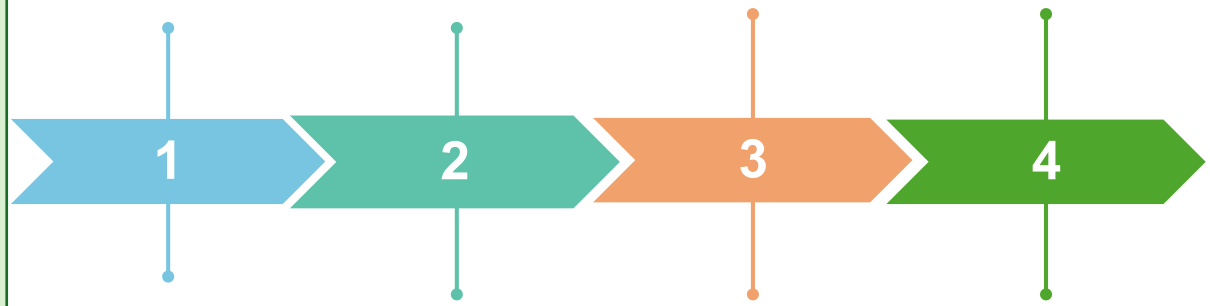

Work order

08 Rooms Constructed and 08 Suite Converted into 04

Construction of Chalets

Project Completion Date

Project Start Date: **29 Jan 2026**

Completion Date as per PC-I: **30 Dec 2026**

Next 30 Days Plan:

- Renovation/ Construction of Chalets 20 Sep 2026
- External Development/ Cobal Stone 20 Sep 2026

Back

Components of the Project

Component Name	Physical Progress	Expected Completion	Status
Renovation of main building	60%	30.11.2026	On Track
Renovation / Construction of chalets	70%	15.11.2026	On Track
Construction of rooms / Restaurant	50%	30.11.2026	On Track
Construction of 04 Nos. Suit	50%	30.11.2026	On Track
External development / Parking Area (tuff tiling etc.)	70%	30.09.2026	On Track
Jetty area Viewing deck (01 No.)	40%	15.11.2026	On Track
Fountain, viewing deck	20%	15.11.2026	On Track
Gazebos (05 Nos)	5%	15.11.2026	Delayed
Landscaping and site development	0%	15.11.2026	Delayed

- On Track
- Delayed
- Critical

Improvement, Revitalization and Upgradation of TDCP Tourist Resort Dharabi Dam, District Chakwal

Improvement, Revitalization and Upgradation of TDCP Tourist Resort Dharabi Dam, District Chakwal

Main Building

Physical Progress: 60%
Completion Date: 30.11.2026

Proposed

Work in Progress

Improvement, Revitalization and Upgradation of TDCP Tourist Resort Dharabi Dam, District Chakwal

Chalets

Physical Progress: 70%
Completion Date: 15.11.2026

Work in Progress

Improvement, Revitalization and Upgradation of TDCP Tourist Resort Dharabi Dam, District Chakwal

Chalets

Physical Progress: 70%
Completion Date: 15.11.2026

Work in Progress

Improvement, Revitalization and Upgradation of TDCP Tourist Resort Dharabi Dam, District Chakwal

External Tough Tiling

Physical Progress: 70%
Completion Date: 30.09.2026

Work in Progress

Improvement, Revitalization and Upgradation of TDCP Tourist Resort Dharabi Dam, District Chakwal

Std Rooms 1st floor

Physical Progress: 50%
Completion Date: 30.11.2026

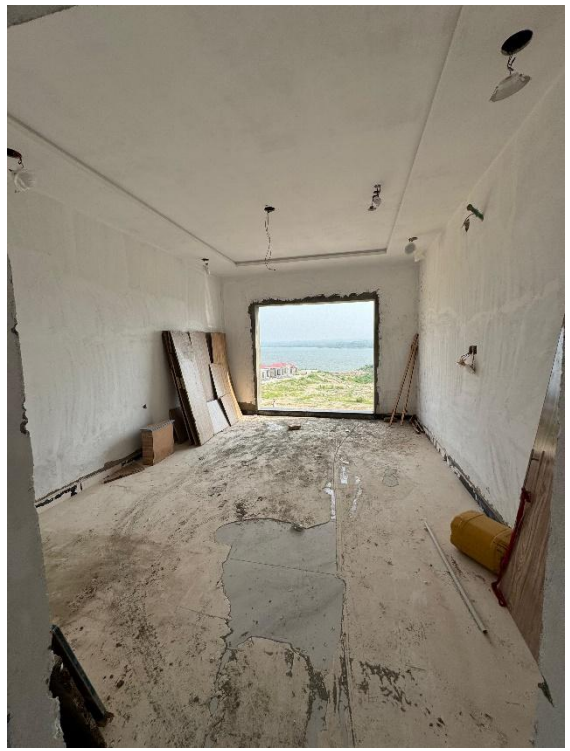

Work in Progress

Improvement, Revitalization and Upgradation of TDCP Tourist Resort Dharabi Dam, District Chakwal

4 VIP Rooms 1st floor

Physical Progress: 50%
Completion Date: 30.11.2026

Work in Progress

Improvement, Revitalization and Upgradation of TDCP Tourist Resort Dharabi Dam, District Chakwal

Restaurant

Physical Progress: 50%
Completion Date: 15.11.2026

Proposed

Work in Progress

Improvement, Revitalization and Upgradation of TDCP Tourist Resort Dharabi Dam, District Chakwal

Jetty area

Physical Progress: 40%
Completion Date: 15.11.2026

Proposed

Work in Progress

Improvement, Revitalization and Upgradation of TDCP Tourist Resort Dharabi Dam, District Chakwal

Fountain

Physical Progress: 20%

Completion Date: 15.11.2026

Work in Progress

Improvement, Revitalization and Upgradation of TDCP Tourist Resort Dharabi Dam, District Chakwal

Proposed Design/3D Render

Improvement, Revitalization and Upgradation of TDCP Tourist Resort Dharabi Dam, District Chakwal

Proposed Design/3D Render (Night View)

Remarks for Dharabi Dam Resort:

- Overall progress remains incomplete, with several key areas still under construction despite ongoing activities across the site.
- Ground-floor kitchen works are incomplete, as the washrooms remain unfinished and the roof is still damaged; only the kitchen tiling has been completed.
- Left corridor flooring in the back gallery is still pending, leaving the area in an unfinished condition despite completion of tile work in both back galleries.
- Chalet works are progressing slowly, with the first two chalets requiring finishing work and the third chalet only at the plastering and flooring stage.
- Canteen construction is still at the initial stage, indicating that significant works remain to be completed in this area.
- At the jetty a crew is operating tractors and cranes to finalize the structure.
- At the main entrance, workers are engaged in shifting stone tiles to level the access road. Inside the grounds, the fountain area is fully paved with cobblestone.
- No of workers reduced by now.

Site Focal Person	Phone Number
Naveed Anjum	+92 3335114603

Back

Improvement, Revitalization, and Upgradation of Tourist Rest House Dhanoi, Kotli Sattian , District Murree.

Responsibility: TAM / C&W / TDCP
Cost: PKR **167.870** million

Scope of work	Progress so far
1. Renovation of Rest House (01) 2. Dome POD (06) 3. Gazebo (05) 4. Bonfire (01) 5. Walkway (01) 6. Parking (01) 7. Tree Deck (03)	1. Wood work and sun room left (In progress 65% complete) 2. Dome POD (06 Nos. Installed internal separation wall , fibre sheet) 3. Gazebo (05 Nos. installed Civil Works Complete, wood polish left) 4. Bonfire (Civil Works Completed, Stone work is in progress) 5. Walkway (Main entrance, washroom ww complete, Stone work is in Progress) 6. Parking (Drainage pipe left Stone work is in Progress) 7. Tree Deck 55%

Project Start Date: **15 December 2025**
Completion Date as per PC-I: **30 December 2026**

Physical Progress	**55%**
Financial Progress	**31%**
Allocation CFY 2026-27:	**20 Mn**
Additional Funds Demand:	**130.425 Mn**

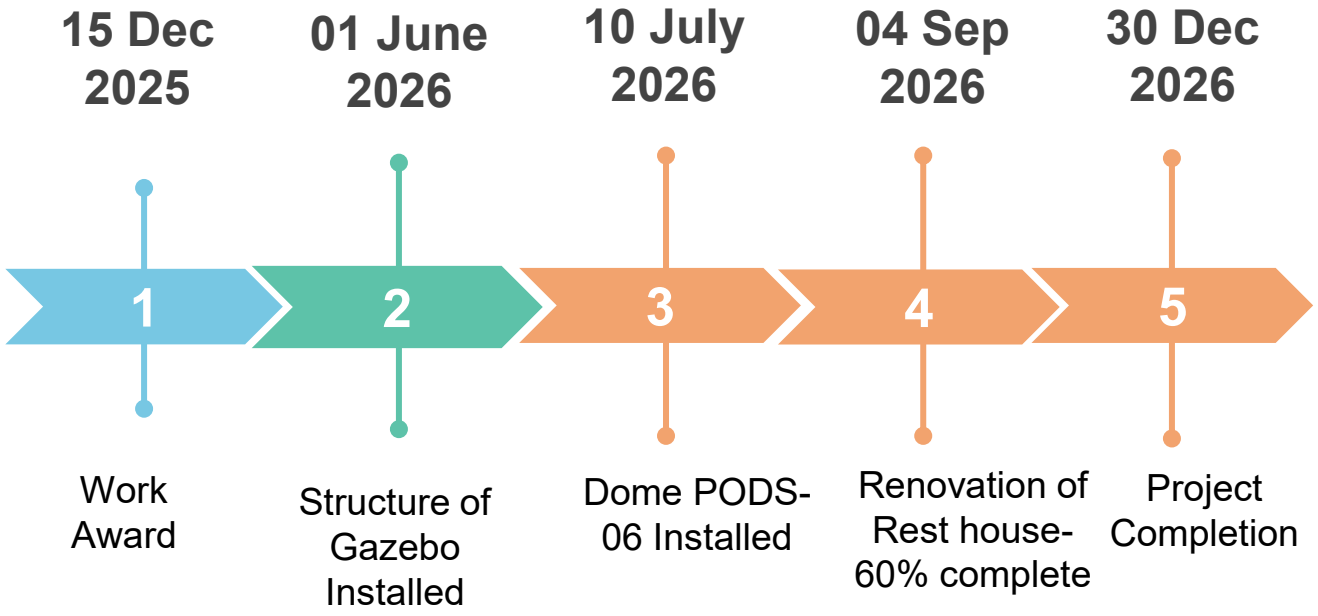

Next 30 Days Plans:
Gazebo & External Development 30 Sep 2026

Back

Components of the Project

Component Name	Physical Progress	Expected Completion	Status
Renovation of Rest House	65 %	30-10-2026	On Track
Gazebo	85%	10-09-2026	On Track
Dome Pods	45%	30-11-2026	On Track
Walkway	65%	30-10-2026	On Track
Bonfire Area	85%	30-10-2026	On Track
Parking	60%	30-10-2026	On Track

- On Track
- Delayed
- Critical

Improvement, Revitalization, and Upgradation of Tourist Rest House Dhanoi, Kotli Sattian , District Murree.

Drone Video

Improvement, Revitalization, and Upgradation of Tourist Rest House Dhanoi, Kotli Sattian , District Murree.

REST HOUSE EXTERIOR

Physical Progress: 65%
Completion Date: 30-10-2026

Proposed

Work In Progress

Improvement, Revitalization, and Upgradation of Tourist Rest House Dhanoi, Kotli Sattian , District Murree.

INTERIOR

Physical Progress: 75%
Completion Date: 30-09-2026

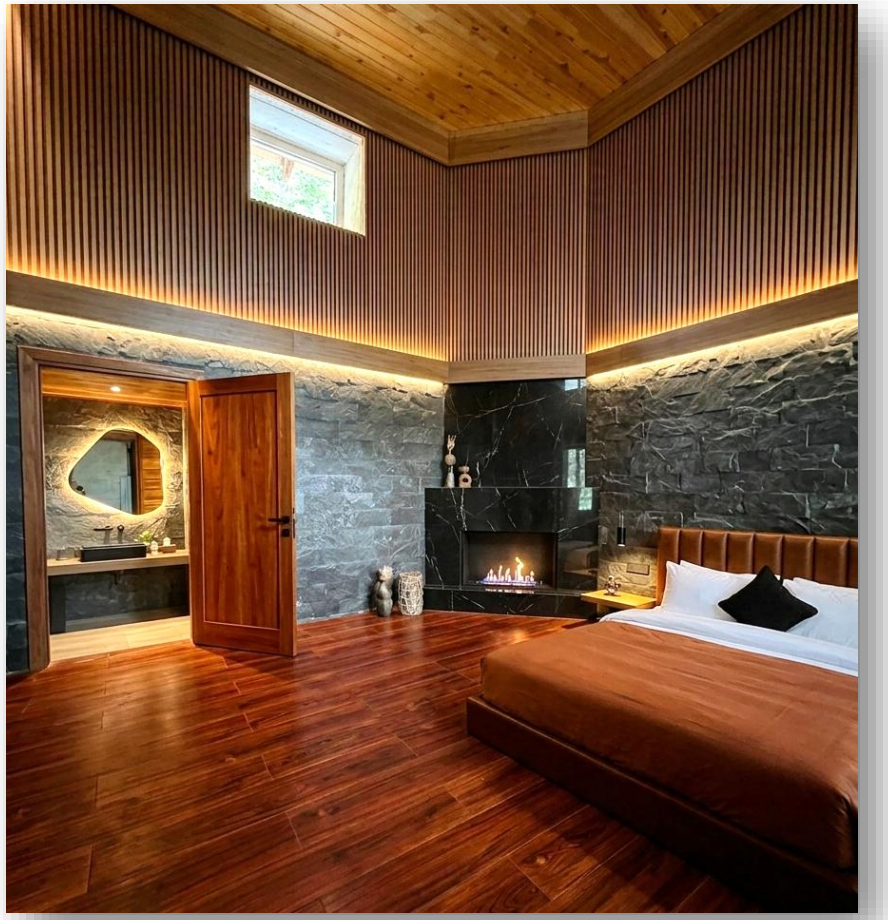

Proposed

Work In Progress

Improvement, Revitalization, and Upgradation of Tourist Rest House Dhanoi, Kotli Sattian , District Murree.

GAZEBO

Physical Progress: 85%
Completion Date: 10-09-2026

Proposed

Work In Progress

Improvement, Revitalization, and Upgradation of Tourist Rest House Dhanoi, Kotli Sattian , District Murree.

PODS

Physical Progress: 45%
Completion Date: 30-11-2026

Proposed

Work In Progress

Improvement, Revitalization, and Upgradation of Tourist Rest House Dhanoi, Kotli Sattian , District Murree.

WALKWAY

Physical Progress: 65%
Completion Date: 30-10-2026

Work In Progress

Work In Progress

Improvement, Revitalization, and Upgradation of Tourist Rest House Dhanoi, Kotli Sattian , District Murree.

BONFIRE

Physical Progress: 85%
Completion Date: 30-10-2026

Proposed

Work In Progress

Improvement, Revitalization, and Upgradation of Tourist Rest House Dhanoi, Kotli Sattian , District Murree.

Tree Deck

Physical Progress: 60%
Completion Date: 30-10-2026

Proposed

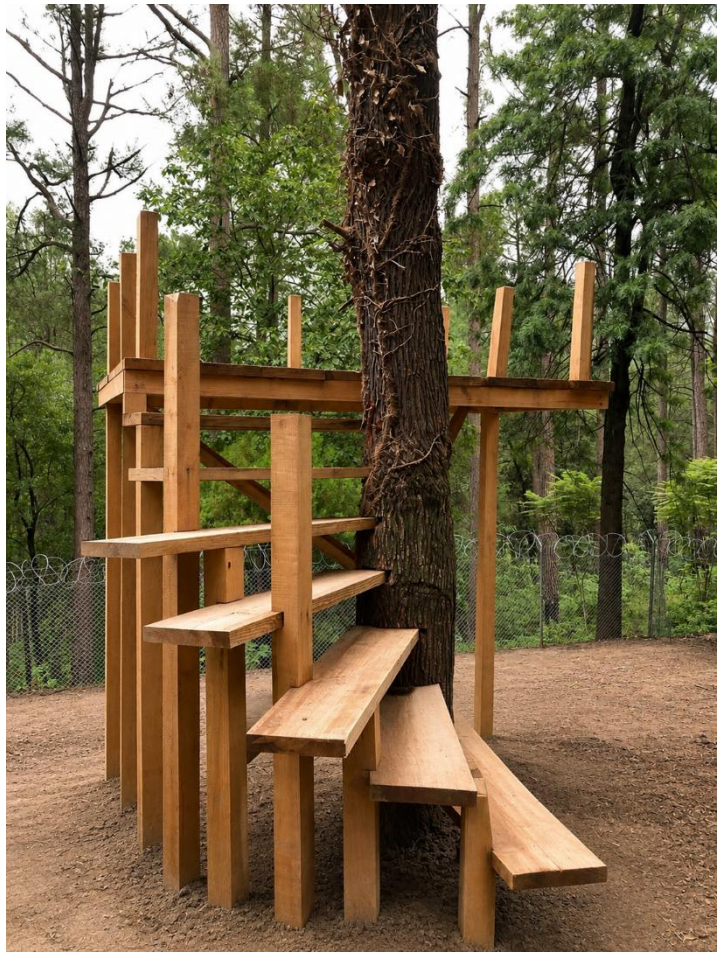

Work In Progress

Improvement, Revitalization, and Upgradation of Tourist Rest House Dhanoi, Kotli Sattian , District Murree.

Parking

Physical Progress: 60%
Completion Date: 30--2026

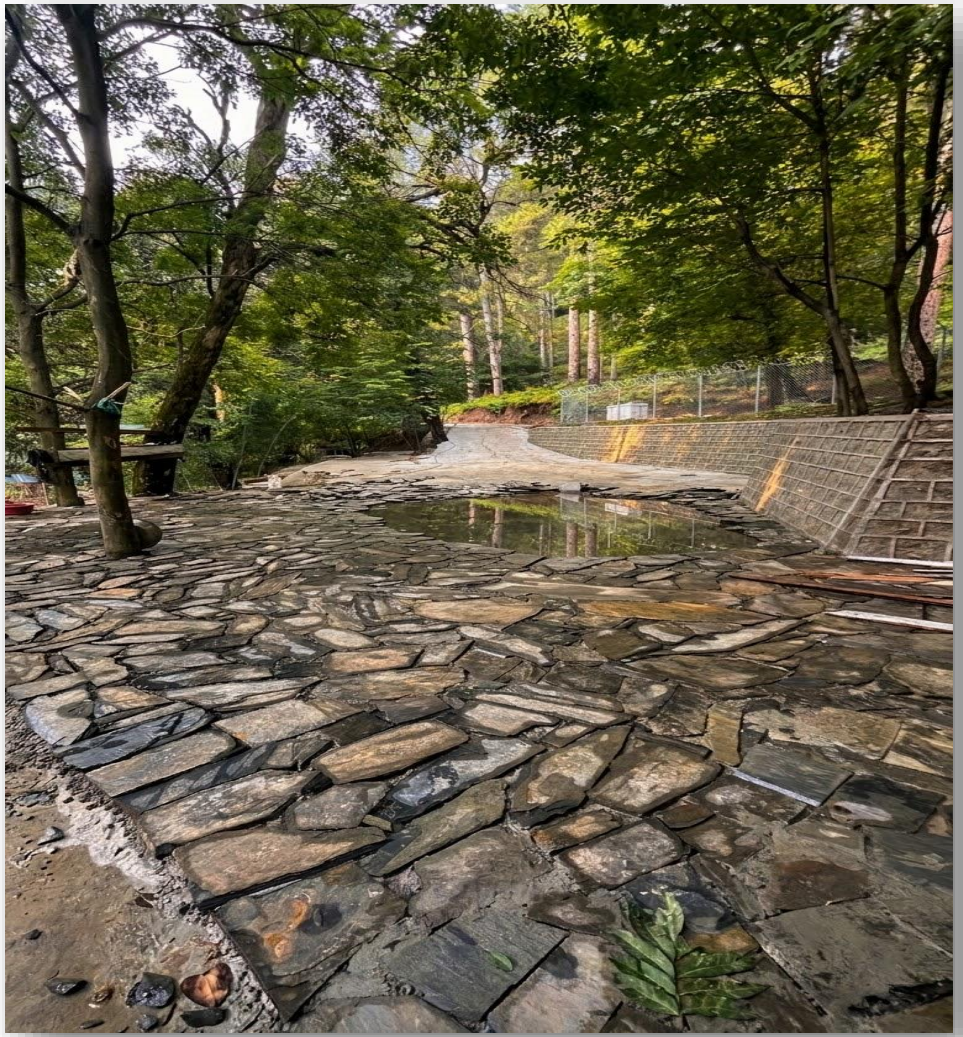

Work In Progress

Back

Project Status & Reasons for Delay

• **Weather Conditions:** Minor delays have been experienced due to ongoing rainfall, which is affecting the pace of work at the site.

• **Bore Work:** The bore installation is currently pending due to the unavailability of an electricity connection at the site. All necessary payments have already been made, and TDCP has confirmed that the electricity connection will be arranged; however, the connection has not yet been installed.

• **Temporary Power Supply:** As the permanent electricity connection is still pending, Currently ongoing works using two 15 KV generators to maintain site operations.

• **Gazebos:** The gazebo structures have been installed, and finishing works are currently in progress. Approximately **80% of the gazebo work has been completed**.

Site Focal Person	Phone Number
Qamar Hussain	03077499009

Back

Improvement, Revitalization and Upgradation of TDCP Rest House Dharabi (Irrigation), District Chakwal

Responsibility: TAM / C&W/ TDCP
Cost: PKR **258.400 Million**

Scope of work
1. Revamping of Main Building
2. Construction Gazebos (01 No.)
3. Construction of Lawn Steps
4. Development of BBQ Area.
5. Provision of the Street Lights on pathway
6. Provision of Picnic Area (Landscaping and leveling)
7. Construction of Gate and Gate pillar

Progress so far
1. Revamping of Main Building structure completed and false celling installed
2. Construction of Lawn Steps in progress
3. Construction Gazebos (01 No.) yet to be started
4. Development of BBQ Area. Yet to be started
5. Provision of the Street Lights on pathway. Yet to be started
7. Provision of Picnic Area (Landscaping and leveling) Yet to be started
8. Construction of Gate and Gate pillar. Yet to be started

Physical Progress	**34%**
Financial Progress	**24%**
Allocation CFY 2026-27:	**30 Mn**
Additional Funds Demand:	**72 Mn**

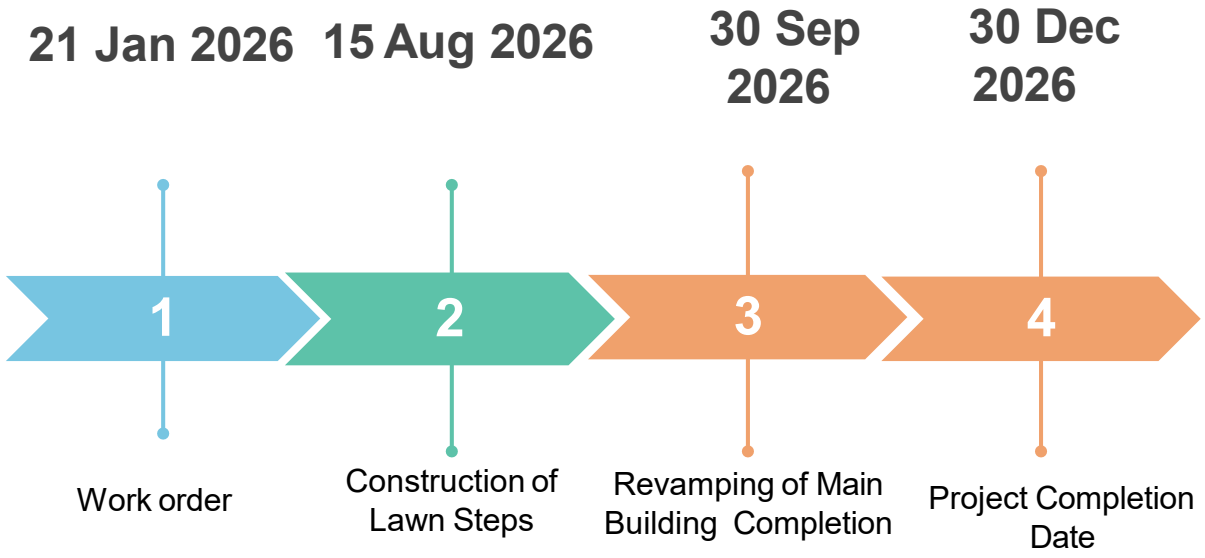

Project Start Date:	**21 Jan 2026**
Completion Date as per PC-I:	**30 Dec 2026**

Next 30 Days Plan:

- Construction is paused due to shortage of funds

Back

Components of the Project

Component Name	Physical Progress	Expected Completion	Status
Revamping of Main Building	70%	30.09.2026	On Track
Construction of Lawn Steps	50%	15.09.2026	On Track
Construction Gazebos (01 No.)	0%	30.12.2026	Delayed
Development of BBQ Area	0%	30.12.2026	Delayed
Development of Public Health System	0%	30.12.2026	Delayed
Provision of the Street Lights on pathway	0%	30.12.2026	Delayed
Provision of Picnic Area (Landscaping and leveling)	0%	30.12.2026	Delayed
Construction of Gate and Gate pillar	0%	30.12.2026	Delayed

- On Track
- Delayed
- Critical

Improvement, Revitalization and Upgradation of TDCP Rest House Dharabi (Irrigation), District Chakwal

Revamping of Main Building

Physical Progress: 70%
Completion Date: 30.09.2026

Proposed

Work in Progress

Improvement, Revitalization and Upgradation of TDCP Rest House Dharabi (Irrigation), District Chakwal

Construction of Lawn Steps

Physical Progress: 50%

Before

Progress so far

Improvement, Revitalization and Upgradation of TDCP Rest House Dharabi (Irrigation), District Chakwal

Aerial View

Proposed

Work in Progress

Back

Remarks for TDCP Rest House Dharabi (Irrigation),

- Overall progress is currently slow.
- Currently flooring work is in progress.
- Construction Gazebos (01 No.) yet to be started
- Development of BBQ Area. Yet to be started
- Provision of the Street Lights on pathway. Yet to be started
- Provision of Picnic Area (Landscaping and leveling) Yet to be started
- Construction of Gate and Gate pillar. Yet to be started
- Overall progress is slow and delayed.

Site Focal Person	Phone Number
Naveed Anjum	+92 3335114603

Back

Project Name:

1- Establishment of Improvement and Up-gradation Of TDCP Patriata Chairlift / Cable Car District Murree (Component-A)

2- Establishment of Improvement and Up-gradation Of TDCP Patriata Chairlift / Cable Car District Murree (Component-B)

Presented by:

M SHAKEEB SHAHID

Establishment of Improvement and Up-gradation Of TDCP Patriata Chairlift / Cable Car District Murree (Component-A)

Responsibility: TAM / TDCP
Cost: PKR **499.545** million

Scope of work
1) Resort Renovation
2) Kiosk 21-Nos
3) Stone pitched Pathways
4) Selfie-Points -2 Nos
5) Huts Renovation 10 Nos
6) Sitting Decks 06 Nos
7) Offices renovation

Progress so far
1) Resort Renovation in progress-95% complete
2) 6-No Kiosk completed and 4-Nos structure installed, 7 no work started.
3) 75 % Stone pitched Pathways completed.
4) 01Selfie-Point frame done, lettuce work left. 01 left–
5) 10/10 Huts renovation done, approach road left
6) Sitting Decks 06 Nos Installed
7) Offices renovation (external part completed)

Physical Progress	**30%**
Financial Progress	**12%**
Allocation CFY 2026-27:	**120 Mn**
Additional Funds Demand:	**205.529 Mn**

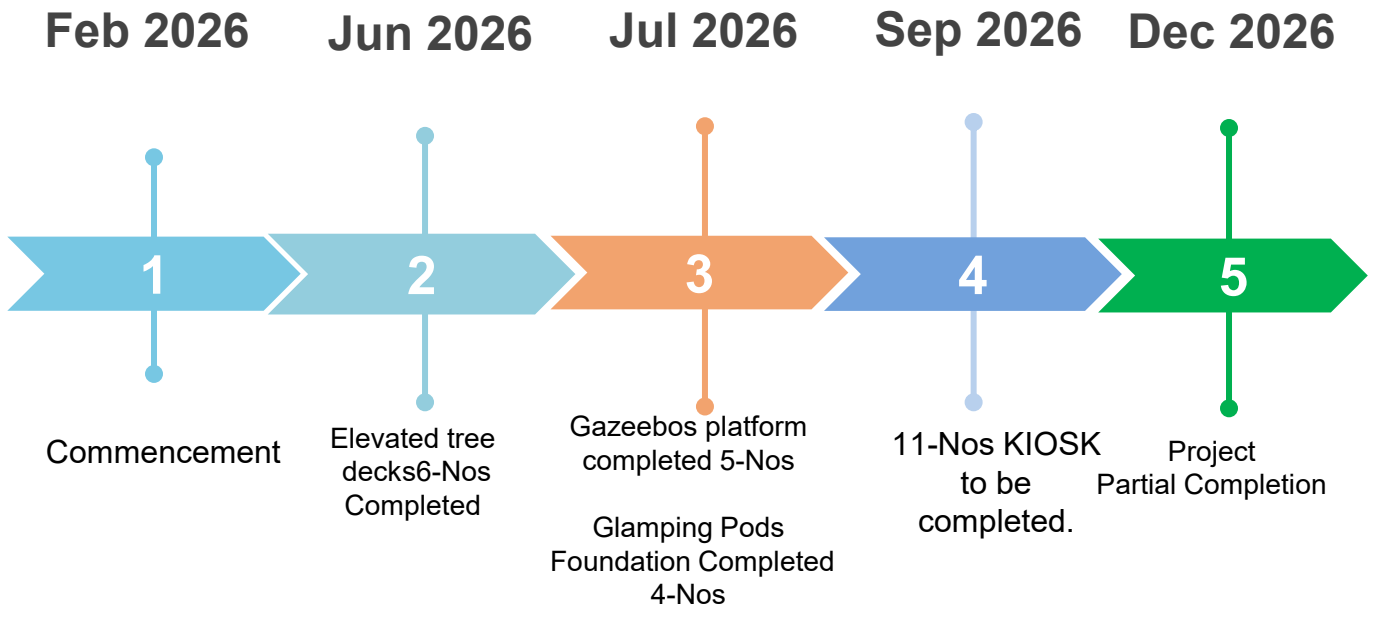

Project Start Date:	**16 Feb 2026**
Completion Time as per PC-1:	**30 Jun 2027**
Completion Time as per TAM:	**30 Dec 2026**

Next 30 Days Plans:

11-Nos KIOSK to be completed	30 Sep 2026
Gate number 2 &3 completed on	30 Sep 2026

Components of the Project

Component Name	Physical Progress	Expected Completion	Status
Whispering Hill-Resort Renovation	95%	30-09-2026	● On Track
Kiosks **6-Nos on Base** **11-Nos on Top**	35%	30-09-2026 for top point only	● On Track
Pathways Stone Pitched (Top and Base Station)	75%	30-09-2026	● On Track
Selfie Point **1-Nos at Base** **1-Nos at Top**	35%	30-09-2026 Base point in progress	● On Track
Huts Renovation **8-Nos Huts on Base** **2-Nos chalet on Base**	100%	Completed	● On Track
Entrance & Informatory Sign boards	100% at base	Completed	● On Track
Elevated tree decks **2-Nos on Base** **4-Nos on Top**	100%	Completed	● On Track

● On Track
● Delayed
● Critical

TDCP Resort PATRIATA (Component-A)

TDCP Resort **PATRIATA (Component-A)**

RESORT

Physical Progress: 95%
Completion Date: 30-09-2026

Completed

TDCP Resort **PATRIATA (Component-A)**

RESORT INTERIOR
ROOM 1

Physical Progress: 100%
Completion Date: Completed

Completed

TDCP Resort **PATRIATA (Component-A)**

RESORT INTERIOR
ROOM 2

Physical Progress: 100%
Completion Date: Completed

Completed

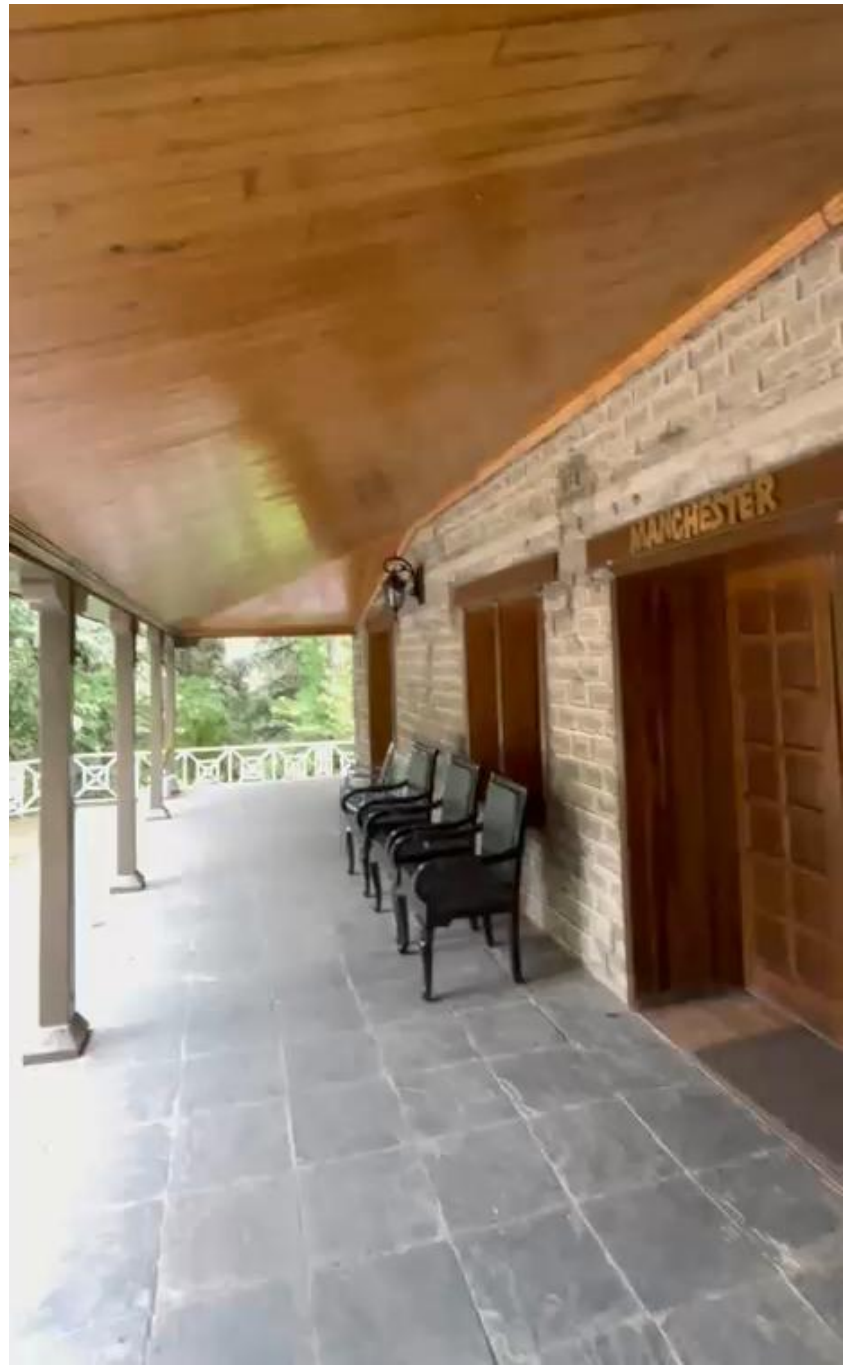
MANCHESTER

TDCP Resort **PATRIATA (Component-A)**

KIOSK PATRIATA BASE

Physical Progress: 70%
Completion Date: 30-09-2026

Proposed

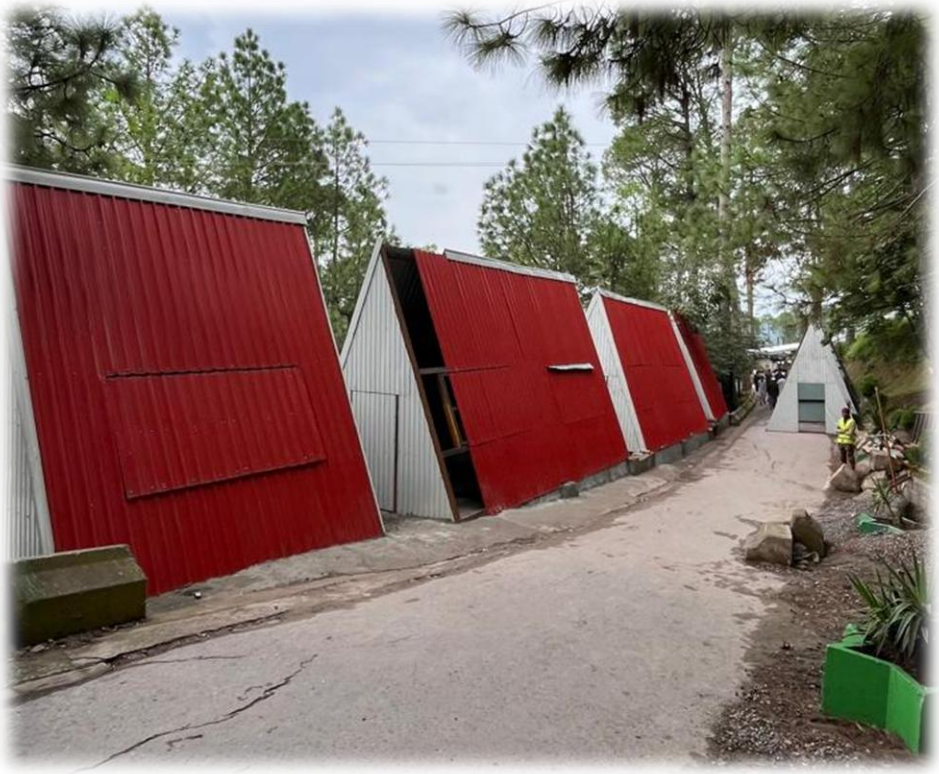

Work in Progress

TDCP Resort **PATRIATA (Component-A)**

KIOSK PATRIATA TOP

Physical Progress: 20%
Completion Date: 30-09-2026

Proposed

In Progress

TDCP Resort **PATRIATA (Component-A)**

Pathways Stone Pitched at Base

Physical Progress: 75%
Completion Date: 30.09.2026

Work in Progress

TDCP Resort **PATRIATA (Component-A)**

SELFIE POINT

Physical Progress: 80%
Completion Date:30-09-2026

Proposed

Work in Progress

TDCP Resort **PATRIATA (Component-A)**

CHALET RENOVATION

Physical Progress: 100%
Completion Date: completed

Completed

TDCP Resort **PATRIATA (Component-A)**

1-CHALET RENOVATION

Physical Progress: 100%
Completion Date: completed

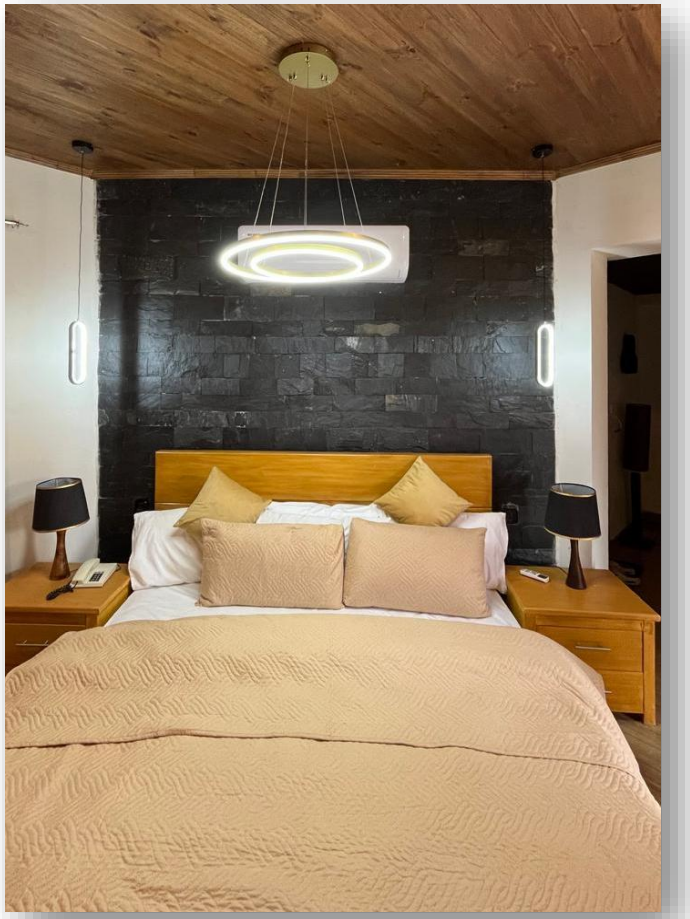

Completed

TDCP Resort **PATRIATA (Component-A)**

2-CHALET RENOVATION

Physical Progress: 100%
Completion Date: completed

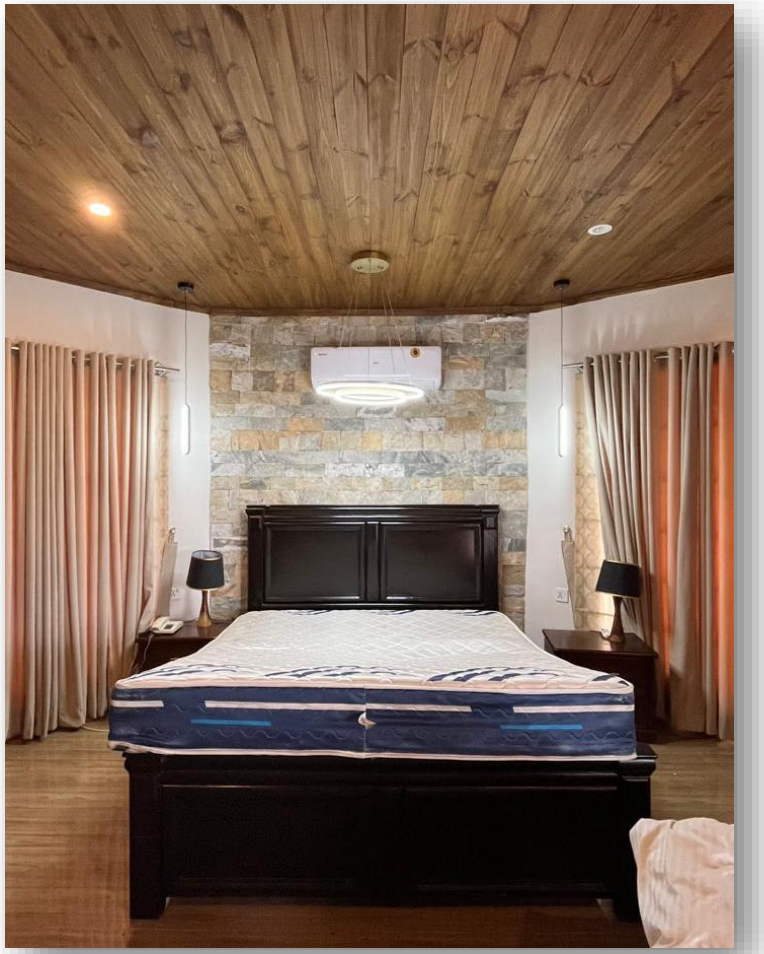

Completed

TDCP Resort **PATRIATA (Component-A)**

HUTS RENOVATION

Physical Progress: 100%
Completion Date: completed

Completed

TDCP Resort **PATRIATA (Component-A)**

HUTS RENOVATION

Physical Progress: 100%
Completion Date: completed

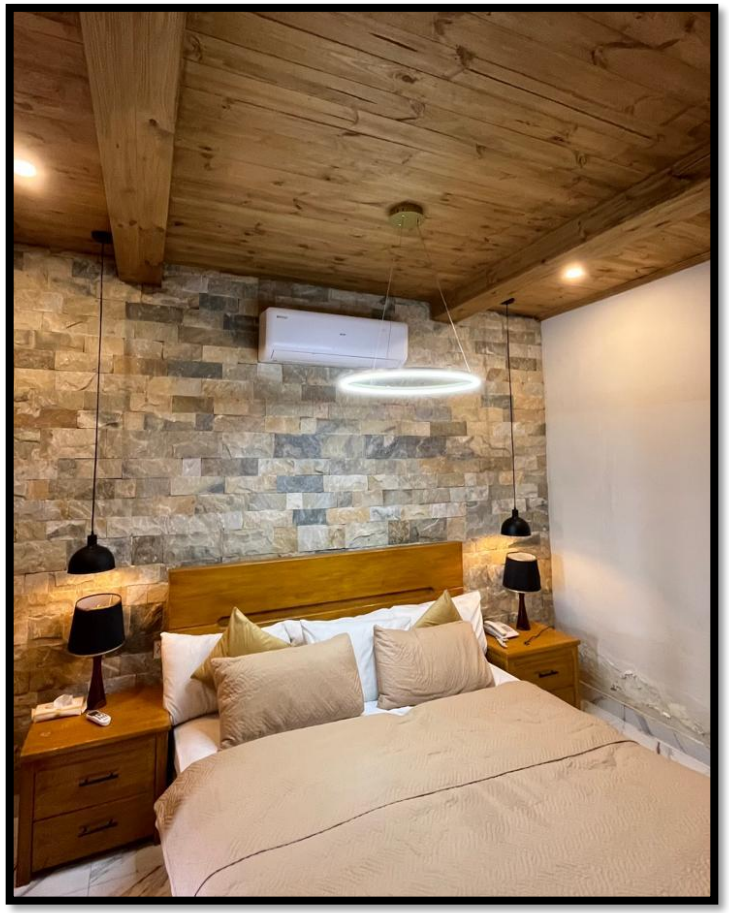

Completed

TDCP Resort **PATRIATA (Component-A)**

INFORMATORY SIGN BOARDS

Physical Progress: 100%

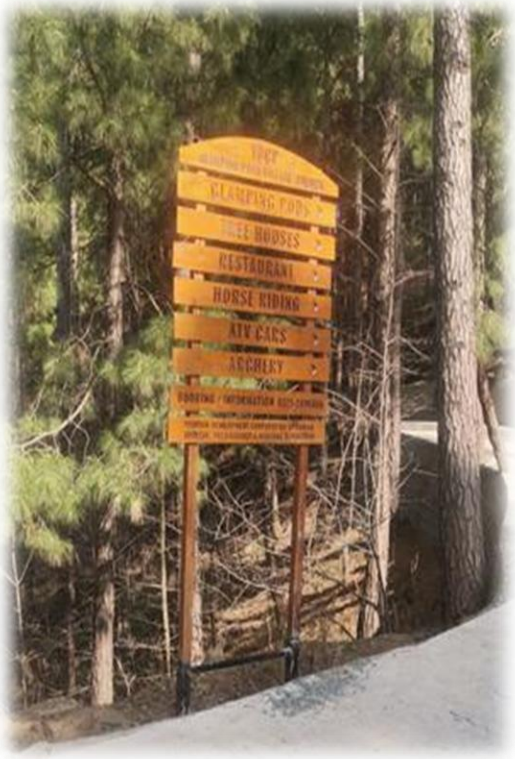

Completed

TDCP Resort **PATRIATA (Component-A)**

ELEVATED TREE DECKS

Physical Progress: 100%

Completed

Remarks:

- **Kiosks:** Physical progress of kiosk at base and on top is delayed
- **Gates:** Work is in progress on 2-Nos Gates only at base,work is pending on 2 Gates at base , meanwhile no any physical work is placed on gates present on Patriata Top.
- **Souvenior Shops:** out of 6, just 4 are in progress which include the framework
- **Waiting area:** 1 is nearly to complete on top,1 at base and 1 at top is under construction, meanwhile no work is started on remaining waiting areas (1 at base & 1 at top).
- **Car Parking:** Shuttering work and cvil work is Delayed due to weather Conditions, no work is started on the gates of Parking area.
- **Selfie-Point :** work is in progress at base and no work is started at Top.
- **Stone Pitched Pathway:** Stone Pathways have been laid on Base and Top.

Preservation, Restoration, Improvement, Management and Upgradation of Sher Singh Baradari, Lahore

ZARQA ASHRAF

6.Preservation, Restoration, Improvement, Management and Upgradation of Sher Singh Baradari, Lahore

Responsibility: TAM / ARCHAEOLOGY
Cost: PKR **271.234** million

Physical Progress	68%
Financial Progress	12%
Allocation (2026-27)	60 Million
Additional Funds Demand	80 Million

Scope of Work
1.Structural Stabilization
2.Dismantling of Washrooms
3.Illumination
4.Provision of Furniture
5.Laying of Floor
6.Treatment of Wooden Ceiling and Doors
7.Conservation
8.Ornamental Stucco Work
9.Ornamental Fresco Work
10.De-layering of Architectural Features
11.Conservation of Samadhi

Progress So far
1. Structural Stabilization (Completed)
2. Dismantling of Washrooms (Completed)
3. Illumination (Wiring & AC installation in progress)
4. Provision of Furniture (Yet to be purchased)
5. Laying of Floor (Almost completed)
6. Treatment of Wooden Ceiling and Doors (Completed)
7. Conservation (Completed)
8. Ornamental Stucco Work (Completed)
9. Ornamental Fresco Work (In progress)
10. De-layering of Architectural Features (In progress)
11. Conservation of Samadhi (Pucca Kali work in progress)
12. Boundary Wall (Work in progress)
13. Landscaping (Work in progress)

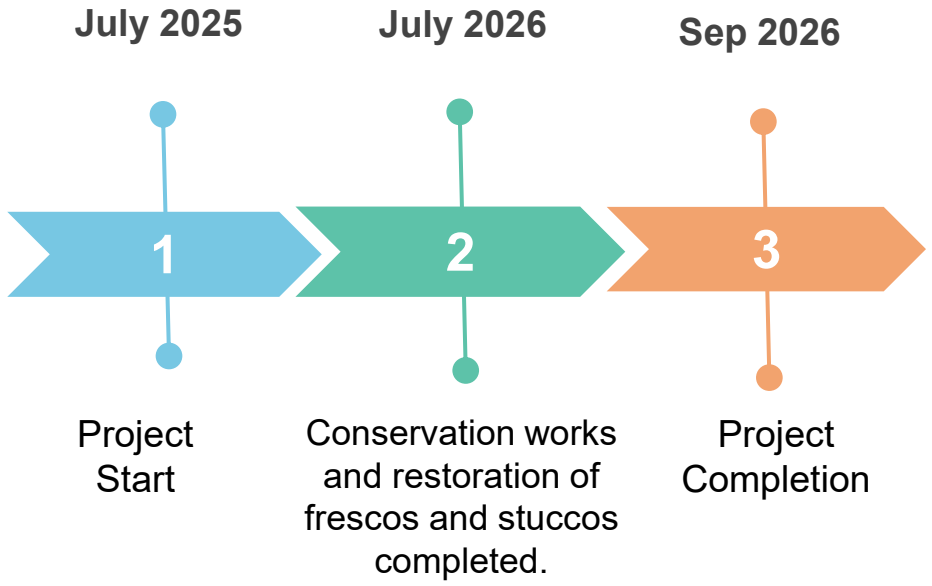

Next 30 Days Plans:

- Completion of Illumination works.
- Completion of furniture provision.
- Continuation of final remaining floor-laying area, as well as remaining treatments of doors and wooden ceilings.

5 Sep 2026

Components of the Project

Component Name	Physical Progress	Expected Completion	Status
Structural Stabilization	100%	completed	completed
Dismantling of Washrooms	100%	Completed	Completed
Laying of Floor	95%	20-09-2026	🟢 On Track
Treatment of Wooden Ceiling & Doors	95%	20-09-2026	🟢 On Track
Conservation	80%	05-11-2026	🟢 On Track
Ornamental Stucco Work	70%	15-09-2026	🟢 On Track
Ornamental Fresco Work	70%	15-09-2026	🟢 On Track
Illumination	60%	30-07-2026	🟢 On Track
Provision of Furniture	Pending	30-07-2026	🟡 Delayed
Conservation of Samadh	70%	15-09-2026	🟢 On Track

🟢 = **On Track**
🟡 = **Delayed**
🔴 = **Critical**

SHERSINGH BARADARI (West Elevation)

Evidence-based restoration of missing Fresco

Physical Progress: 70%
Completion date: 30-07-2026

Before

Current

SHERSINGH BARADARI (West Elevation)

Conservation of Columns

Physical Progress: 70%
Completion date: 30-07-2026

During

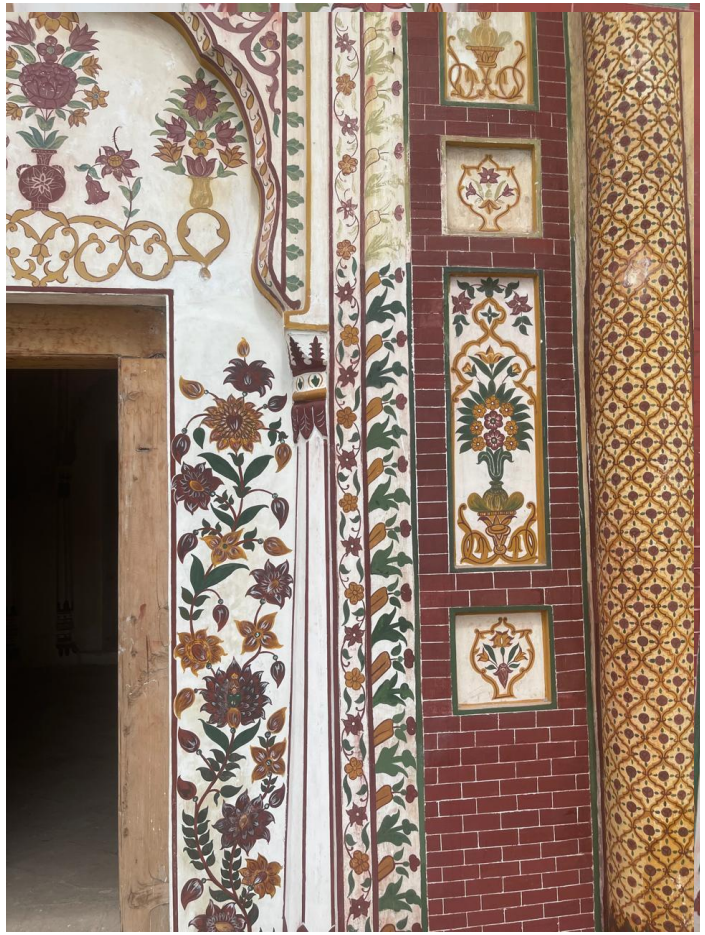

Current

SHERSINGH BARADARI (West Elevation)

Conservation of Interior Baradari

Physical Progress: 75%
Completion date: 30-08-2026

Before

current

SHERSINGH BARADARI (R5 West Elevation)

Conservation of Interior Baradari

Physical Progress: 70%
Completion date: 30-08-2026

Before

current

SHERSINGH BARADARI (R7 West Elevation)

STABILIZATION AND REINTEGRATION OF EXISTING FRESCO AND RESTORATION ON THE BASIS OF ON-SITE EVIDENCE

Physical Progress: 65 %
Completion date: 30-08-2026

Before

Work in Progress

SHERSINGH BARADARI (Surrounding Context)

STABILIZATION AND REINTEGRATION OF EXISTING FRESCO AND RESTORATION ON THE BASIS OF ON-SITE EVIDENCE

Physical Progress: 85%
Completion date: 30-07-2026

Before

Work in Progress

SHERSINGH BARADARI (Surrounding Context)

Improvement of Boundary Wall and Landscape

Physical Progress: 60%
Completion date: 31-08-2026

Before

Work in Progress

LAYING OF FLOOR

Mechanical grinding of the existing floor is in progress.

Physical progress: 95%
Completion Date:20-09-2026

CONSERVATION OF SAMADHI

Physical progress:70%
Completion Date:15-09-2026

APPROACH & ENTRANCE TO SHER SINGH BARADARI

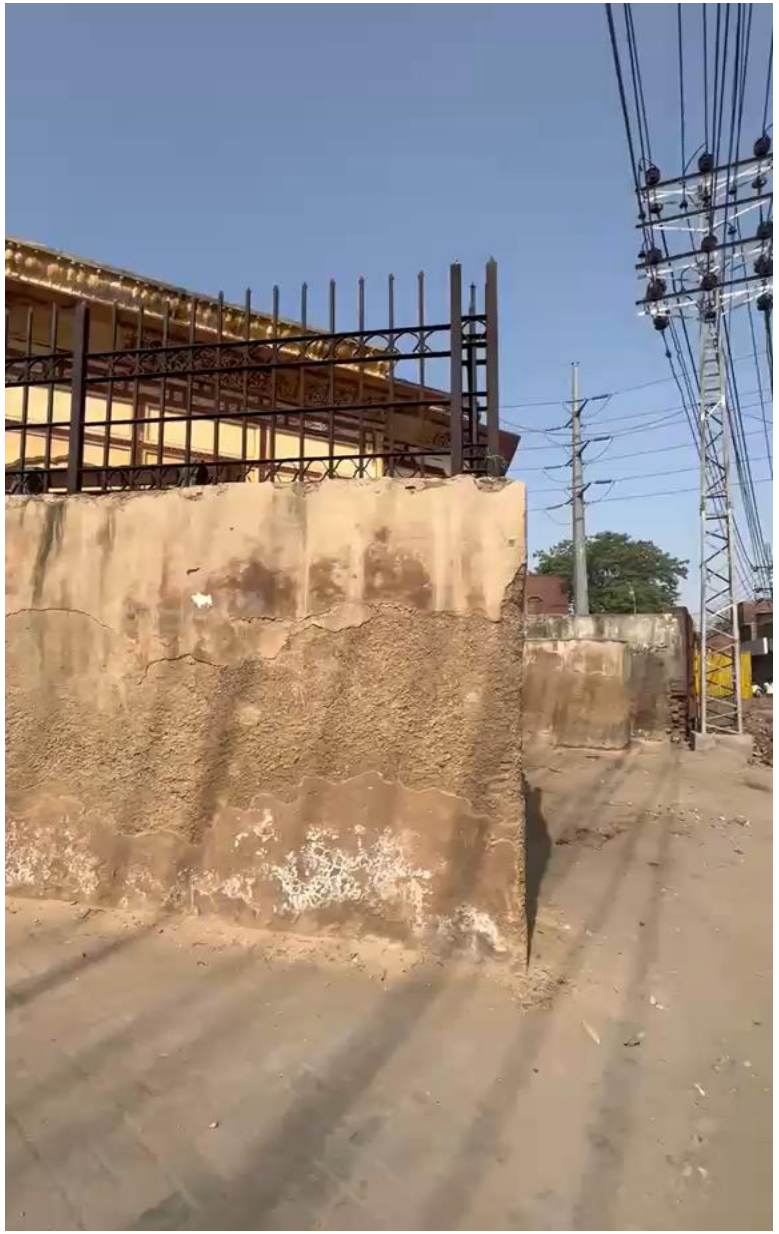

EXTERNAL BOUNDARY & REAR ENTRANCE

WORK IN PROGRESS

PROGRESS REPORT

Physical Progress: Major conservation and stabilization works have been completed, while remaining works are progressing satisfactorily.

Conservation Works: Structural stabilization, conservation, wooden ceiling & doors treatment, and ornamental stucco work have been completed; fresco work is in progress.

Flooring: Floor grinding work is in progress.

Illumination: Wiring and AC installation works are in progress.

Samadh Conservation: Pucca Kali work is in progress.

External Works: Boundary wall and landscaping works are in progress.

Power Supply: Power supply has remained disconnected for the past week and requires prompt restoration.

Fountain & Washroom Pathway: Repair and pathway works are expected to commence/complete within one week.

Furniture: Furniture is yet to be purchased.

Other Works: Café and parking facilities will be taken up at a later stage.

Extension Request: Contractor has requested an extension up to December 2026; the request has been forwarded by the Director to the DG, and the revised completion date will be confirmed upon receipt of the decision.

Site Focal Person	Phone Number
Mukhtar Ahmed	03004293573

Preservation, Restoration, Improvement, Management and Upgradation of Kamran Ki Baradari, Lahore

Responsibility: TAM / ARCHAEOLOGY
Cost: PKR **127. 57** million

Physical Progress	90%
Financial Progress	50 %
Allocation (2026-27)	20 Million
Additional Funds Demand	43.57 Million

Scope of Work	Progress so far
1. Structural Stabilization	**1. 100%**
2. Dismantling of Terrazzo Concrete	**2. 100%**
3. Conservation	**3. 100%**
4. Fountain Work	**4. 100%**
5. Plumbing & Wiring	**5. 100%**
6. Fresco Ornamentation	**6. 100%**
7. Doors Installation	**7. 100%**
8. Chandeliers	**8. 100%**
9. Furniture & Rugs	**9. Pending**
10. Decorative Items	10. 100%
11. Washrooms	11. 100%
12. External Illumination	12. 100%
13. Gazebos	13. 98%
14. Public Toilets	14. 100%
15. Air conditioners & Generators	15. 100%

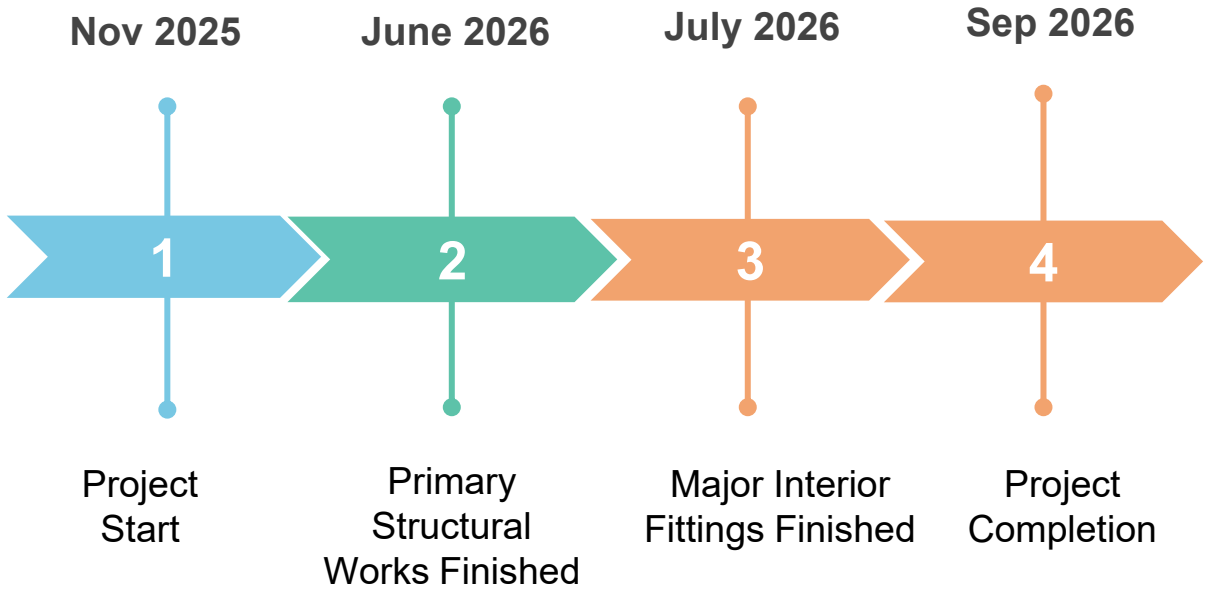

Project Start Date:	**25 Nov 2025**
Completion Date by PC1:	**30 Jun 2027**
Completion Date by TAM:	**15 Sep 2026**

Next 30 Days Plans:

- Completion of gazebo.
- Installation of transformer and electricity meter

Components of the Project

Component Name	Progress	Expected Completion	Status
Structural Stabilization	100 %	Completed	On Track
Dismantling of Terrazzo Concrete	100%	Completed	On Track
Conservation	100%	Completed	On Track
Fountain Works	100%	Completed	On Track
Plumbing & Wiring	100%	Completed	On Track
Generator	100%	Completed	On Track
Washrooms	100%	Completed	On Track
Fresco Ornamentation	100 %	Completed	On Track
Doors	100%	Completed	On Track
External Illumination & Pathways	100%	Completed	On Track
Public Toilets	100%	Completed	On Track
Chandeliers	100%	Completed	On Track
Furniture & Rugs	Pending	15-09-2026	On Track
Decorative Items	100 %	Completed	On Track
Air Conditioners	100%	Completed	On Track
Gazebos	98%	15-09-2026	On Track
Transformer & Electricity Meter	---	15-09-2026	Delayed

● = On Track
● = Delayed
● = Critical

Drone Video

Kamran Ki Baradari

Conservation of Fresco and Fountain Works

Physical Progress: 100%
Completion Date: 15-09-2026

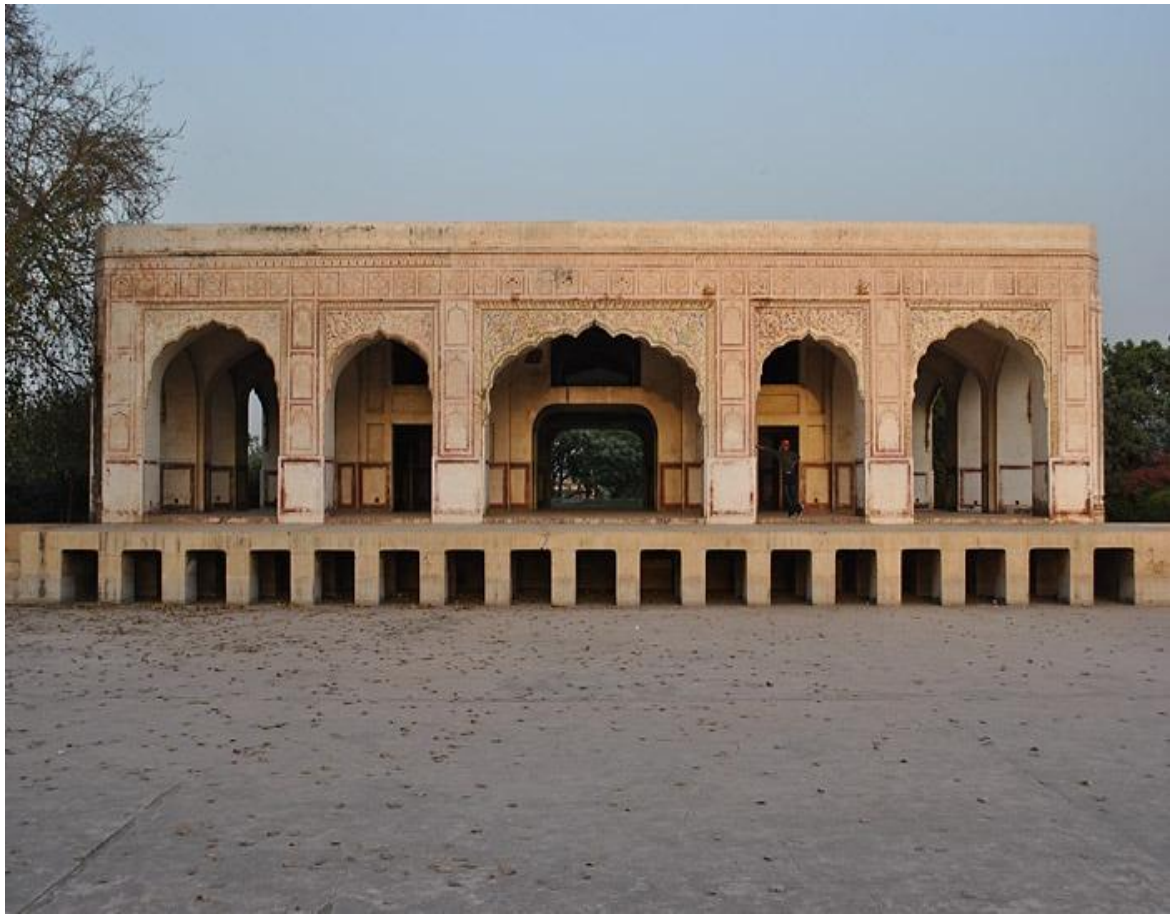

Before

After

Kamran Ki Baradari

Conservation of Interior Fresco

Physical Progress: 100%
Completion Date: 15-09-2026

Before

After

Kamran Ki Baradari

Dismantling & Repaving of Special-sized Bricks

Physical Progress: 100%
Completion Date: 15-09-2026

Before

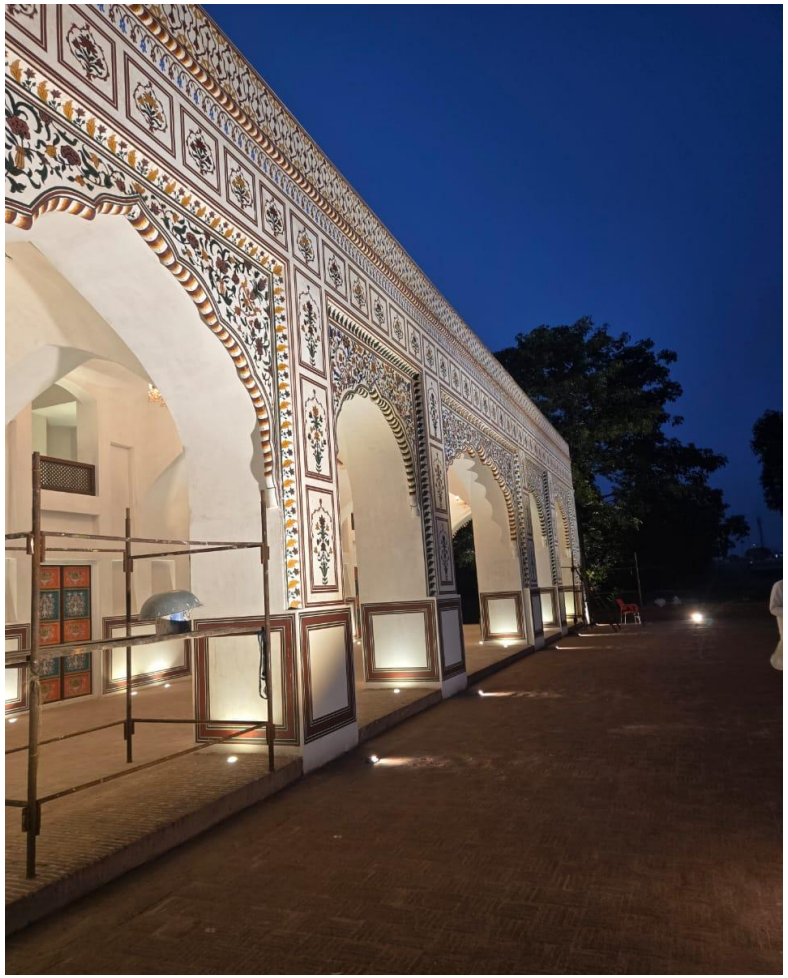

After

Kamran Ki Baradari

Provision of Wooden Doors

Physical Progress: 100%
Completion Date: 15-09-2026

Before

After

Kamran Ki Baradari

Conservation of Interior Fresco

Physical Progress: 100%
Completion Date: 15-09-2026

Before

After

Kamran Ki Baradari

Provision of Gazebos

Physical Progress: 98%
Completion Date: 15-09-2026

Proposed

Work in progress

Kamran Ki Baradari

Illumination of Baradari

Physical Progress: 100%
Completion Date: 15-09-2026

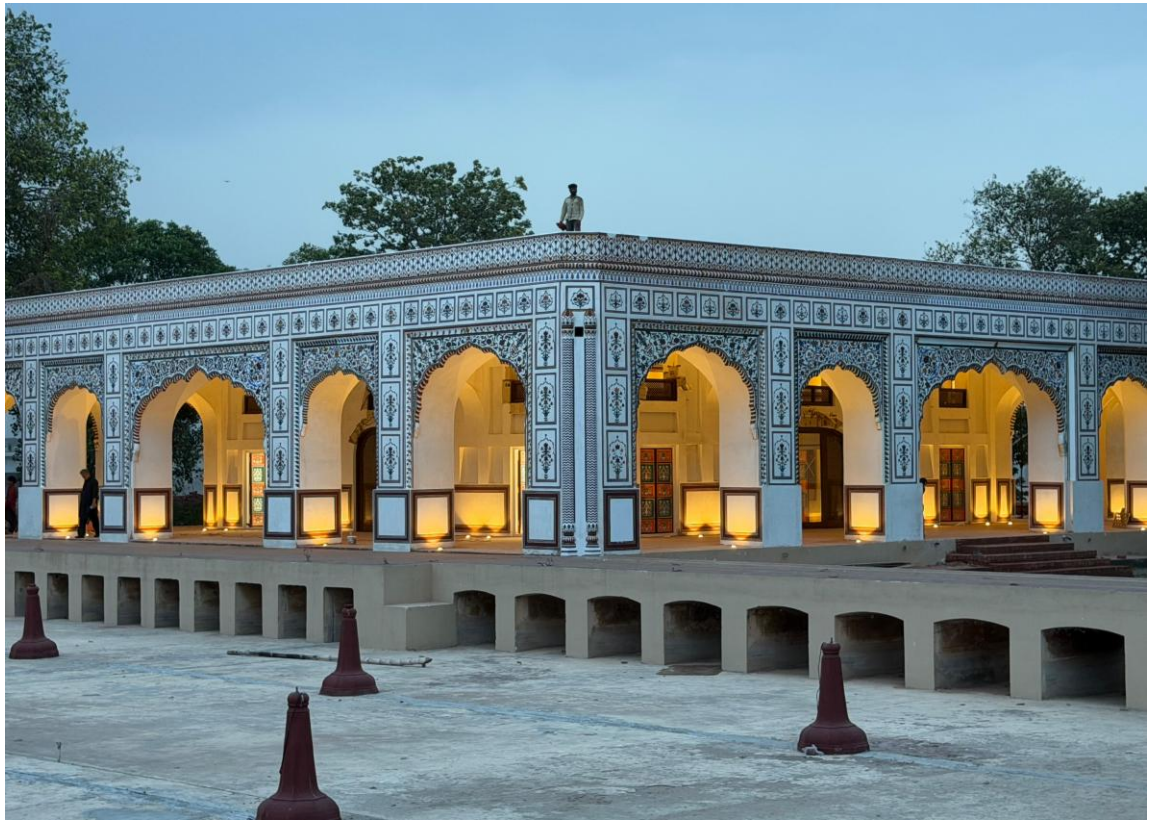

Kamran Ki Baradari

Illumination of Baradari

Physical Progress: 100%
Completion Date: 15-09-2026

Kamran Ki Baradari

Illumination of Baradari

Physical Progress: 100%
Completion Date: 15-09-2026

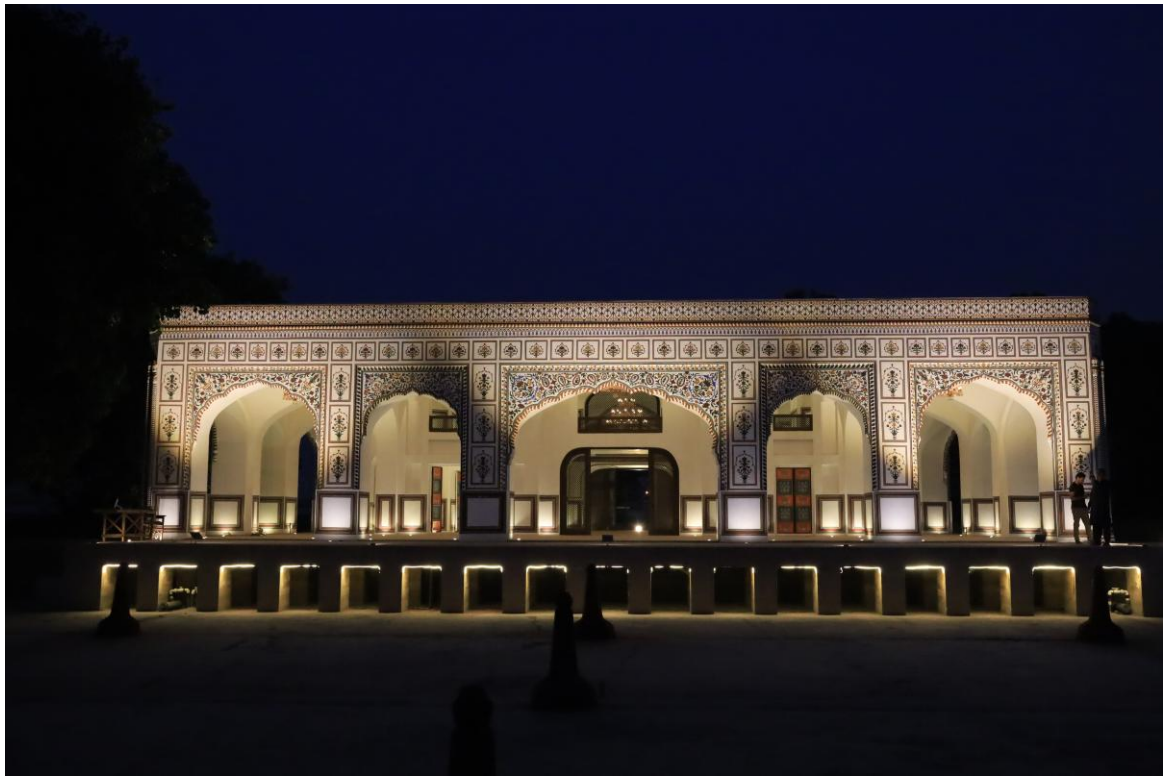

Kamran Ki Baradari

Illumination of Baradari

Physical Progress: 100%
Completion Date: 15-09-2026

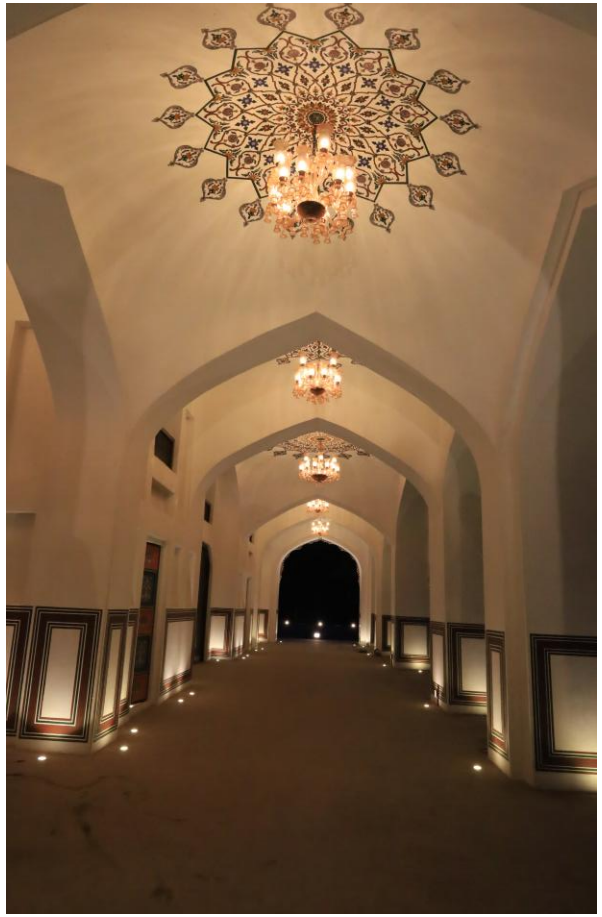

Kamran Ki Baradari

Illumination of Baradari

Physical Progress: 100%
Completion Date: 15-09-2026

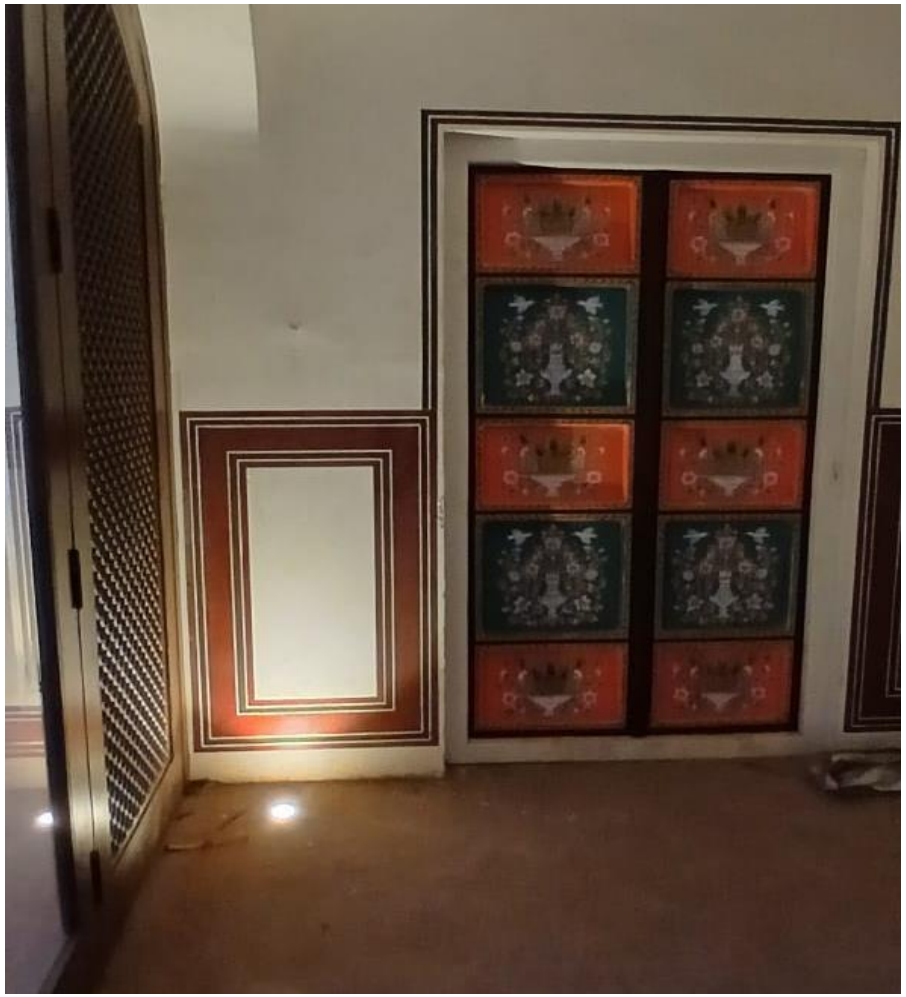

Kamran Ki Baradari

Illumination of Baradari

Physical Progress: 100%
Completion Date: 15-09-2026

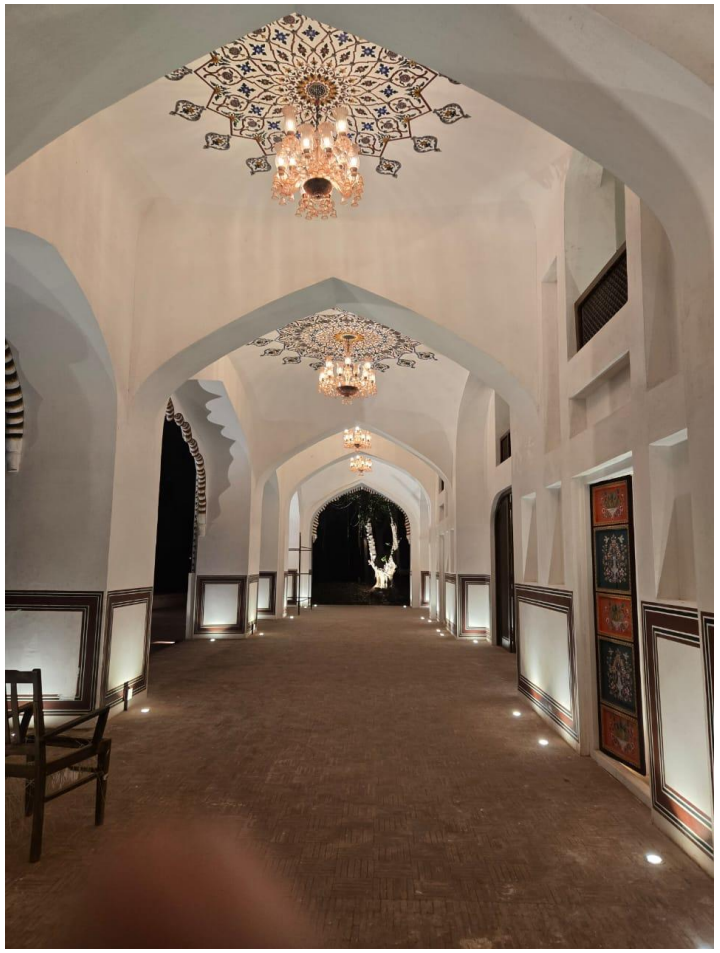

Kamran Ki Baradari

Illumination of Baradari

Physical Progress: 100%
Completion Date:15-09-2026

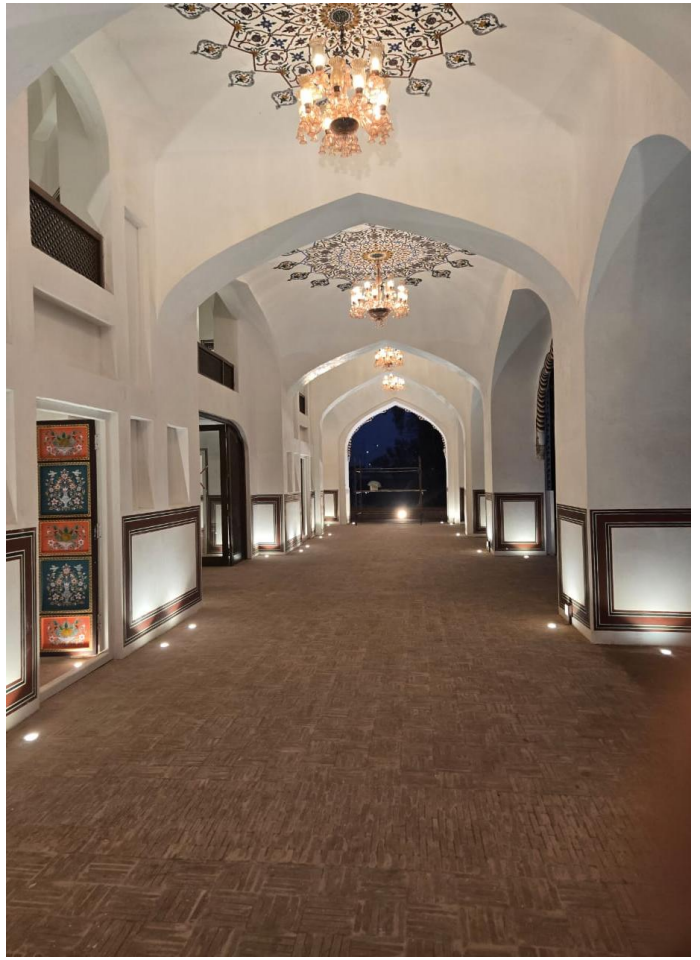

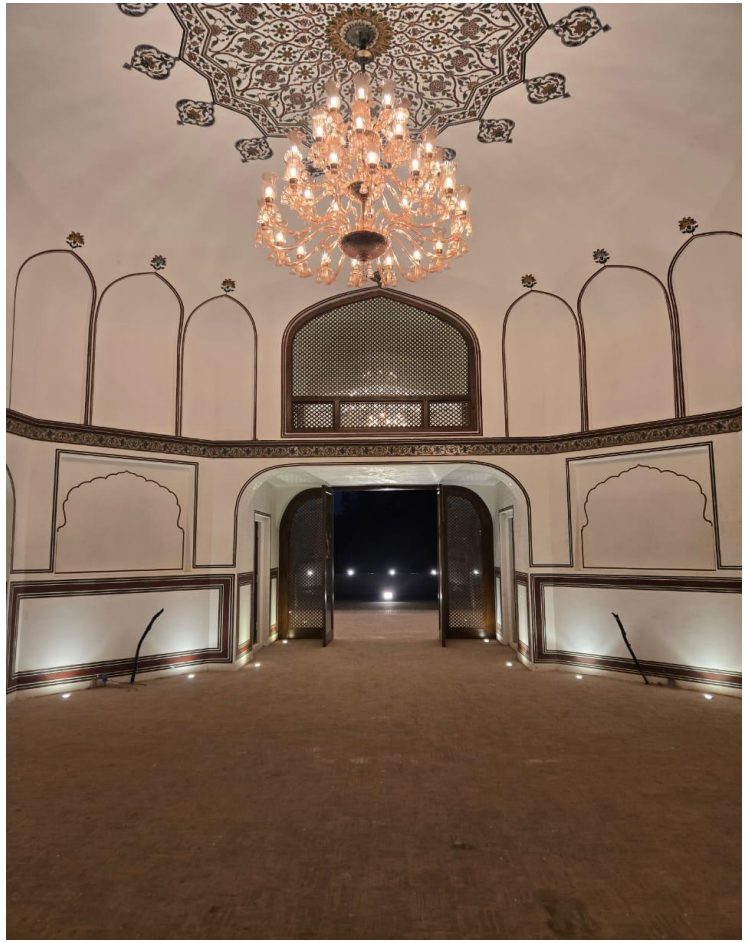

Back

Restoration & Conservation of Saint Andrew's Presbyterian Church, Lahore

Approved Cost: PKR 95.280
Responsibility: TAM / ARCHAEOLOGY

Scope of work
1. Structural Stabilization 2. Sewerage and Storm Water Drainage System 3. Removal of marble on pillars and walls 4. De-layering of architectural features 5. Conservation of church and removal of paint 6. Restoration of washroom 7. Boundary wall 8. Landscape Illumination

Progress so far
1. Structural Stabilization — 100% 2. Sewerage & Storm Water Drainage — 100% 3. Removal of Marble on Pillars and Walls — 100% 4. De-layering of Architectural Features — 100% 5. Conservation & Paint Removal — 90% 6. Restoration of Washroom — 90% 7. Boundary Wall — 80% 8. Landscape Illumination — 50%

Project Start Date: **01 Jul 2025**
Completion Date by PC1: **30 Jun 2027**
Completion Date by TAM: **30 Oct 2026**

Physical Progress: **75 %**
Financial Progress: **30 %**
Allocation (2026-27) **35 Million**
Additional Funds Demand **32.28 Million**

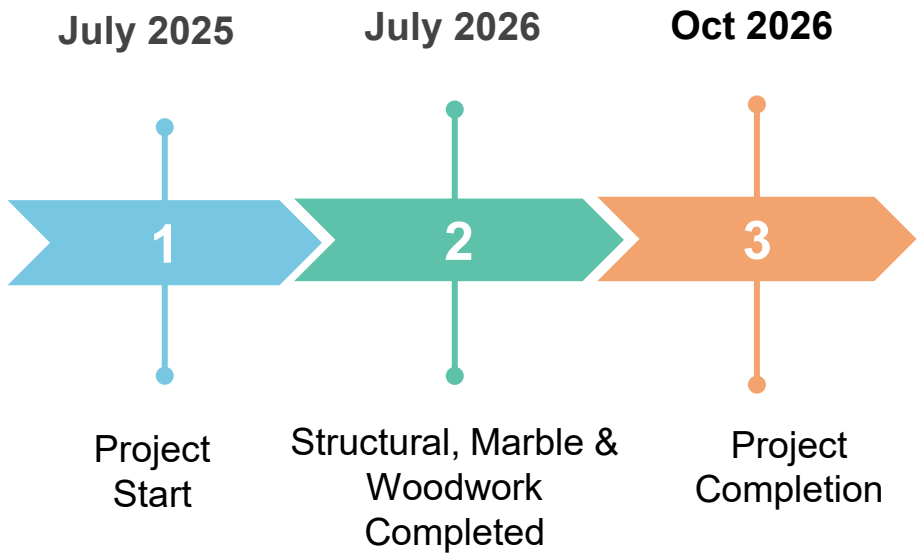

Next 30 Days Plans:

- Completion of conservation of the church, including paint removal.
- Completion of restoration of the washroom.
- Completion of arches inside niches of boundary wall.
- Completion of landscape illumination

Components of the Project

Component	Progress	Completion	Status
Structural Stabilization	100%	Completed	On Track
Sewerage & Storm Water Drainage	100%	Completed	On Track
Removal of Marble on Pillars and Walls	100%	Completed	On Track
De-layering of Architectural Features	100%	Completed	On Track
Conservation & Paint Removal	90%	30-09-2026	On Track
Restoration of Washroom	90%	30-09-2026	On Track
Boundary Wall	80%	30-09-2026	On Track
Landscape Illumination	50%	30-10-2026	On Track

= On Track
= Delayed
= Critical

CM PUNJAB
MARYAM
NAWAZ
MAGNIFICENT
PUNJAB
Back

Saint Andrew's Presbyterian Church

Stain Glass Rose Window & Exterior Wall Restoration

Physical Progress: 80 %
Completion Date: 30-09-2026

Before

Work in Progress

Saint Andrew’s Presbyterian Church

Interior Marble Removal & Lime Plaster Restoration

Physical Progress: 75%
Completion Date: 30-09-2026

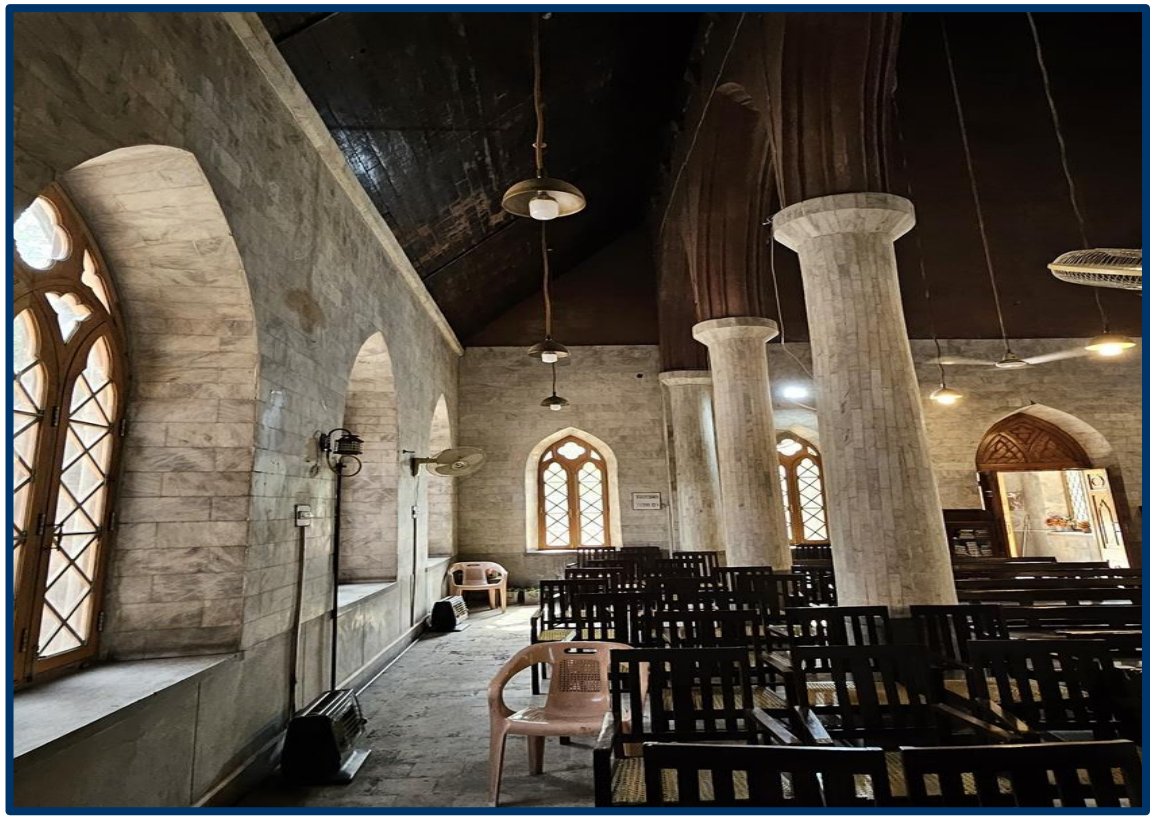

Before

Work in Progress

Saint Andrew’s Presbyterian Church

Marble Removal, Lime Plaster Restoration & Wood Work

Physical Progress: 95%
Completion Date: 30-09-2026

Before

Work in Progress

Saint Andrew’s Presbyterian Church

Marble Flooring Restoration

Physical Progress: 95%
Completion Date: 30-09-2026

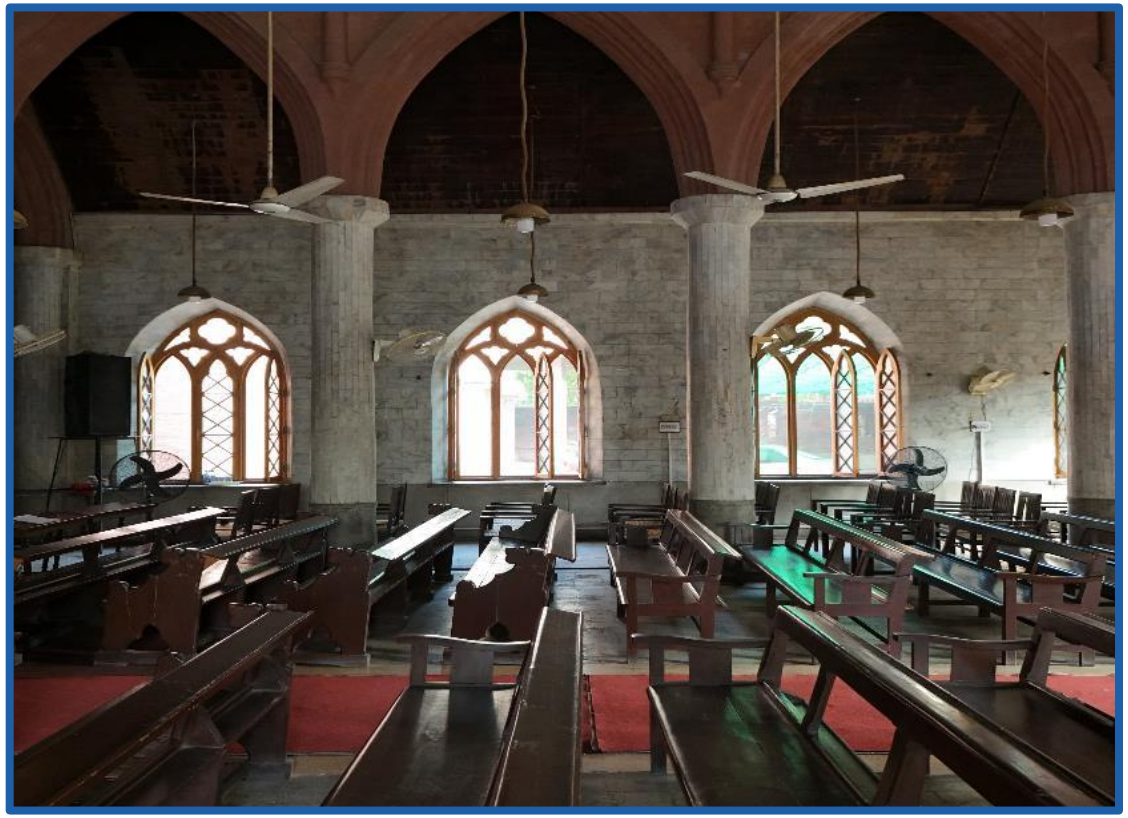

Before

Work in Progress

Saint Andrew’s Presbyterian Church

Exterior Wall Restoration & Roof Waterproofing

Physical Progress: 88%
Completion Date: 30-09-2026

Before

Work in Progress

Saint Andrew's Presbyterian Church

ARCHES INSIDE NICHES

Physical Progress: 80%
Completion Date: 30-09-2026

Before

Work in Progress

Saint Andrew's Presbyterian Church

Landscape

Physical Progress: 80%
Completion Date: 30-09-2026

Work in Progress

Work in Progress

Back

Establishment of Improvement and Up-gradation Of TDCP Patriata Chairlift / Cable Car District Murree (Component-B)

Responsibility: TAM / TDCP
Cost: PKR **499.545** million

Scope of work
1) Gates 7-Nos
2) Waiting Areas (2 No at Base & ,3-No at patriata Top)
3) Gazebos-5 Nos
4) Glamping Pods-12-Nos.
5) Parking
6) Souvenir Shop 6-Nos

Progress so far
1) 1-Gate at base installed fabrication left; gate 2 pillars installed. Rest 2 base plus 3 top remaining
2) Waiting Areas (1 No at top completed, 01 No at top frame work is installing, 01 remaining at top, no work on 02 on base
3) Gazebos platforms are complete, structure of 5 left
4) Glamping PODs (square and dome shape) 2 as a sample structure being prepared
5) 40% Parking civil work completed.
6) Souvenir Shops 4-Nos in progress, frame complete, 2 no work

Physical Progress 30%
Financial Progress12%
Allocation CFY 2026-27: 120 Mn
Additional Funds Demand: 205.529 Mn

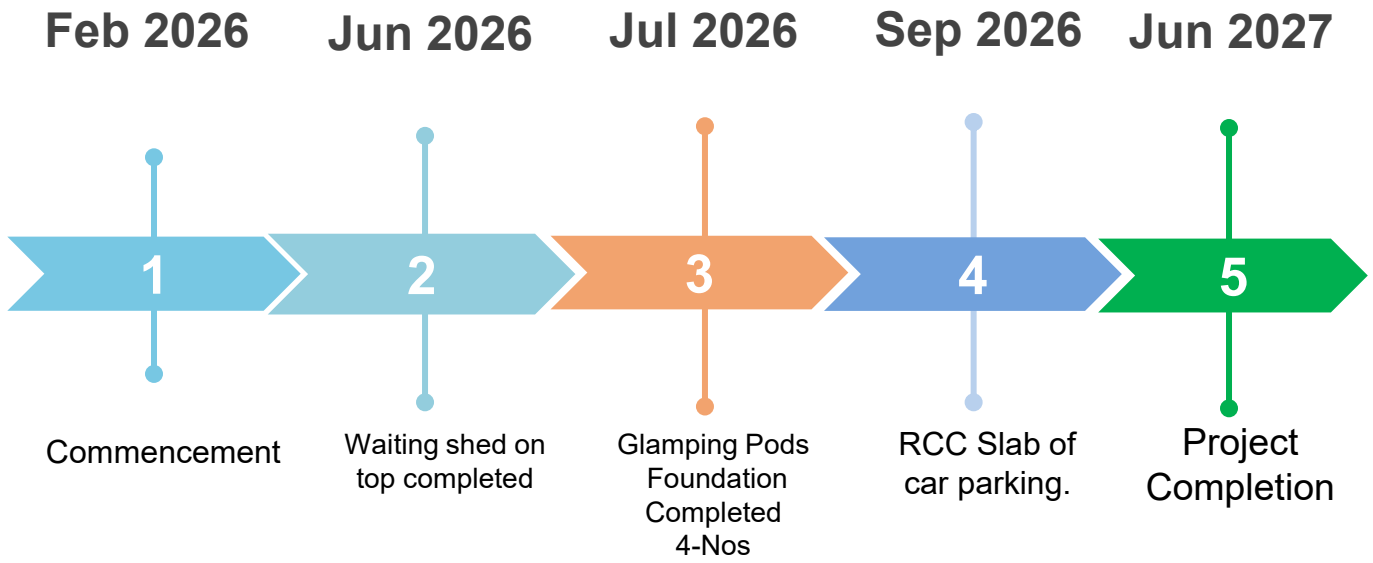

Project Start Date: **16 Feb 2026**
Completion Date as per PC-1: **30 Jun 2027**

Next 30 Days Plans:

RCC Slab of car parking to be completed	30 Sep 2026
Waiting shed to be completed	30 Sep 2026

Components of the Project

Component Name	Physical Progress	Expected Completion	Status
Gates 4-Nos at Base 3-Nos at Top	15%	20-03-2027 Base point two gates to be completed by 30.09.2026	On Track
Waiting Area 2-Nos at Base 3-Nos at Top	30%	20-03-2027 one on top point is complete and one on base point in progress completion date 30.09.2026	On Track
Gazebos- (5 Nos)	30%	25-03-2027 foundations for 5 complete structure is in progress	On Track
Glamping Pods- 7-Nos Square Shape on Top 5-Nos Dome Shape on Top	15%	30-03-2027	On Track
Souvenir Shop 6-Nos	20%	15-04-2027	On Track
Car Parking	25%	30-09-2026 RCC slab to be completed by 30.09.2026	On Track

On Track
Delayed
Critical

TDCP Resort **PATRIATA (Component-B)**

Gate 1
At Base

Physical Progress: 0%
Completion Date:Work Not Started

Proposed

Not started

TDCP Resort **PATRIATA (Component-B)**

Gate 2
At Base

Physical Progress: 10%
Completion Date:20-03-2027

Proposed

Work in Progress

TDCP Resort **PATRIATA (Component-B)**

Gate 3
At Base

Physical Progress: 60%
Completion Date:20-03-2027

Proposed

Work in Progress

TDCP Resort **PATRIATA (Component-B)**

Gate 4
At Base

Physical Progress: 0%
Completion Date: Work Not Started

Proposed

Not started

TDCP Resort **PATRIATA (Component-B)**

Gate 1
At Top

Physical Progress: 0%
Completion Date: Work Not Started

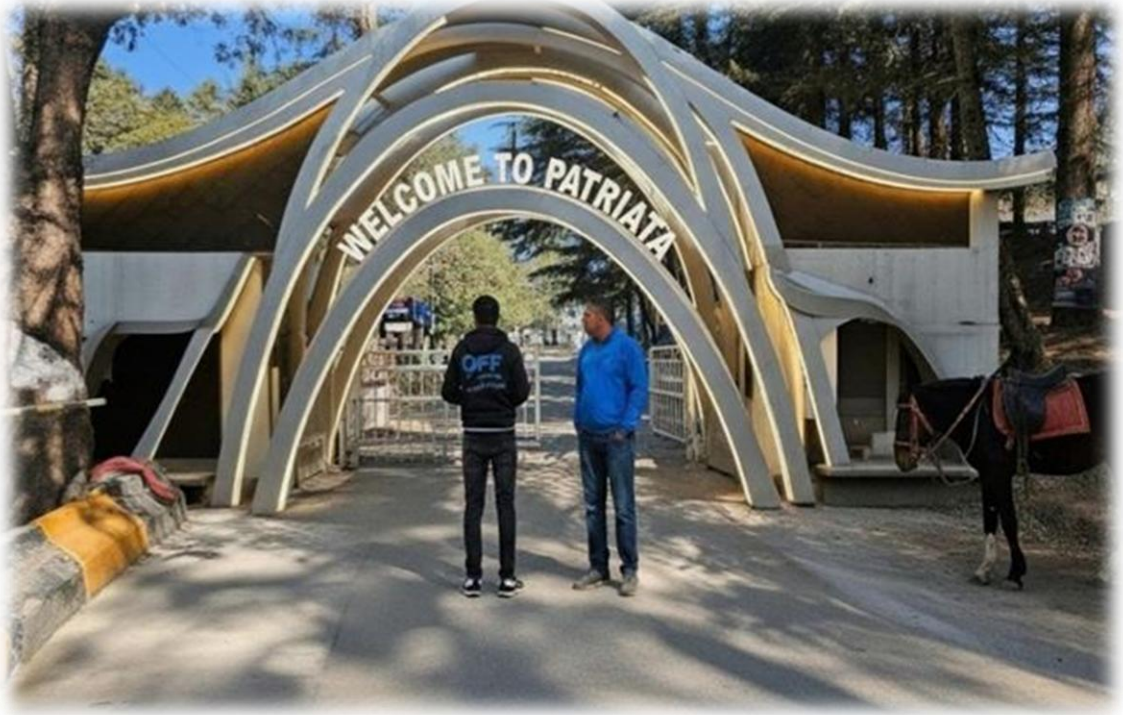

Proposed

Not started

TDCP Resort **PATRIATA (Component-B)**

Waiting area 1
At Base

Physical Progress: 20%
Completion Date: 20-03-2027

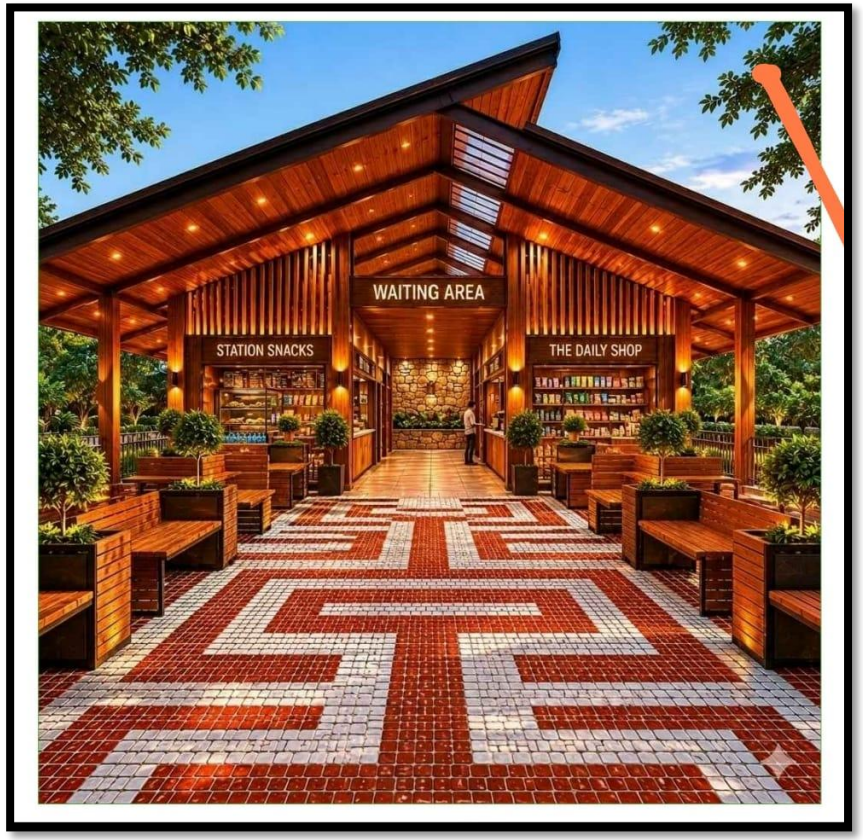

Proposed

Work in Progress

TDCP Resort **PATRIATA (Component-B)**

Waiting area 2
At Base

Physical Progress: 0%
Completion Date: Work Not Sarted

Proposed

Not started

TDCP Resort **PATRIATA (Component-B)**

Waiting area 1
At Top

Physical Progress: 90%
Completion Date: 30.09.2026

Proposed

Work in Progress

TDCP Resort **PATRIATA (Component-B)**

Waiting area 2
At Top

Physical Progress: 30%
Completion Date: 20-03-2027

Proposed

Work in Progress

TDCP Resort **PATRIATA (Component-B)**

Waiting area 3
At Top

Physical Progress: 0%
Completion Date: Work Not Started

Proposed

Not started

TDCP Resort **PATRIATA (Component-B)**

Gazeebos

Physical Progress: 30%
Completion Date: 25-03-2027

Proposed

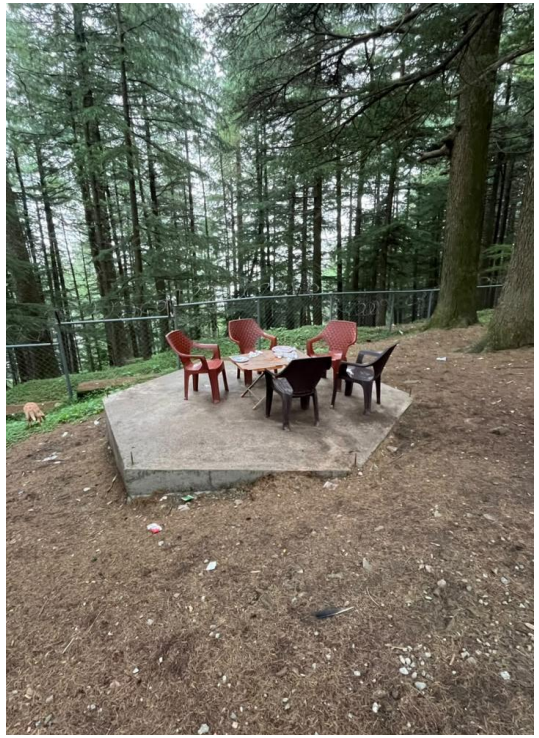

Work in Progress

TDCP Resort **PATRIATA (Component-B)**

DOME SHAPE GLAMPING PODS

Physical Progress: 80%
Completion Date: 30.03.2027

Proposed

Work in Progress

TDCP Resort **PATRIATA (Component-B)**

SQUARE SHAPE GLAMPING PODS

Physical Progress: 80%
Completion Date: 30.03.2027

Proposed

Work in Progress

TDCP Resort **PATRIATA (Component-B)**

Souvenir shop

Physical Progress: 20%
Completion Date: 15-04-2027

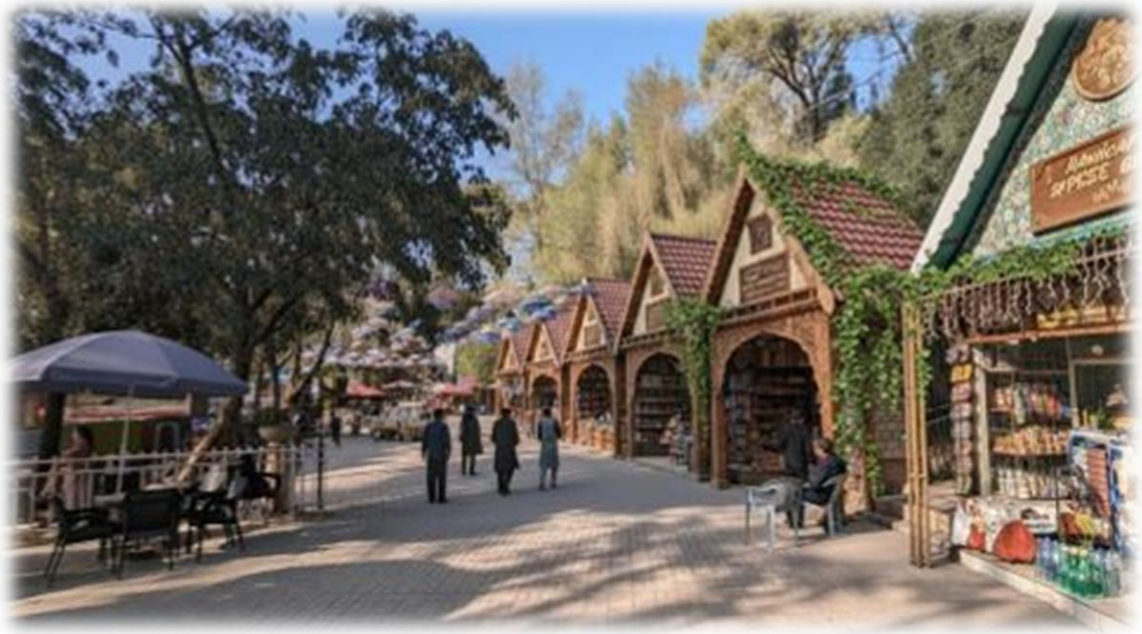

Proposed

Work in Progress

TDCP Resort **PATRIATA (Component-B)**

Car Parking

Physical Progress:25%
Completion Date: 30-09-2026

Proposed

Work in Progress

TDCP Resort **PATRIATA (Component-B)**

Car Parking
Entrance Gate 1

Physical Progress: 0%
Completion Date: work not started

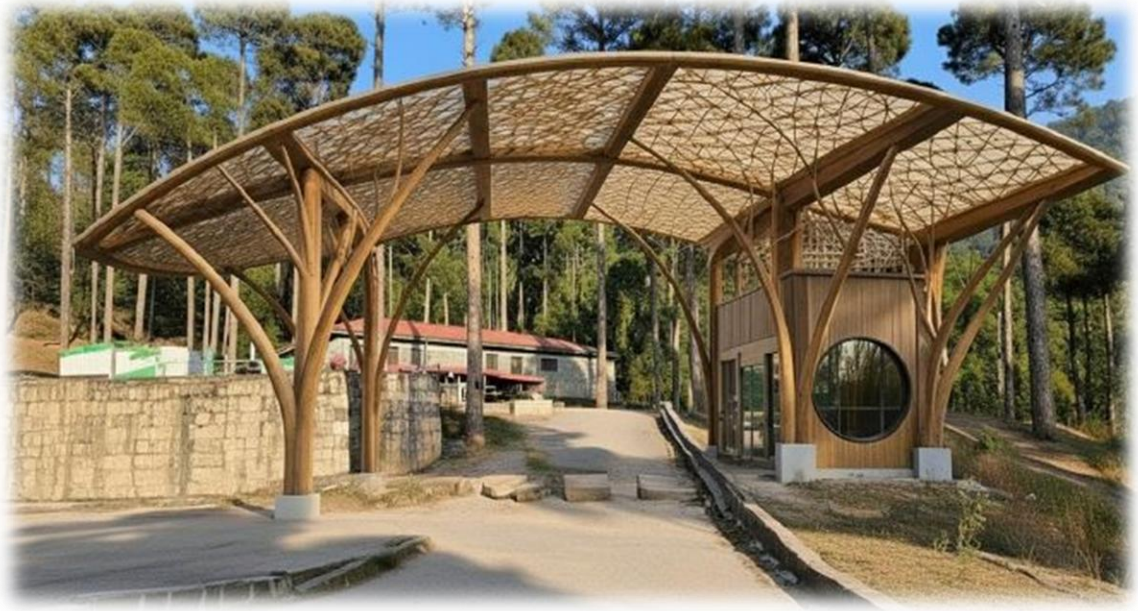

Proposed

Work not started

TDCP Resort **PATRIATA (Component-B)**

Car Parking
Exit Gate 2

Physical Progress: 0%
Completion Date: work not started

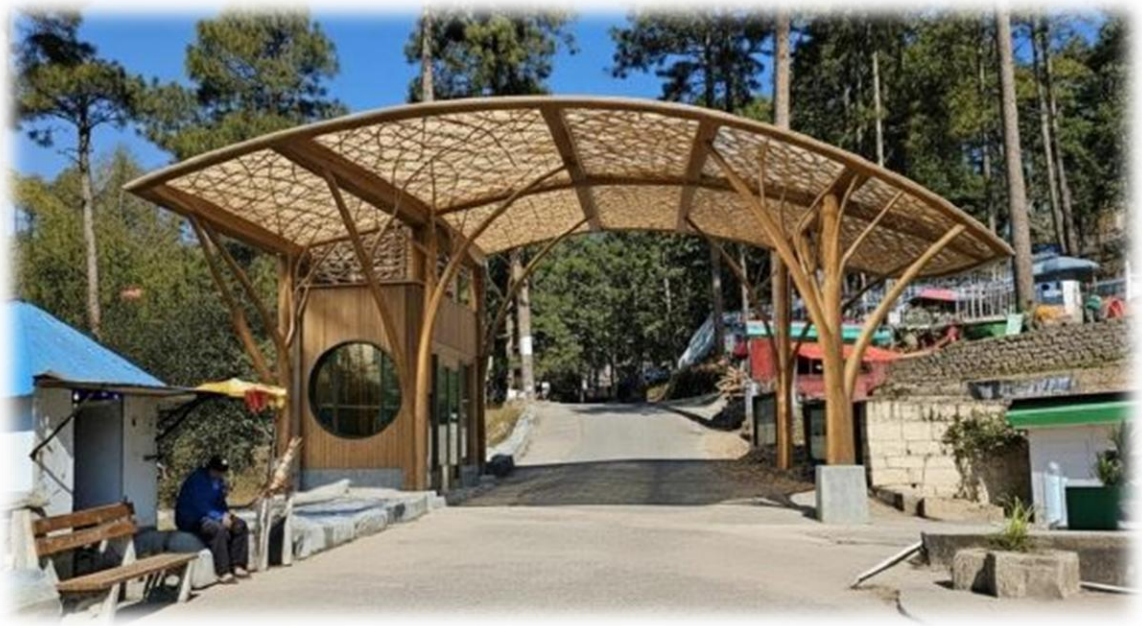

Proposed

Work not started

Remarks:

- **Kiosks:** Physical progress of kiosk at base and on top is delayed
- **Gates:** Work is in progress on 2-Nos Gates only at base,work is pending on 2 Gates at base , meanwhile no any physical work is placed on gates present on Patriata Top.
- **Souvenior Shops:** out of 6, just 4 are in progress which include the framework
- **Waiting area:** 1 is nearly to complete on top,1 at base and 1 at top is under construction, meanwhile no work is started on remaining waiting areas (1 at base & 1 at top).
- **Car Parking:** Shuttering work and cvil work is Delayed due to weather Conditions, no work is started on the gates of Parking area.
- **Selfie-Point :** work is in progress at base and no work is started at Top.
- **Stone Pitched Pathway:** Stone Pathways have been laid on Base and Top.

Observations:

According to demand and scope of work Deployed labour is very less on average on daily basis.
Project working pace is slow due to weather condition.
No any kind of work has been started on Mid Point.

ESTABLISHMENT OF PARAGLIDING CLUB AT CHEWRA HILL TOP, KOTLI SATTAIN

Responsibility: TAM / TDCP
Cost: PKR **423.927** million

Physical Progress	47%
Financial Progress	25%
Allocation CFY 2026-27:	30 Mn
Additional Funds Demand:	190.012 Mn

Scope of work
1) Eco-Friendly Glamping Pods- 10 Nos
2) Tree Houses- 2 Nos
3) Gazebos- 5 Nos
4) Bonfire (03)
5) A-frame steel frame (Restaurant)
6) External Works including Boundary Wall , OHR & Gates etc.

Progress so far
1) 2 out of 8-GLAMPING PODS ready, 05 PODS steel structure ready, 03 Pods base ready.
2) Tree House 02 polish and woodwork on pillars in progress
3) 3 Gazebos wooden work completed, 01 Gazebo half done, 01 Base ready
4) Bonfire civil work completed, Stone work is in progress
5) 20% civil works for restaurant completed. Steel frame left
6) External works completed 25%

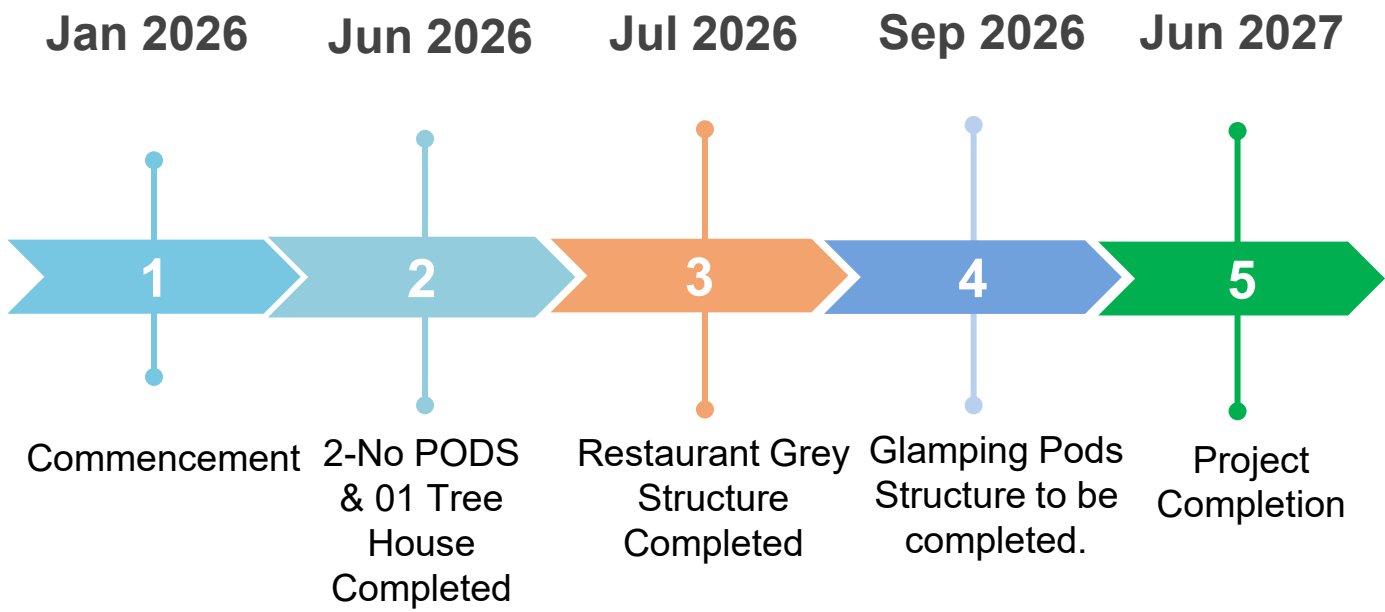

Project Start Date:	16 January 2026
Completion Date by PC-I:	30 June 2027

Next 30 Days Plans:

Gazebos to be completed	30 Sep 2026
Both Tree-Houses to be completed	30 Sep 2026

Back

Components of the Project

Component Name	Physical Progress	Expected Completion	Status
Bonfire	75%	30-09-2026	On Track
Tree-House (02)	75%	30-10-2026	On Track
Gazebos(05)	75%	30-10-2026	On Track
Glamping PODS (10-Nos)	35 %	30-04-2027	On Track
External Works (OHR, BW, Main Gate, Pathways & Street Lights)	25%	30-06-2027	On Track
Restaurant (A-Frame)	20%	30-04-2027	On Track

- On Track
- Delayed
- Critical

ESTABLISHMENT OF PARAGLIDING CLUB AT CHEWRA HILL TOP, KOTLI SATTAIN

Drone Video

ESTABLISHMENT OF PARAGLIDING CLUB AT CHEWRA HILL TOP, KOTLI SATTAIN

BONFIRE

Physical Progress: 75%
Completion Date: 30-09-2026

Proposed

Work in Progress

ESTABLISHMENT OF PARAGLIDING CLUB AT CHEWRA HILL TOP, KOTLI SATTAIN

Tree House

Physical Progress: 75%
Completion Date: 30-10-2026

Design Concept

Work in Progress

ESTABLISHMENT OF PARAGLIDING CLUB AT CHEWRA HILL TOP, KOTLI SATTAIN

GAZEBO

Physical Progress: 75%
Completion Date: 30-10-2026

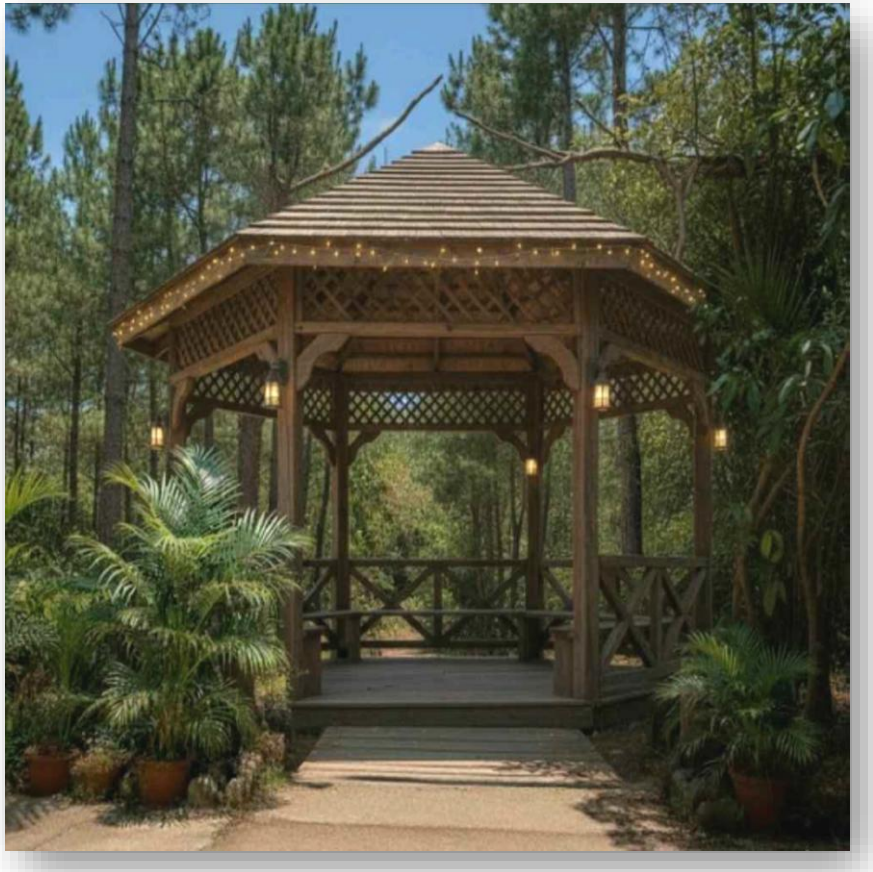

Proposed

Work in Progress

ESTABLISHMENT OF PARAGLIDING CLUB AT CHEWRA HILL TOP, KOTLI SATTAIN

GLAMPING POD

Physical Progress: 35%
Completion Date: 30-04-2027

Proposed

Work in Progress

ESTABLISHMENT OF PARAGLIDING CLUB AT CHEWRA HILL TOP, KOTLI SATTAIN

INTERIOR

ESTABLISHMENT OF PARAGLIDING CLUB AT CHEWRA HILL TOP, KOTLI SATTAIN

ESTABLISHMENT OF PARAGLIDING CLUB AT CHEWRA HILL TOP, KOTLI SATTAIN

EXTERNAL WORKS

Physical Progress: 25%
Completion Date: 30-06-2027

OHR, Public Wash Room & Boundary Wall

ESTABLISHMENT OF PARAGLIDING CLUB AT CHEWRA HILL TOP, KOTLI SATTAIN

RESTAURANT

Physical Progress: 20%
Completion Date: 30-04-2027

Proposed

Work in Progress

Back

Project Status & Reasons for Delay

• **Weather Conditions:** Minor delays are being experienced due to ongoing rainfall, which is affecting the pace of work at the site.

Wire Issue: The main wire is passing through the site, which is affecting the work. Because of this, the boundary wall work is on hold. The fountain, gazebo and gate works are also affected. And the issue has already been discussed with the TDCP team

Labour: The labour force is also less than required at the moment, which is affecting the overall progress.

Site Focal Person	Phone Number
Rana Arif	03214255624

Back

Improvement, Revitalization, and Upgradation of TDCP Tourist Resort Jallo, District Lahore

Responsibility: TAM / TDCP
Cost: PKR **599.000** million

Scope of Work	Progress so far
1.Revamping of Guest Room Type A & B with Mini Pools 9 Nos 2.Construction of Convention Center. 3.Construction of Restaurant New 4.Construction of 4 Mud Houses. 5.Construction of Elevated Tree Deck 10 Nos 6.Pathways 7.Sewerage System & Soakage Well 8.Upgradation of Café existing.	1.Guest Room Type A big grey structure done, one A type into mud house. One B type ready Work only 3 B type Guest Houses in progress, rest 4 stopped 2.Convention Center RCC frame structure 90% completed. 3.Restaurant New RCC gray structure completed 4.All Mud house's gray structure completed 5.Elevated Tree deck 6/10 completed. 6. Pathways in progress 7.Soakage Well 85% complete & Sewerage lines in progress 8.Upgradation of Café in progress

Project Start Date:	**12 Feb 2026**
Completion Date by PC-1:	**30 Jun 2027**

Physical Progress	**40%**
Financial Progress	**21%**
Allocation CFY 2026-27:	**115 Mn**
Additional Funds Demand:	**357 Mn**

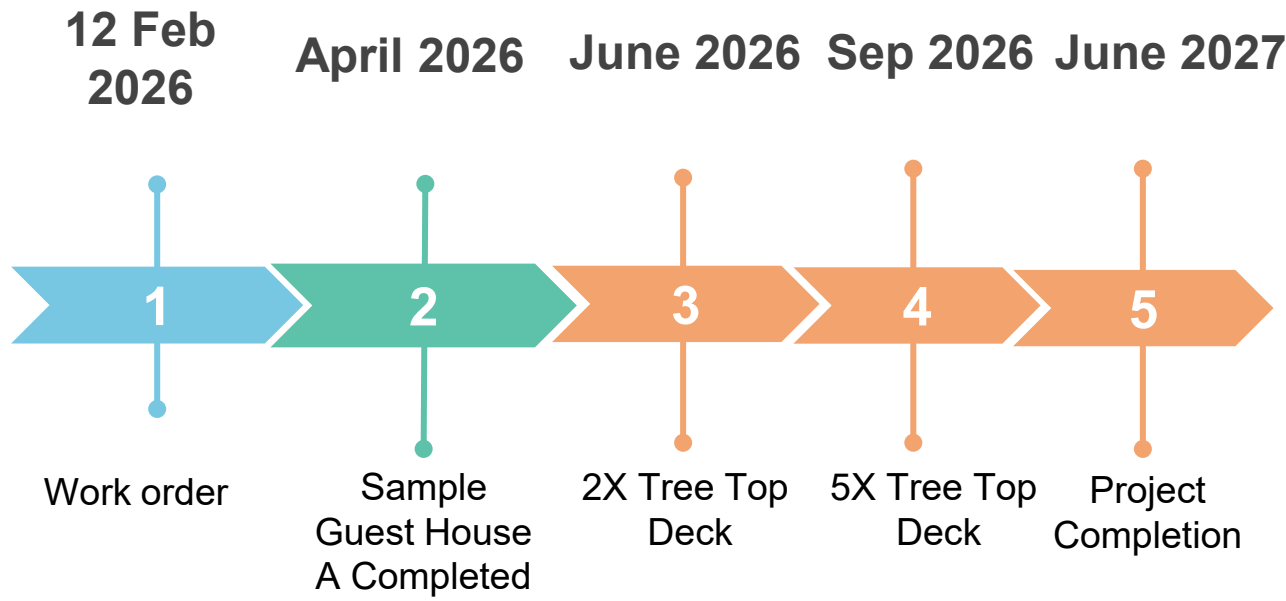

Next 30 Days Plans:

10 x Elevated tree deck completed	30 Sep 2026
Mud houses completed on	30 Sep 2026

Back

Components of the Project

Component Name	Physical Progress	Expected Completion	Status
Guest Houses Type A & B 9 Nos	40%	20-04-2027	On Track
Restaurant New	55%	30-04-2027	On Track
Convention Center	45 %	30-03- 2027	On Track
Mud Houses 4 Nos	75%	15-09-2026	On Track
Elevated Tree Deck 10 Nos	70%	15-09-2026	On Track
Sewerage System & Soakage Well	45%	30-04-2027	On Track
Café	30%	31-12-2026	On Track

On Track
Delayed
Critical

Improvement, Revitalization, and Upgradation of TDCP Tourist Resort Jallo, District Lahore

Guest Rooms Type B completed

Physical Progress: 40%
Completion Date: 20-04-2027

Proposed

Complete

Improvement, Revitalization, and Upgradation of TDCP Tourist Resort Jallo, District Lahore

Physical Progress: 40%
Completion Date: 20-04-2027

Guest Rooms Type B

Proposed

Complete

Improvement, Revitalization, and Upgradation of TDCP Tourist Resort Jallo, District Lahore

Guest Rooms Type A

Physical Progress: 40%
Completion Date: 20-04-2027

Work in Progress

Improvement, Revitalization, and Upgradation of TDCP Tourist Resort Jallo, District Lahore

Guest Rooms Type B

Physical Progress: 40%
Completion Date: 20-04-2027

Work in Progress

Work in Progress

Improvement, Revitalization, and Upgradation of TDCP Tourist Resort Jallo, District Lahore

Restaurant New

Physical Progress: 55%
Completion Date: 30-04-2027

Proposed

Work in Progress

Improvement, Revitalization, and Upgradation of TDCP Tourist Resort Jallo, District Lahore

Restaurant New

Physical Progress: 55%
Completion Date: 30-04-2027

Work in Progress

Improvement, Revitalization, and Upgradation of TDCP Tourist Resort Jallo, District Lahore

Convention Centre

Physical Progress: 45%
Completion Date: 30-04- 2027

Proposed

Work in Progress

Improvement, Revitalization, and Upgradation of TDCP Tourist Resort Jallo, District Lahore

Mud Houses

Physical Progress: 75%
Completion Date: 15-09-2026

Proposed

Work in Progress

Improvement, Revitalization, and Upgradation of TDCP Tourist Resort Jallo, District Lahore

Improvement, Revitalization, and Upgradation of TDCP Tourist Resort Jallo, District Lahore

Elevated Tree Deck

Physical Progress: 70%
Completion Date: 15-09-2026

Proposed

Work in Progress

Improvement, Revitalization, and Upgradation of TDCP Tourist Resort Jallo, District Lahore

Café

Physical Progress: 30%
Completion Date: 31-12-2026

Work in Progress

Back

Construction of Sky Glass Bridge at Panjpeer Rocks Tehsil Kotli Sattain District Murree

Responsibility: TAM / TDCP
Estimated Cost: PKR **2.4** billion

Scope of work
• Land Acquisition • Glass Bridge Deck Glass and Fabricated Steel • Architectural Works • Structures • Electrical Works • Plumbing and External Water Supply & Drainage • Road Works • Firefighting • Slope Stabilization

Progress
• Feasibility completed • Scheme stands approved from PDWP and included in ADP-2026-27 • Land Acquisition and EPC tender is published

Physical Progress: **100% (Feasibility)**
Financial Progress:
Allocation CFY 2026-27: **20 Mn**
Additional Funds Demand: **945 Mn**

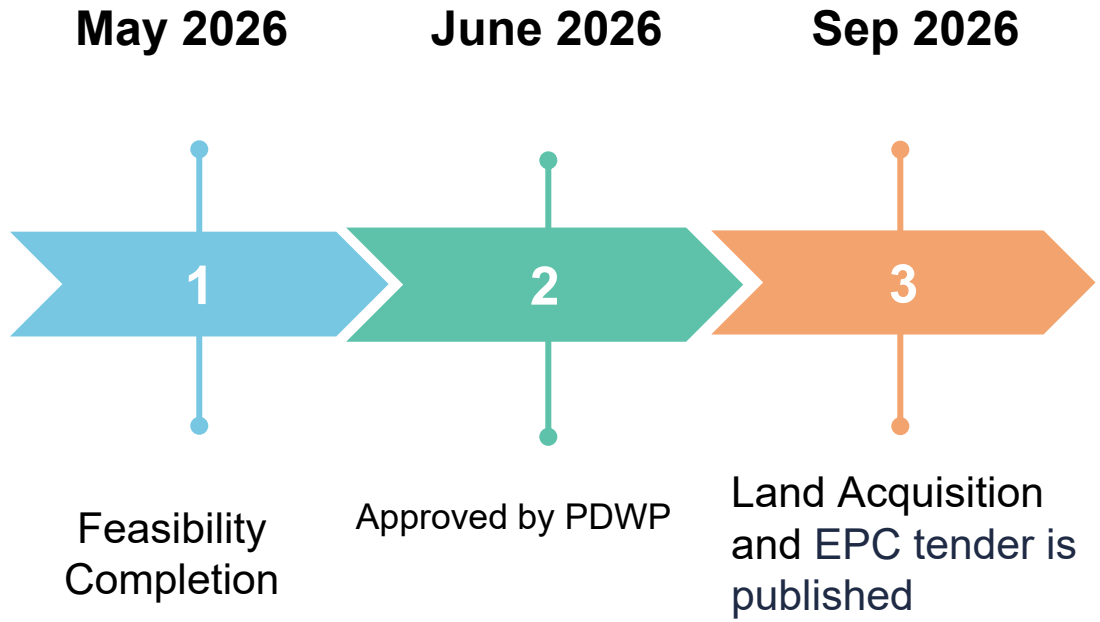

Project Start Date: **16 Feb 2026**
Completion Date as per PC-1: **30 Jun 2028**

Next 30 Days Plans:
Land Acquisition

Back

Construction of Sky Glass Bridge at Panjpeer Rocks Tehsil Kotli Sattain District Murree

Proposed Design

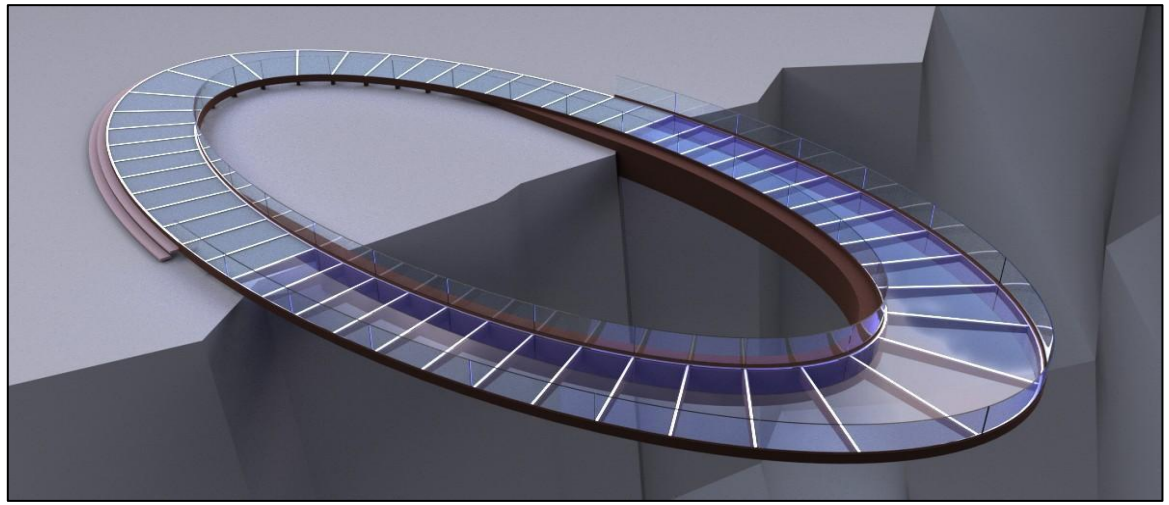

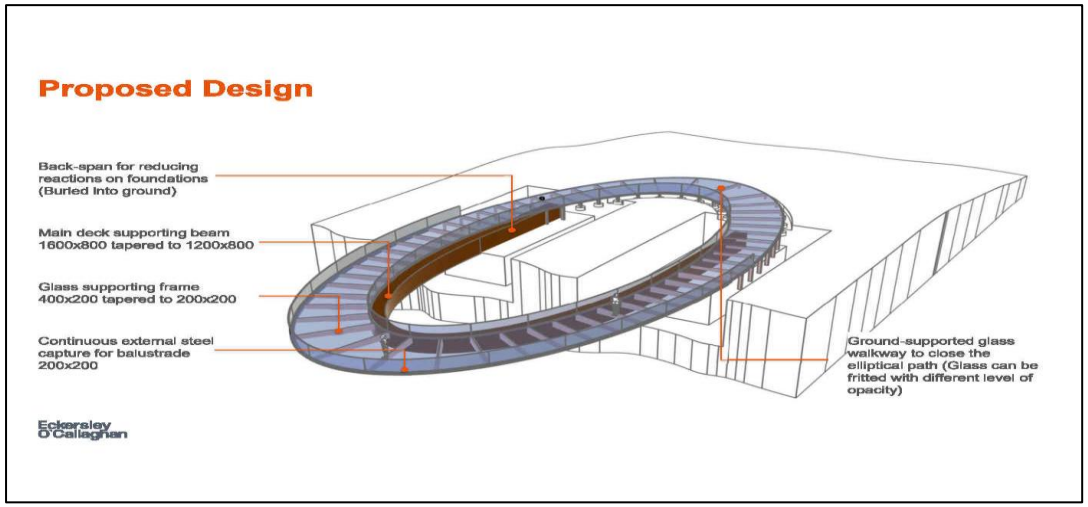

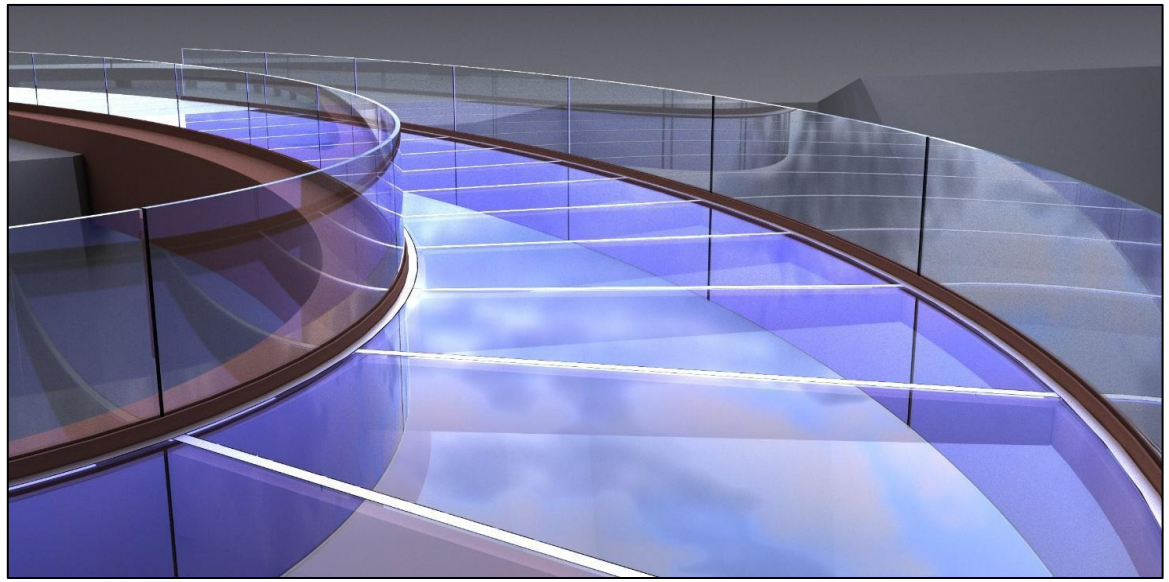

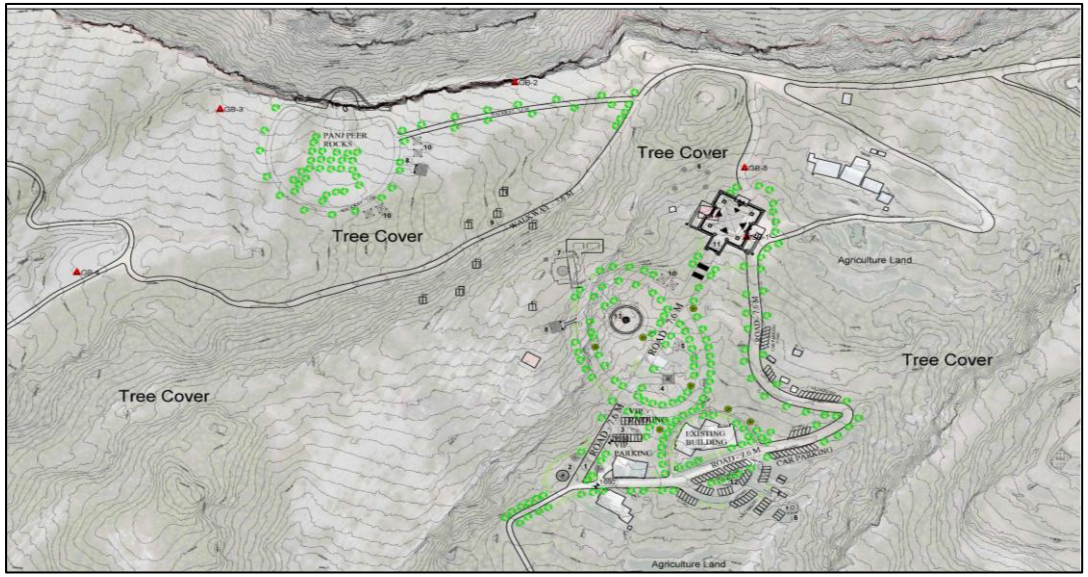

Construction of Sky Glass Bridge at Panjpeer Rocks Tehsil Kotli Sattain District Murree

Selected Site for Sky Walk Glass Bridge

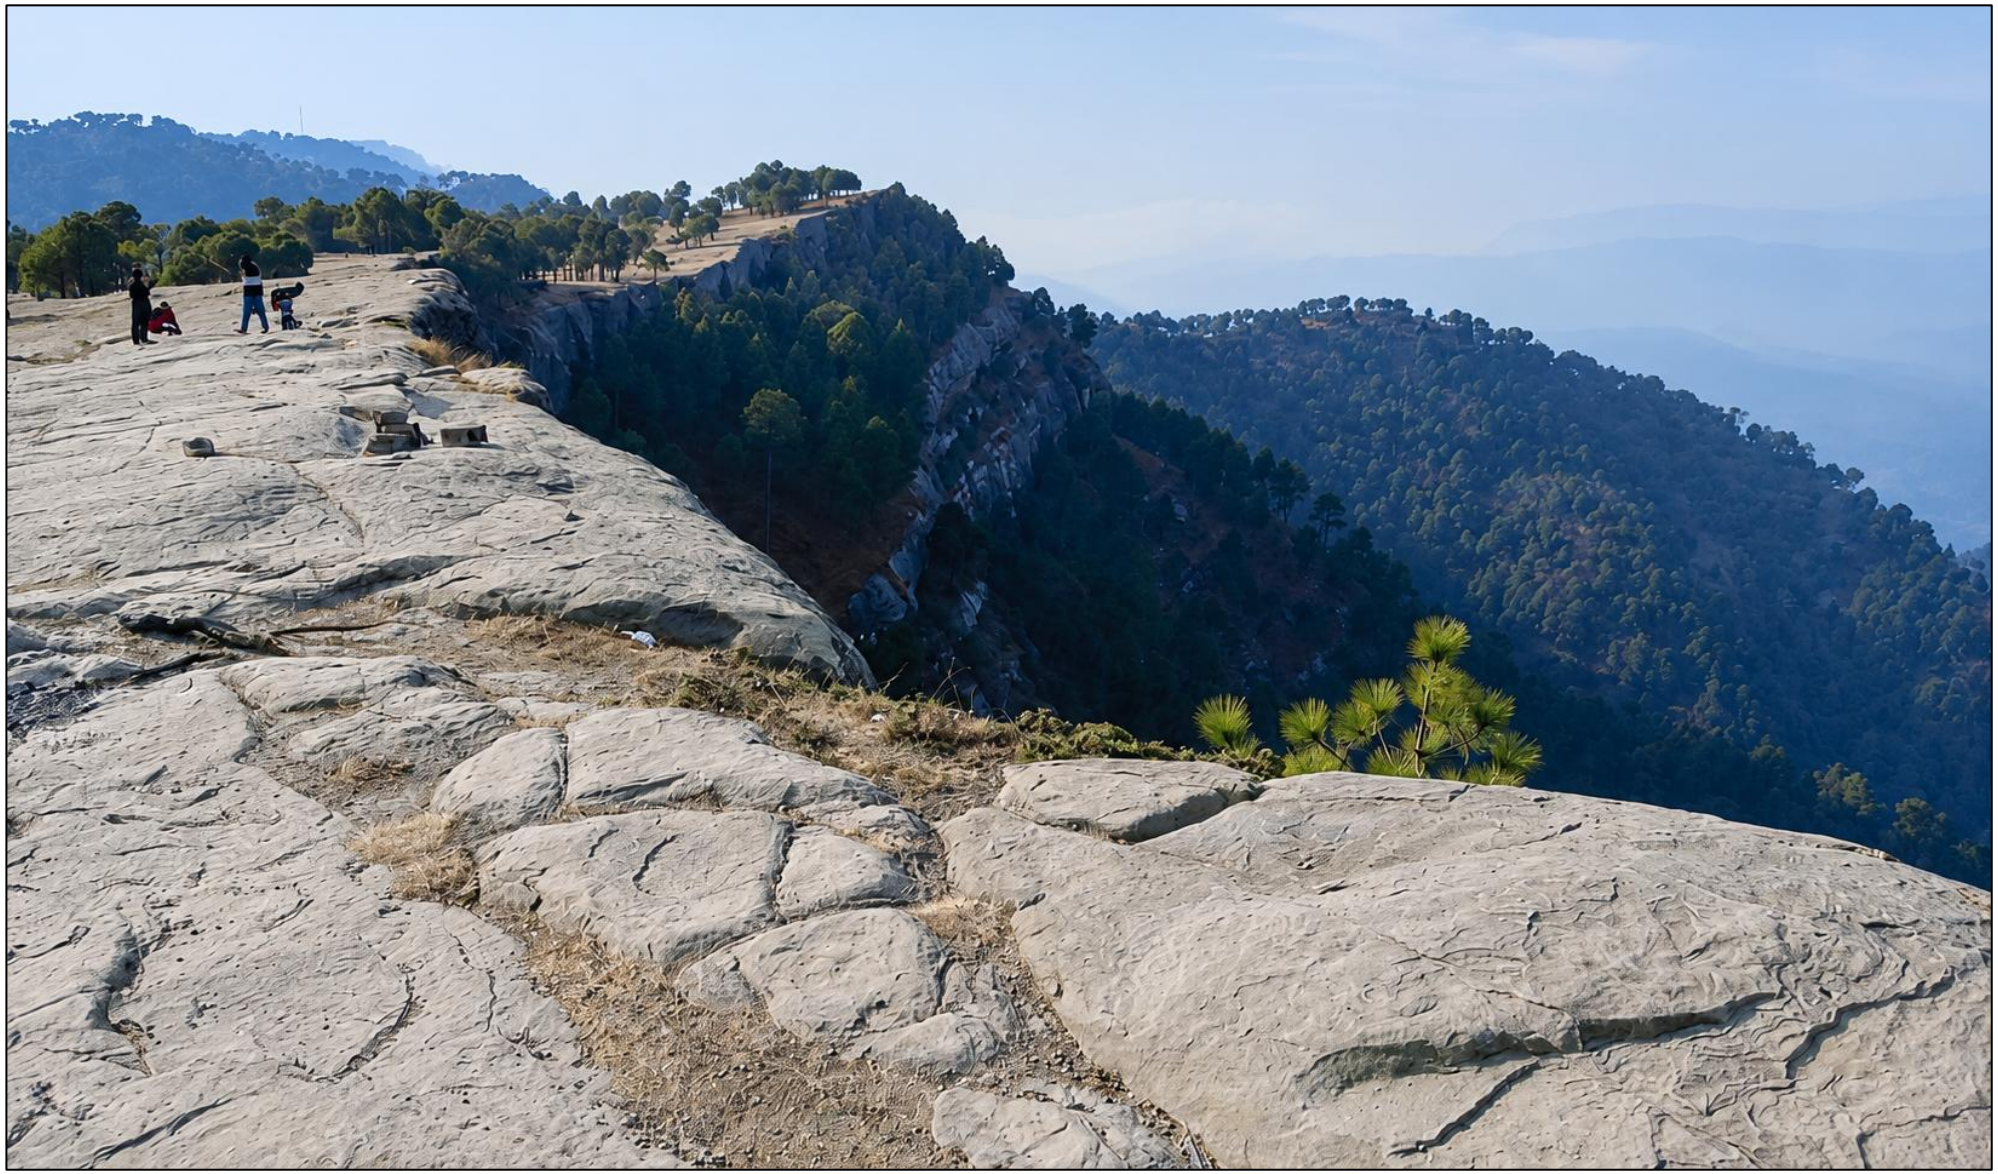

Back

Daak Bungalows-Missa Kaswal

Responsibility: TAM / TDCP
Cost: 50.7 million

Scope of work
1. Structural stabilization and restoration
2. Repair and conservation of masonry and plaster
3. Roof rehabilitation and waterproofing
4. Installation of doors, windows, and woodwork
5. Landscaping and site improvement works

Progress so far
1. Structural Stabilization and Restoration — 80%
2. Repair and Conservation of Masonry and Plaster — 85%
3. Roof Rehabilitation and Waterproofing — 80%
4. Restoration of Doors, Windows, and Woodwork — 10%
5. Landscaping and Site Improvement Works — 30%

Project Start Date:	**October 2025**
Completion Date As Per PC1:	**30 Jun 2027**
Completion Date As Per TAM:	**31 March 2027**

Physical Progress:	60%
Financial Progress:	40%
Allocation (2026-27)	10 Million
Additional Funds Demand	30 Million

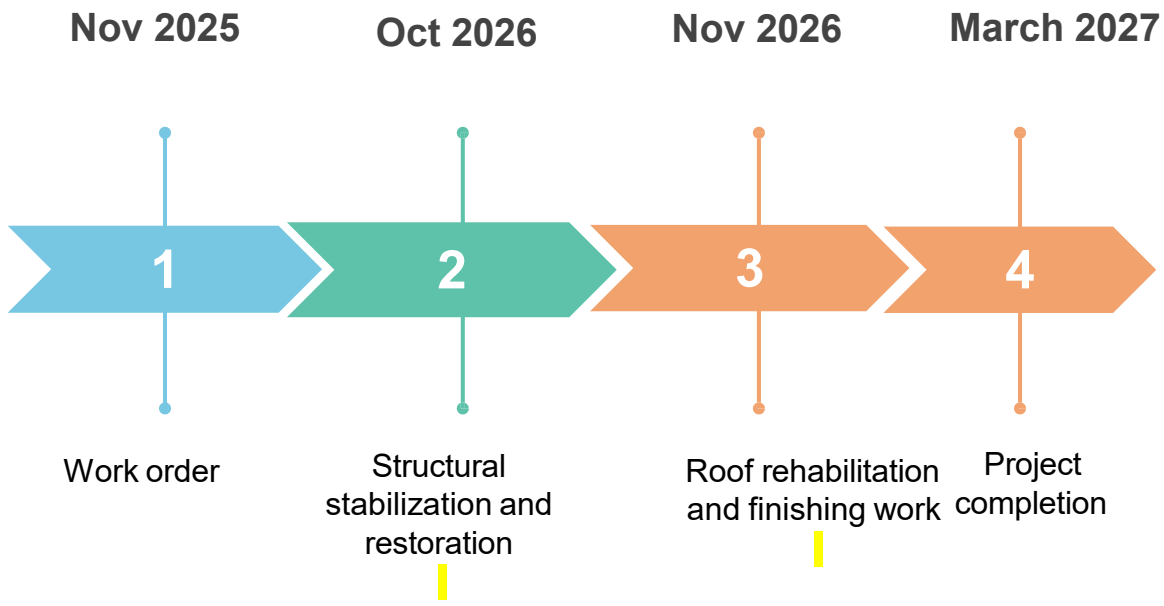

Next 30 Days Plans:

Structural stabilization and restoration

Components of the **Project-** Restoration of Missa Kaswal

Component	Progress	Completion	Status
Structural stabilization and restoration	80%	30-10-2026	On Track
Repair and conservation of masonry and plaster	85%	30-10-2026	On Track
Roof rehabilitation and waterproofing	80%	15-12-2026	On Track
Installation of doors, windows, and woodwork	10%	30-02-2027	On Track
Landscaping and site improvement works	30%	31-03-2027	On Track

= **On Track**
= **Delayed**
= **Critical**

Daak Bungalows

Conservation work at Missa Kaswal

Physical progress: 80%
Completion: 31-09-2026

Before

Work in Progress

Daak Bungalows

Conservation work at Missa Kaswal

Physical progress: 85%
Completion: 31-03-2027

Before

Work in Progress

Daak Bungalows

Conservation work at Missa Kaswal

Physical progress:80%
Completion:31-03-2027

Before

Work in Progress

Daak Bungalows

Conservation work at Missa Kaswal

Physical progress:80%
Completion:31-03-2027

Before

Work in Progress

Daak Bungalows

Conservation work at Missa Kaswal

Physical progress:10%
Completion:31-03-2027

Work in Progress

Work in Progress

Daak Bungalows

Conservation work at Missa Kaswal

Physical progress:30%
Completion:31-03-2027

Work in Progress

Work in Progress

Project Observations

- **Overall Status:** Progress is very good, with **60% physical progress** and **85% financial progress**. The overall project status is **On Track**.
- **Key Achievements:**
  - Structural stabilization & restoration: **80% complete**.
  - Masonry & plaster repairs: **85% complete**.
  - Roof rehabilitation & waterproofing: **80% complete**.
  - Landscaping & site improvement: **30% complete**.

Pending Work: Installation of doors, windows, and woodwork is currently at **10%**

Site Focal Person	Phone Number
Shoaib	03454888824

Back

Daak Bungalows-Tibbi Syedan

Responsibility: TAM / TDCP
Cost: 46.056 million

Scope of work	Progress so far
1. Structural stabilization and restoration	1. Structural Stabilization and Restoration — 80%
2. Repair and conservation of masonry and plaster	2. Repair and Conservation of Masonry and Plaster — 70%
3. Roof rehabilitation and waterproofing	3. Roof rehabilitation and waterproofing ___ 70%
4. Restoration of doors, windows, and woodwork	4. Restoration of doors, windows, and woodwork ___ 10%
5. Landscaping and site improvement works	5. Landscaping and site improvement works__ 15%

Completion Date As Per PC1: **30 Jun 2027**
Completion Date As Per TAM: **31st May 2027**

Physical Progress:	**50**%
Financial Progress:	**2**0%
Allocation (2026-27)	10 Million
Additional Funds Demand	30 Million

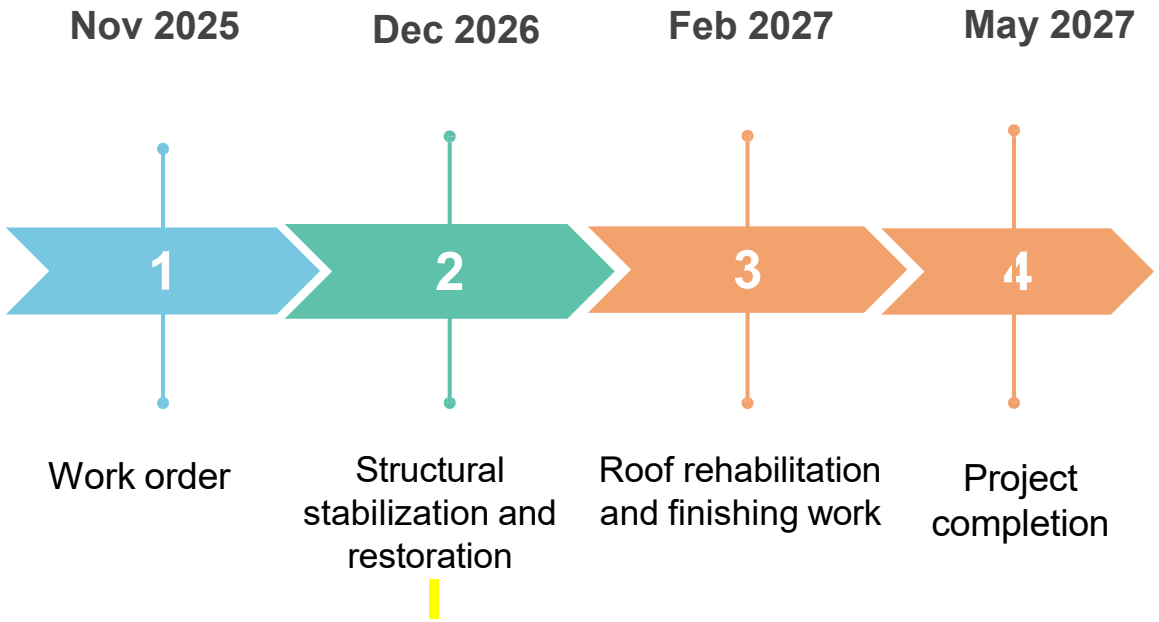

Next 30 Days Plans:

Structural stabilization and restoration

Components of the Project-Restoration of Tibbi Syedan

Component	Progress	Completion	Status
Structural stabilization and restoration	80%	30-11-2026	On Track
Repair and conservation of masonry and plaster	70%	30-12-2026	On Track
Roof rehabilitation and waterproofing	70%	15-01-2027	On Track
Restoration of doors, windows, and woodwork	10%	15-02-2027	On Track
Landscaping and site improvement works	15%	30-05-2027	On Track

= On Track
= Delayed
= Critical

Daak Bungalows

Conservation work at Tibbi Syedan

Physical progress:80%
Completion:31-05-2027

Before

Work in Progress

Daak Bungalows

Conservation work at Tibbi Syedan

Physical progress: 80%
Completion:31-05-2027

Before

Work in Progress

Daak Bungalows

Conservation work at Tibbi Syedan

Physical progress: 80%
Completion:31-05-2027

Before

Work in Progress

Daak Bungalows

Conservation work at Tibbi Syedan

Physical progress: 10%
Completion:31-05-2027

Work in Progress

Work in Progress

Daak Bungalows

Conservation work at Tibbi Syedan

Physical progress: 70%
Completion:31-05-2027

Work in Progress

Work in Progress

Project Observations

- **Overall Status:** Physical progress is at **50%** (component site photos show overall site progress around 50%) with **20% financial progress**. Overall project status is **On Track**.
- **Key Achievements:**
  - Structural stabilization: **80% complete**.
  - Masonry & plaster conservation: **80% complete**.
  - Roof rehabilitation & waterproofing: **70% complete**.
- **Pending Work:**
  - Doors, windows, and woodwork: **10% complete**.

Landscaping & site works: **15% complete**.

Site Focal Person	Phone Number
Shoaib	03454888824

Back

Preservation, Restoration, Improvement, Management and Upgradation of UMAR HAYAT MAHAL, CHINIOT

Presented by Hassan

Preservation, Restoration, Improvement, Management and Upgradation of UMAR HAYAT MAHAL, CHINIOT

Responsibility: TAM / ARCHAEOLOGY
Cost: PKR 143.469 M

Physical Progress	70%
Financial Progress	70%
Allocation (2026-27)	10 Million
Additional Funds Demand	20 Million

Scope of Work
1. Conservation/Restoration of Palace
2. Restoration of Floors
3. Fresco & Stucco work
4. Furniture
5. Illumination
6. Restoration of Wood Work (Doors and Jharoka)

Progress So far
1. Structural Stabilization — 70%
2. Restoration of Floors — 90%
3. Ornamental Stucco Work — 80%
4. Ornamental Fresco Work — 70%
5. Wooden Tarseem Bandi — 90%
6. Ornamental Ceiling Work — 90%
7. Furniture — 50%
8. Illumination — 50%
9. Restoration of Wood Work (Doors and Jharoka) — 90%

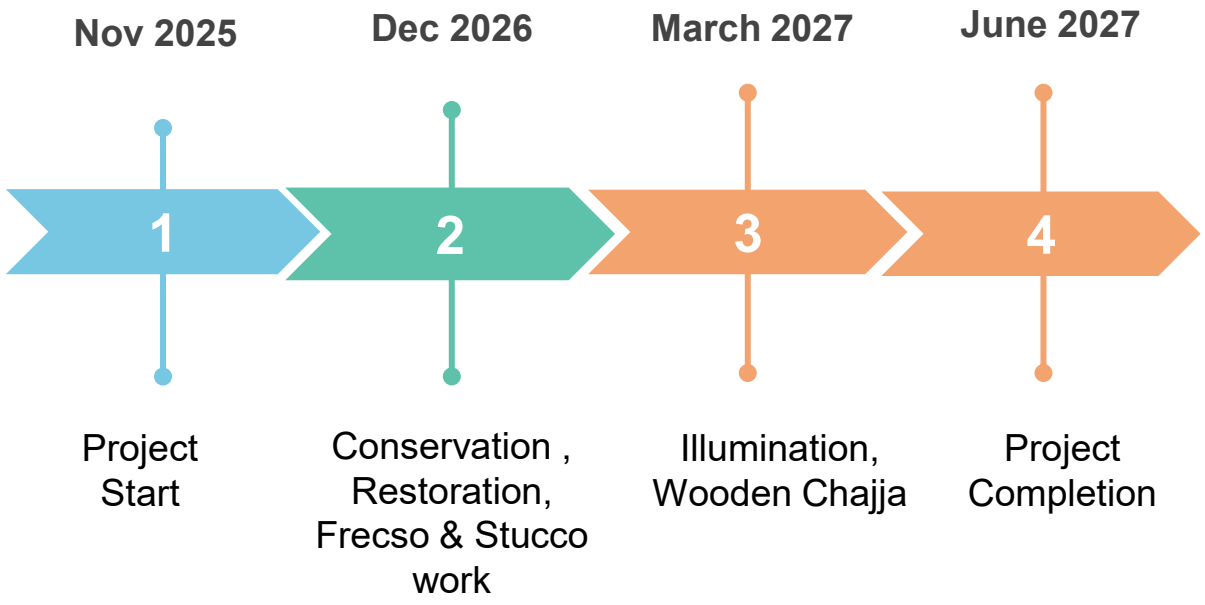

Project Start Date: **01 Jul 2024**
Completion Date by PC1: **June 2027**
Completion Date by TAM: **30 Jun 2027**

Next 30 Days Plans:

- Completion of furniture work.
- Completion of restoration of wood work.

Components of the Project

Component Name	Physical Progress	Expected Completion	Status
Structural Stabilization	70 %	31-10-2026	On Track
Restoration of Floors	90 %	30-09-2026	On Track
Ornamental Stucco Work	80%	31-10-2026	On Track
Ornamental Fresco Work	70 %	31-10-2026	On Track
Wooden Tarseem Bandi	90 %	15-09-2026	On Track
Ornamental Ceiling Work	90 %	15-09-2026	On Track
Furniture	Tender in process	31-11-2026	On Track
Illumination	Tender in process	30-10-2026	Delayed
Restoration of Wood Work (Doors and Jharoka)	90 %	30-12-2026	On Track
Development work	Tender in process	30-06-2027	Delayed

● = On Trac
● = Delayed
● = Critical

UMAR HAYAT MAHAL

1972 picture

UMAR HAYAT MAHAL

Physical Progress: 20%
Completion date: 30-06-2027

Amenity Area

Current

UMAR HAYAT MAHAL

Restoration of Wood Work Doors

Physical Progress: 80 %
Completion date: 30-10-2026

Before

Current

UMAR HAYAT MAHAL

Restoration of Wood Work Doors

Physical Progress: 90 %
Completion date: 30-09-2026

Before

Work in Progress

UMAR HAYAT MAHAL

Structural Stabilization

Physical Progress: 15 %
Completion date: 30-09-2026

Before

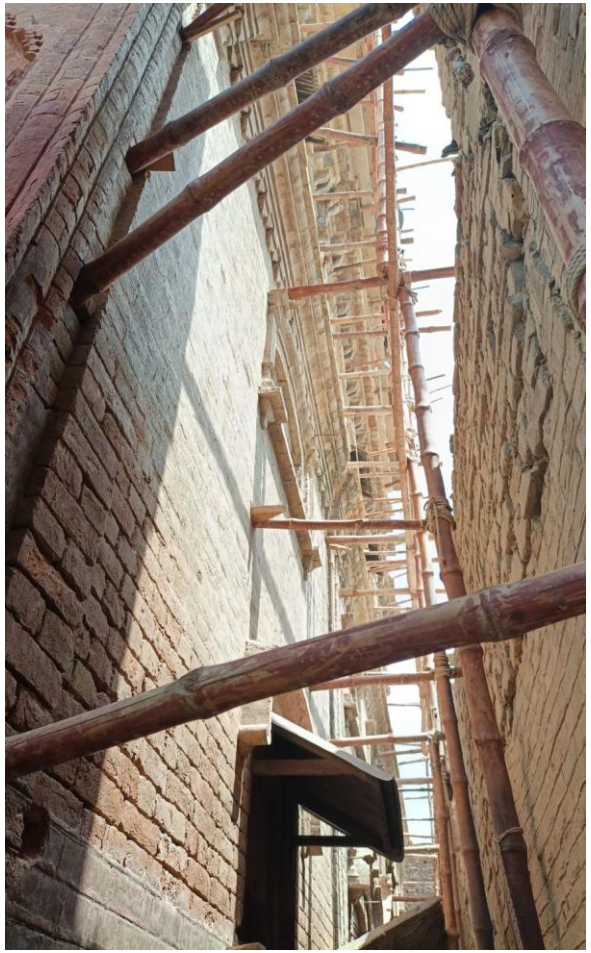

Work in Progress

UMAR HAYAT MAHAL

Stabilization of front Jahroka

Physical Progress: 90 %
Completion date: 30-09-2026

Before

Work in Progress

UMAR HAYAT MAHAL

Restoration of Wood Work Doors Jahroka

Physical Progress: 90 %
Completion date: 30-09-2026

Before

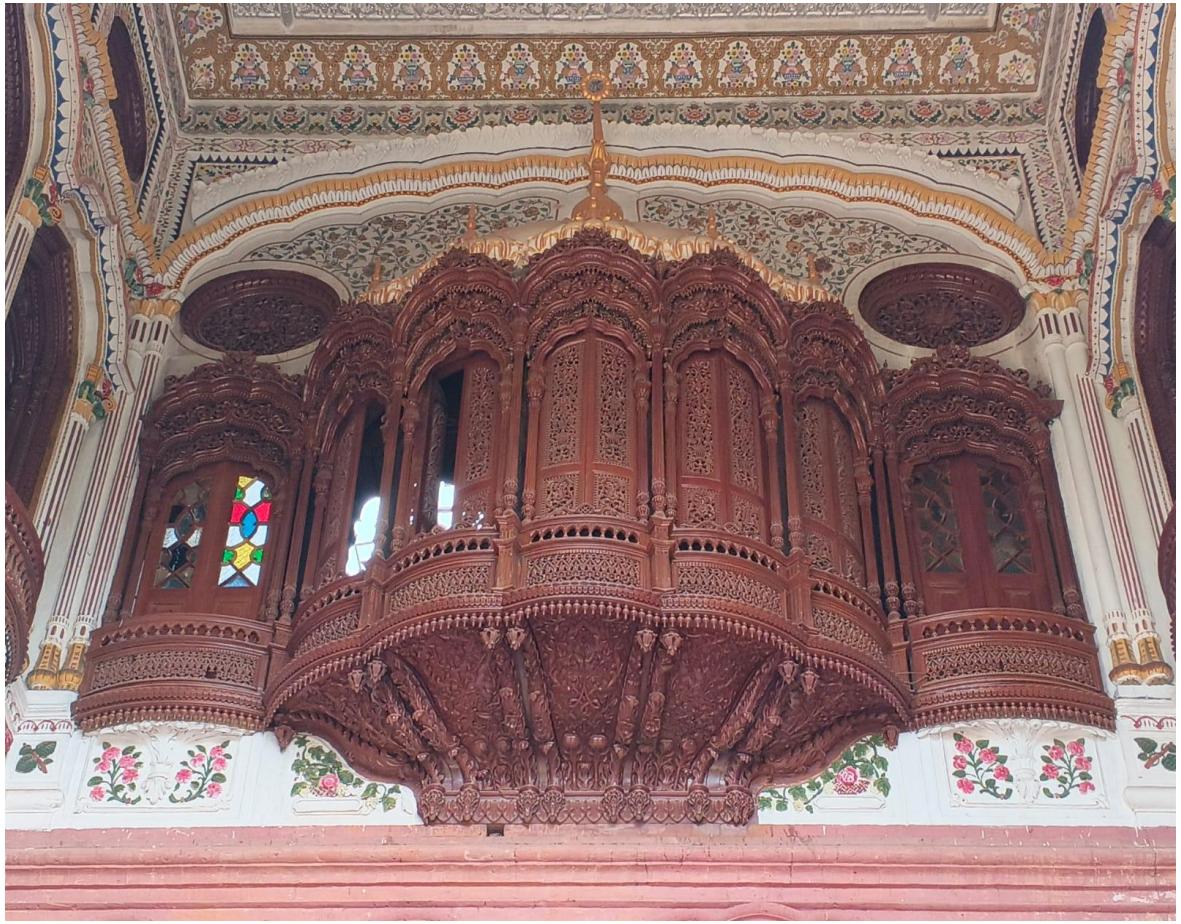

After

UMAR HAYAT MAHAL

Restoration of Iron Grill

Physical Progress: 90 %
Completion date: 30-09-2026

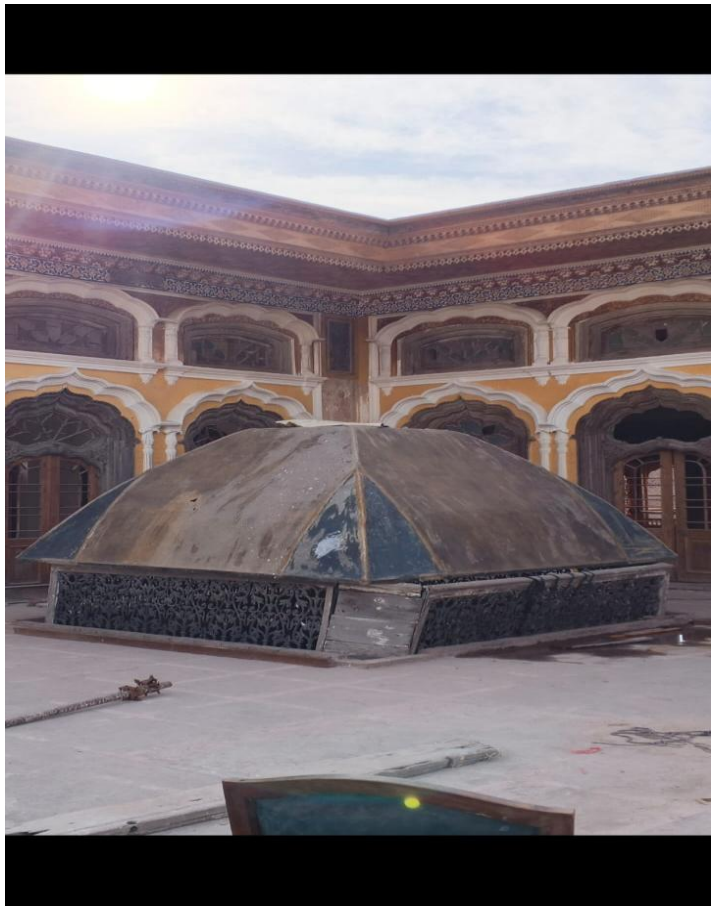

Before

After

UMAR HAYAT MAHAL

Wooden jhalar

Physical Progress: 90 %
Completion date: 30-09-2026

Before

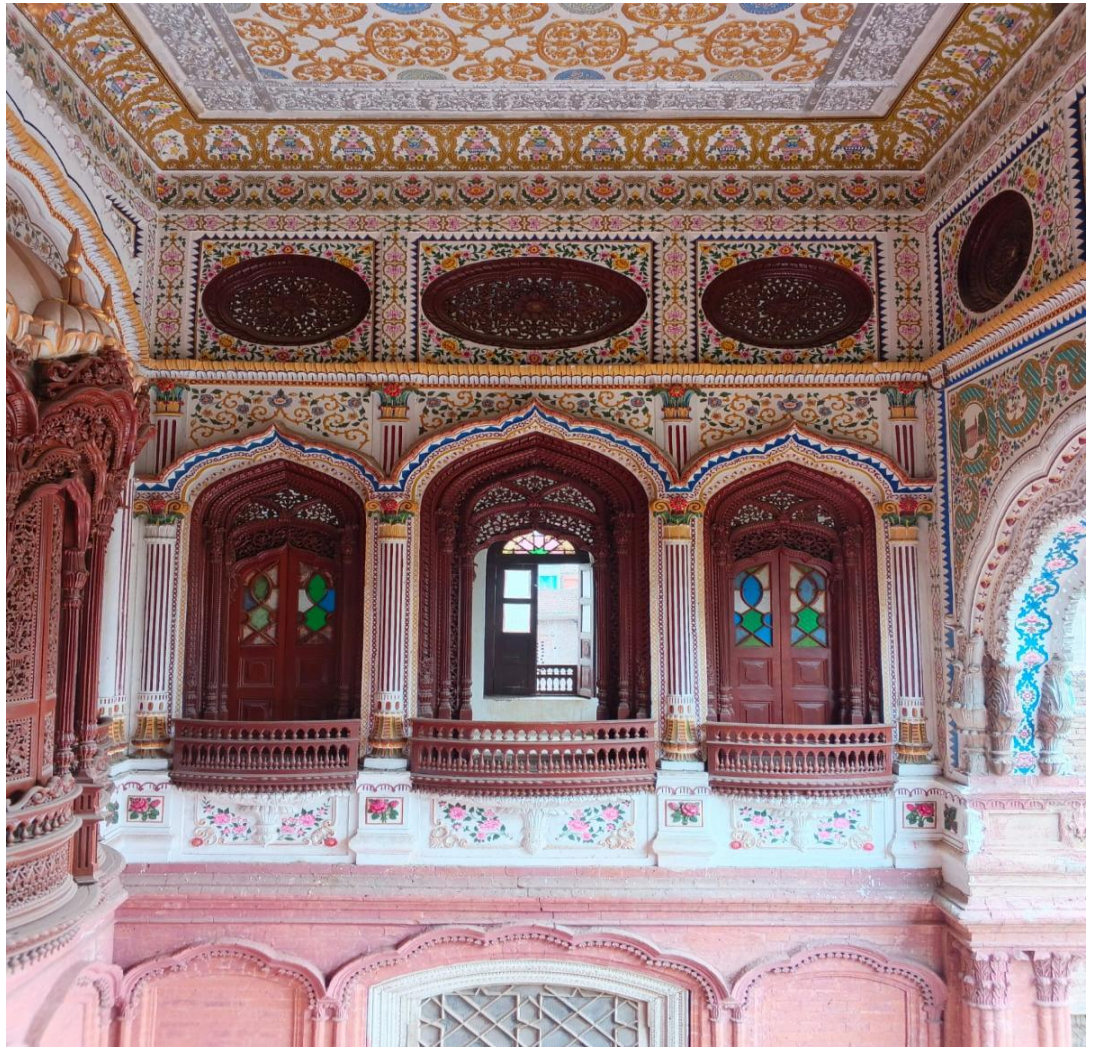

After

UMAR HAYAT MAHAL

Physical Progress: 80 %
Completion date: 31-10-2026

Ornamental Stucco Work

Before

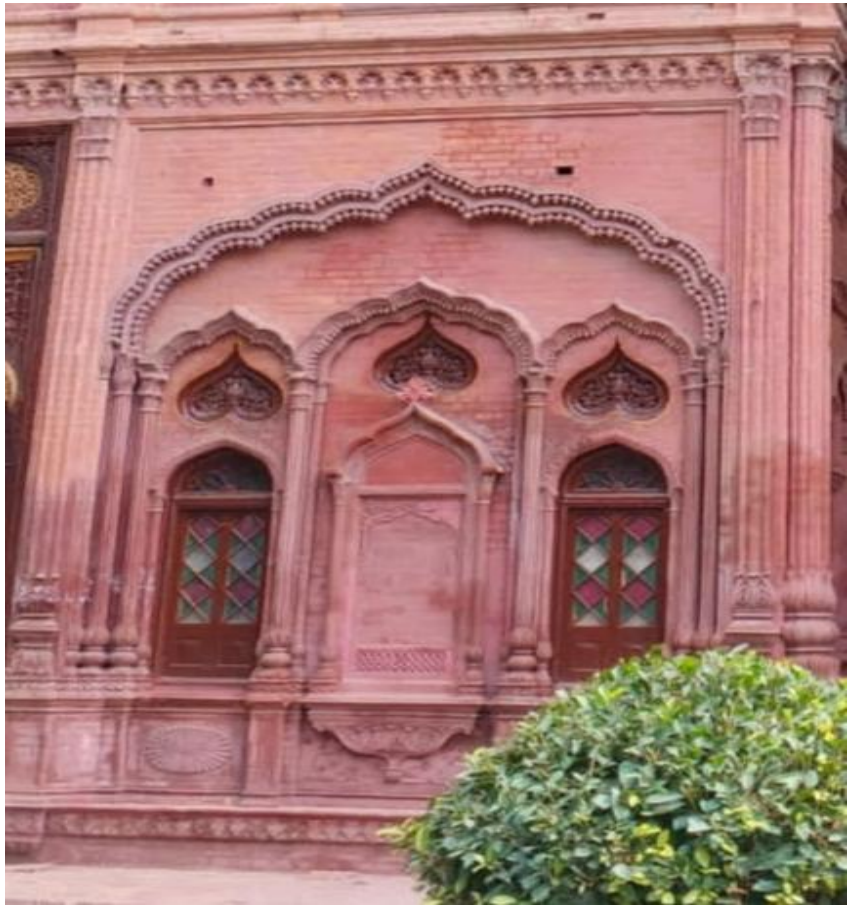

Current

UMAR HAYAT MAHAL

Wood , fresco , stucco work

Physical Progress: 90 %
Completion date: 30-09-2026

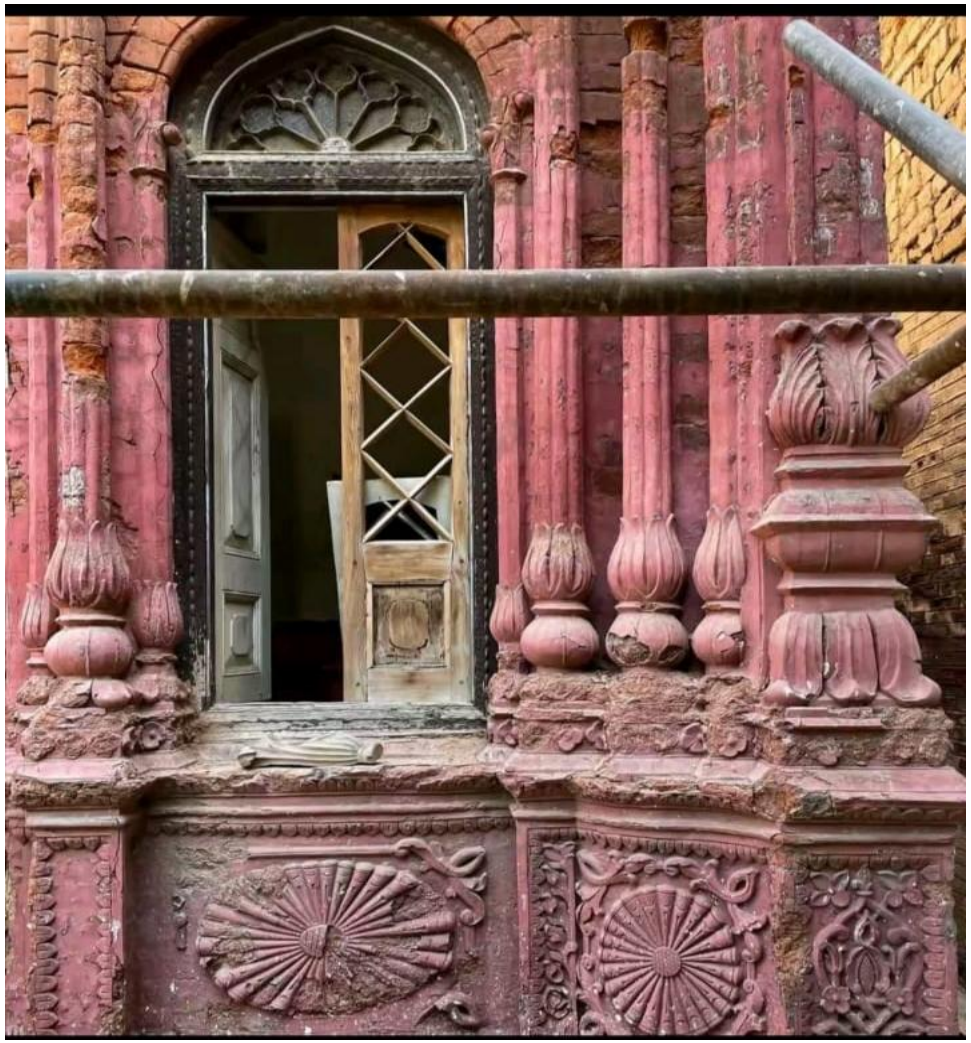

Before

After

UMAR HAYAT MAHAL

Physical Progress: 90 %
Completion date: 30-09-2026

Ornamental Ceiling, Stucco and Fresco Work

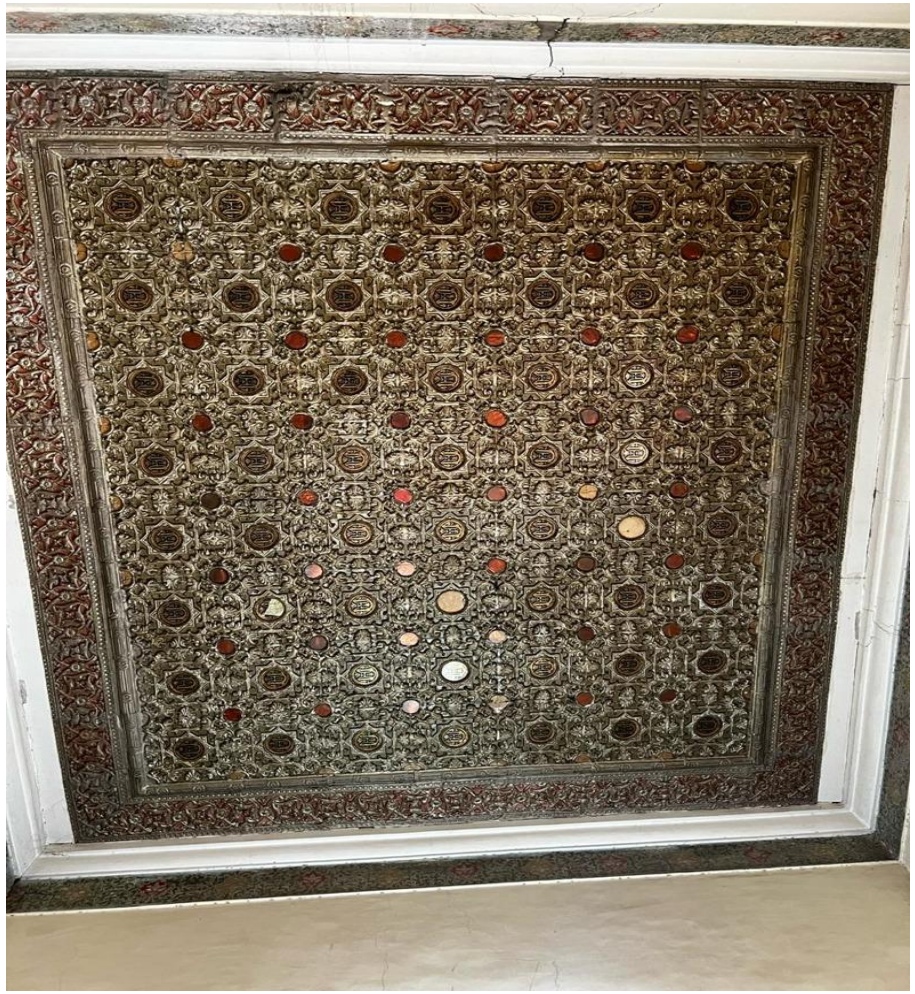

Before

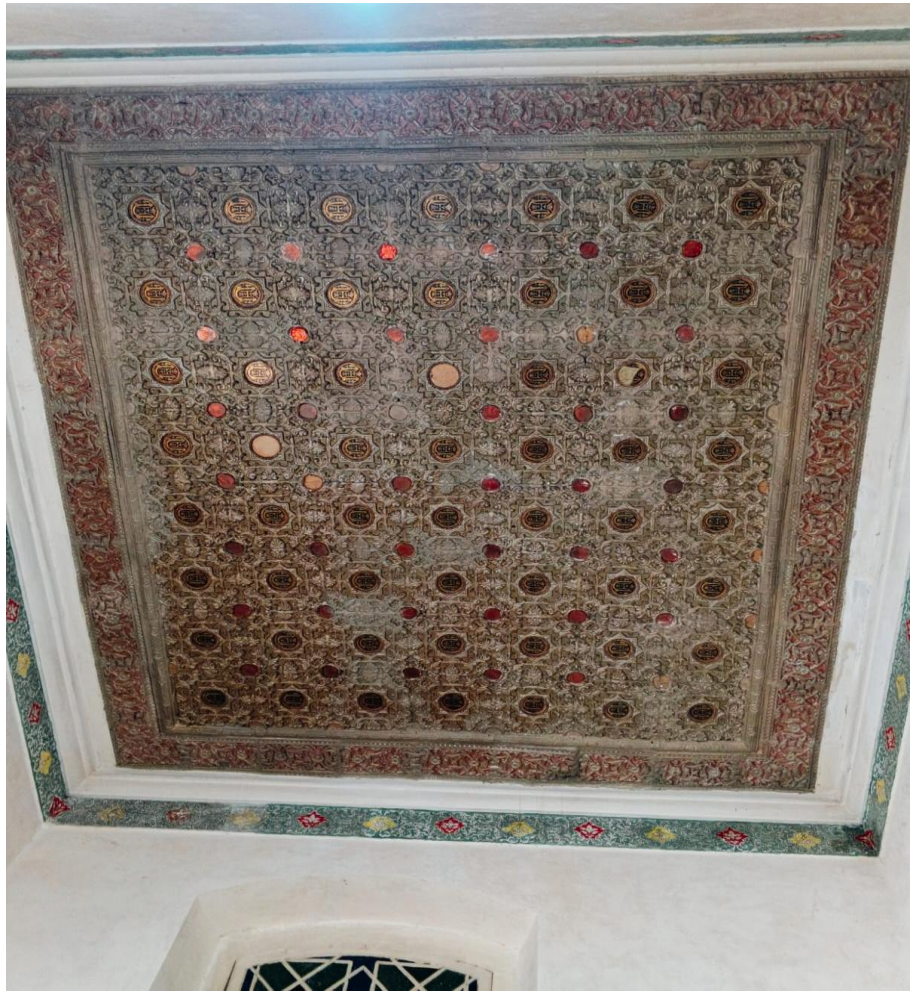

After

UMAR HAYAT MAHAL

Structure Stabilization

Physical Progress: 70 %
Completion date: 31-10-2026

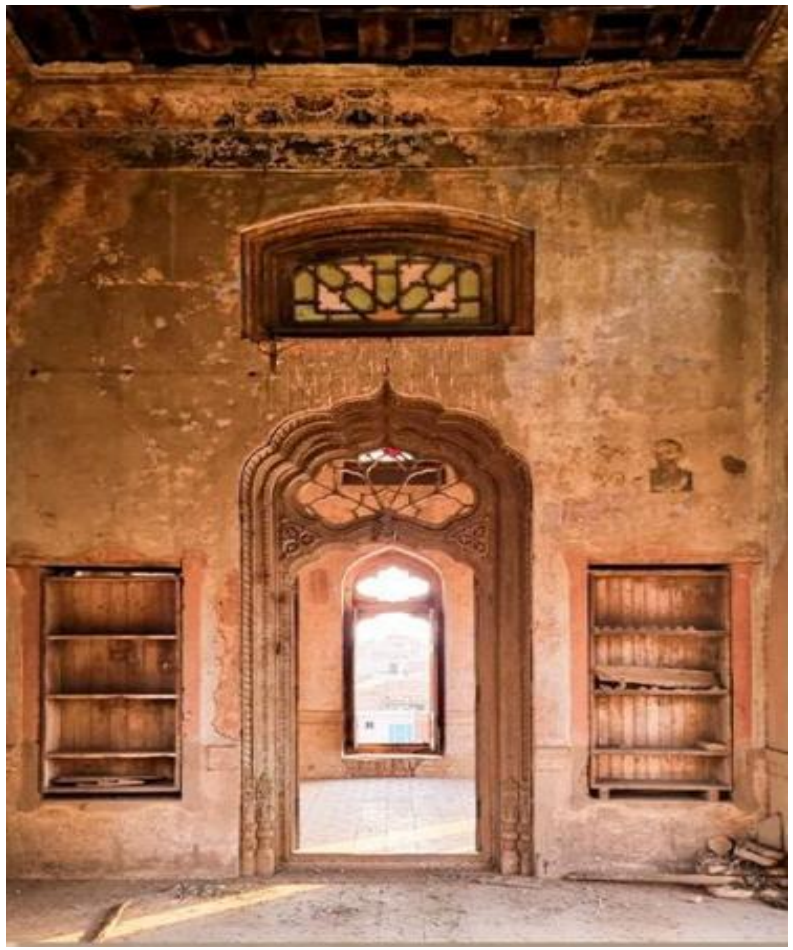

Before

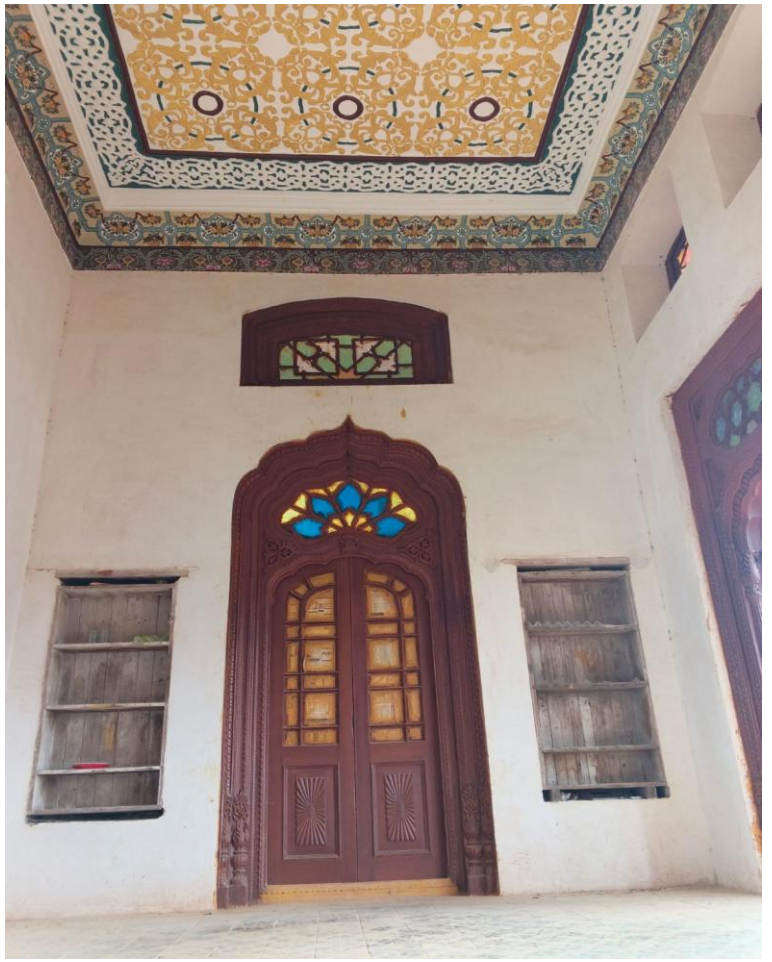

After

UMAR HAYAT MAHAL

Ornamental Stucco & Fresco Work

Physical Progress: 70 %
Completion date: 31-10-2026

Before

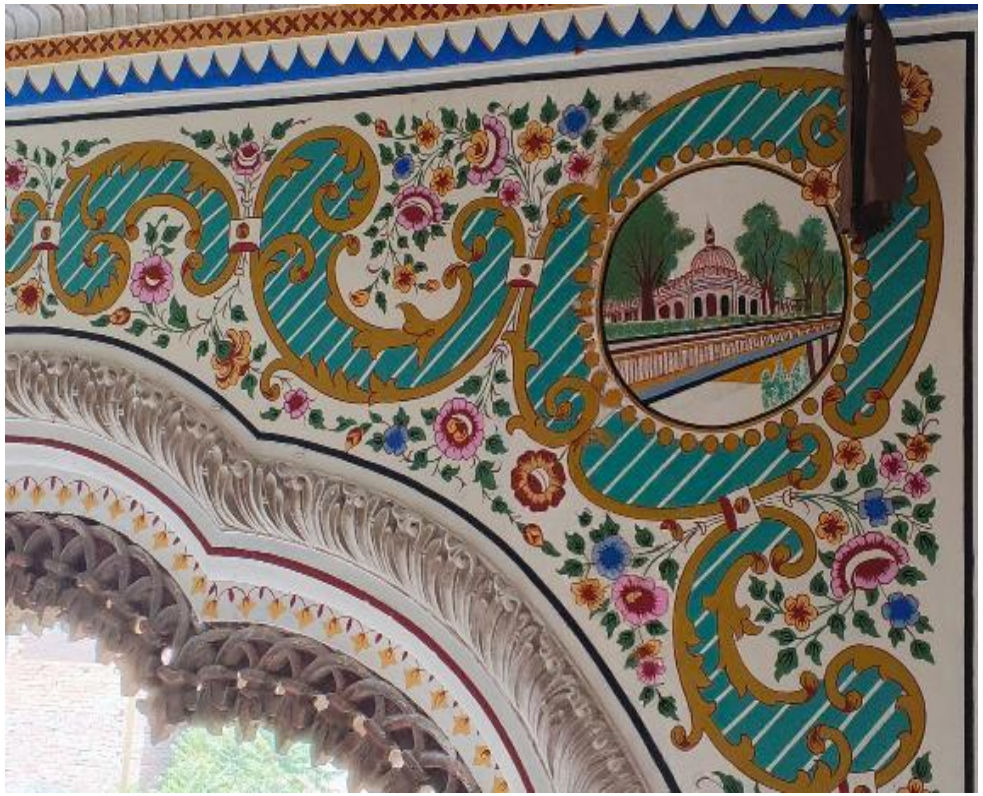

After

UMAR HAYAT MAHAL

Ornamental Wood Work

Physical Progress: 80 %
Completion date: 31-10-2026

Before

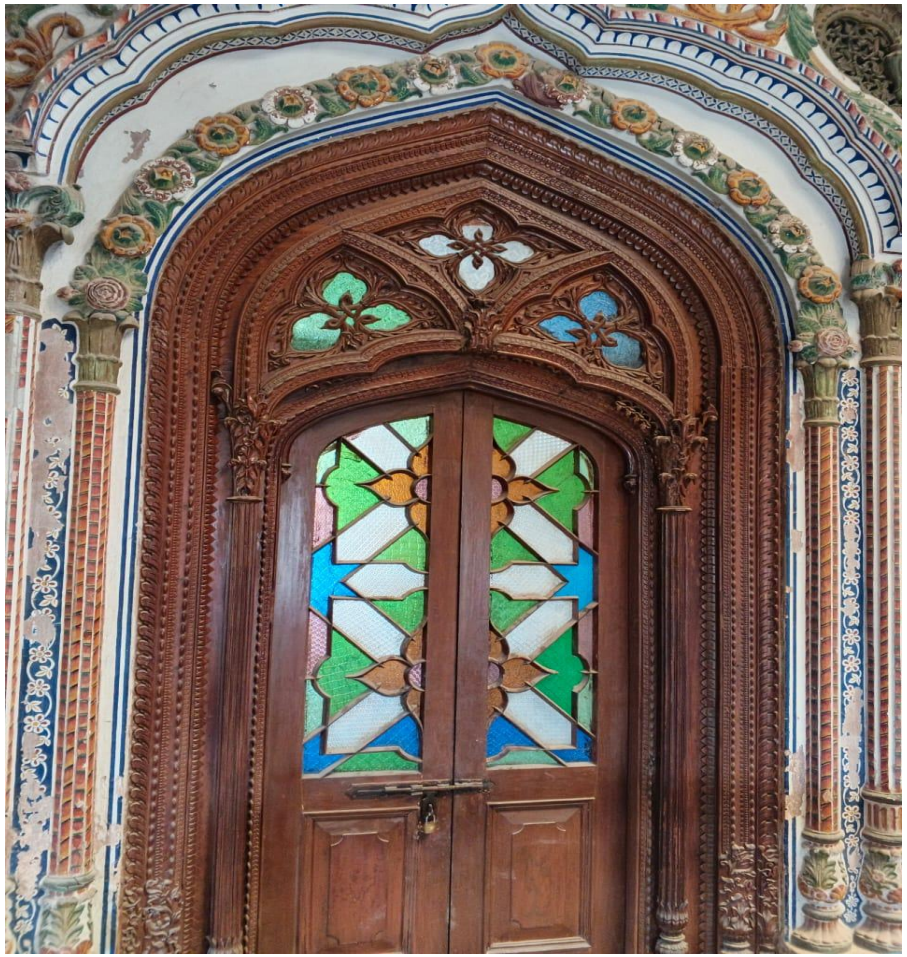

Work in Progress

UMAR HAYAT MAHAL

Ornamental Wood Work

Physical Progress: 80 %
Completion date: 31-10-2026

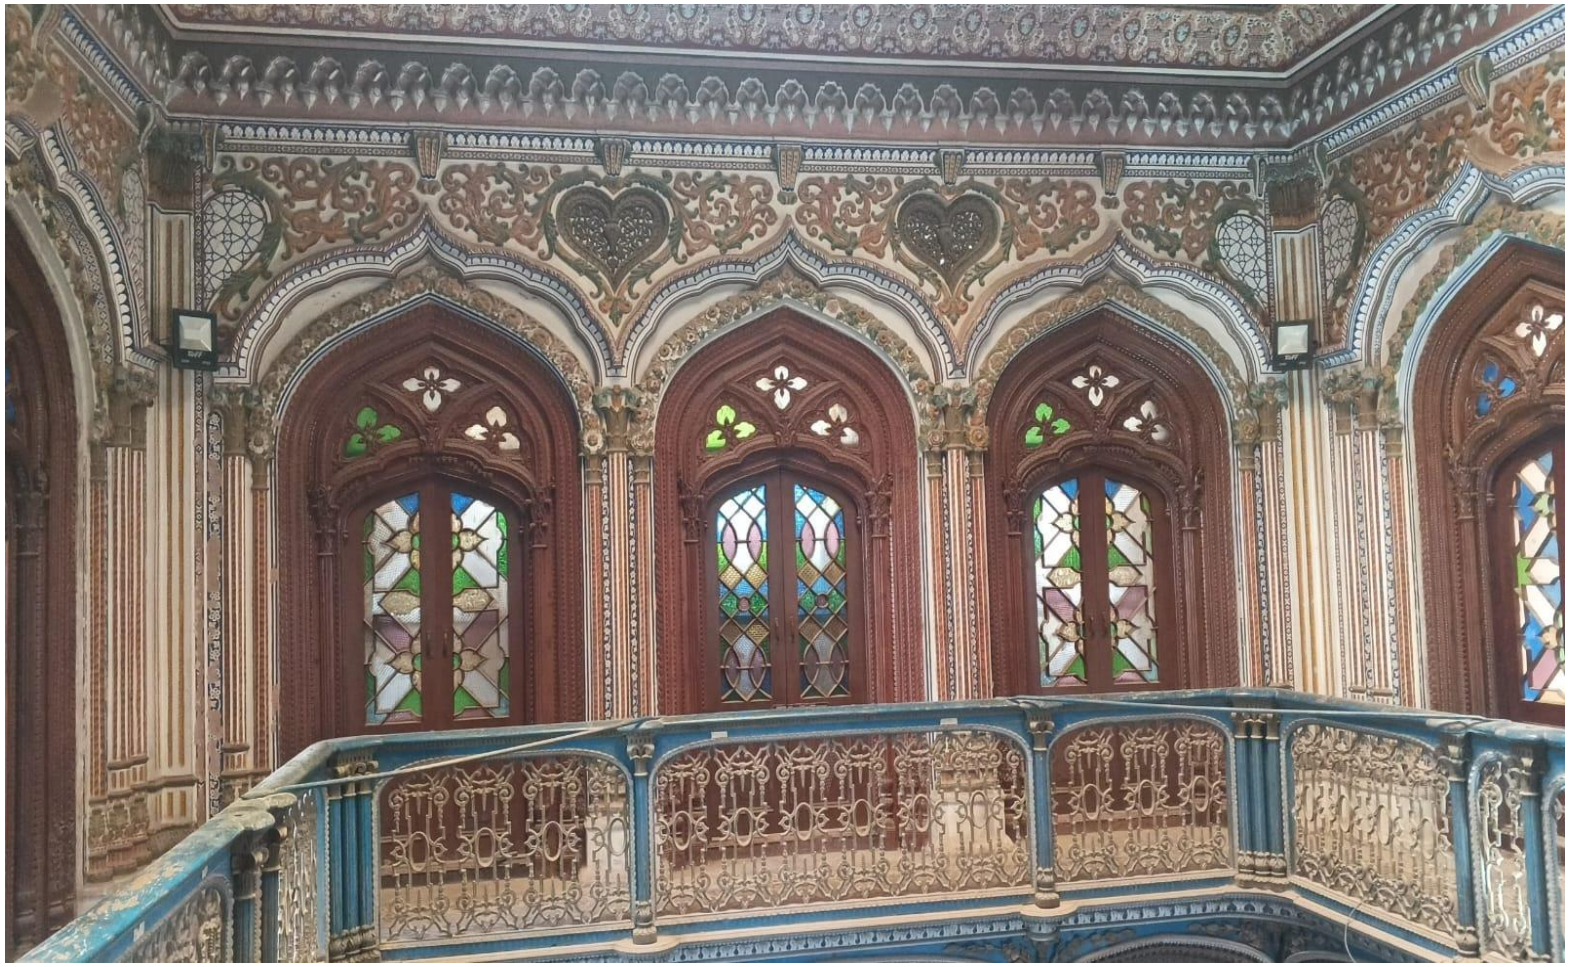

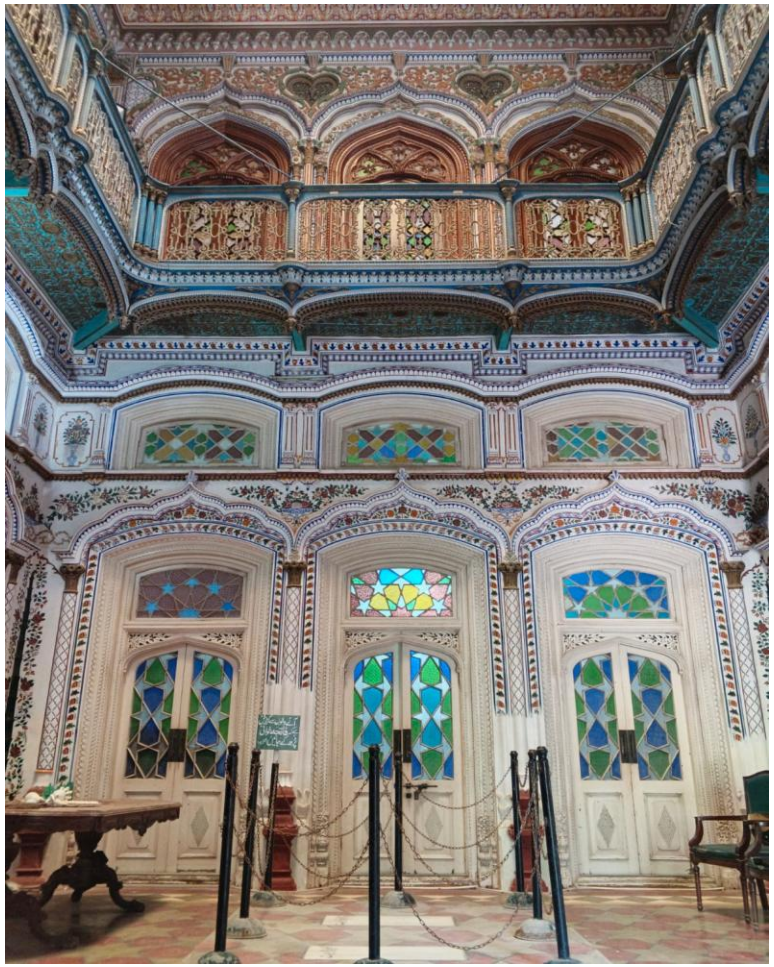

Work in Progress

UMAR HAYAT MAHAL

Ornamental Ceiling, Stucco and Fresco Work

Physical Progress: 80 %
Completion date: 15-09-2026

Before

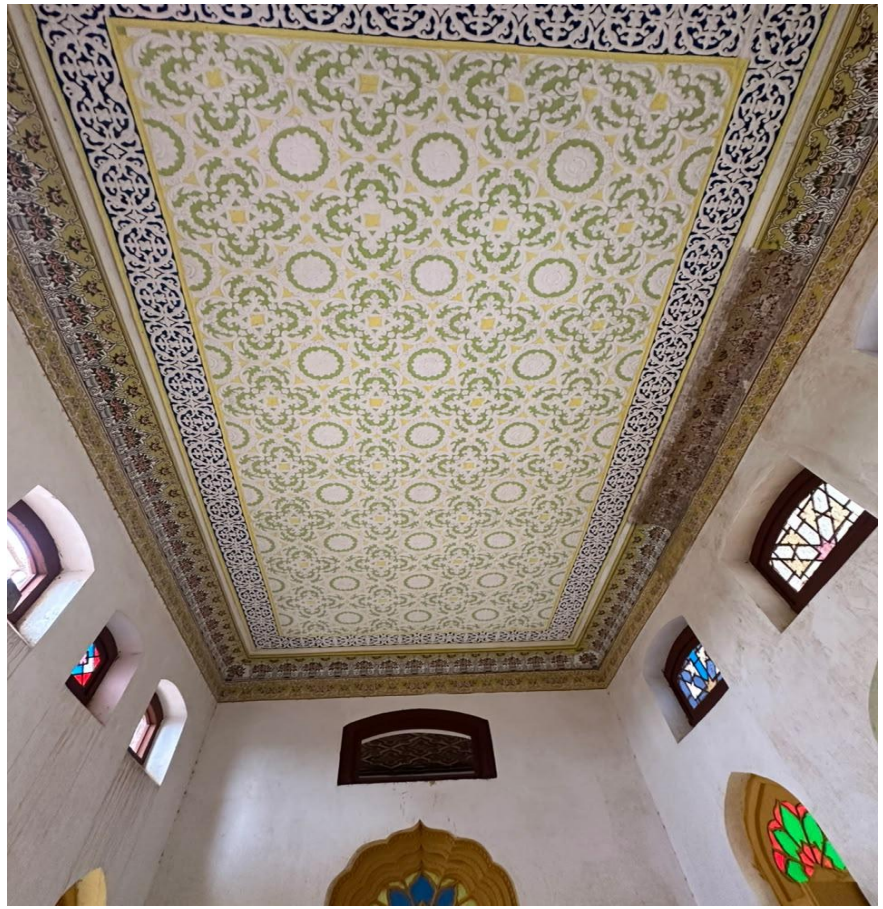

Completed

UMAR HAYAT MAHAL

Physical Progress: 80 %
Completion date: 15-09-2026

Wooden Terseem Bandi

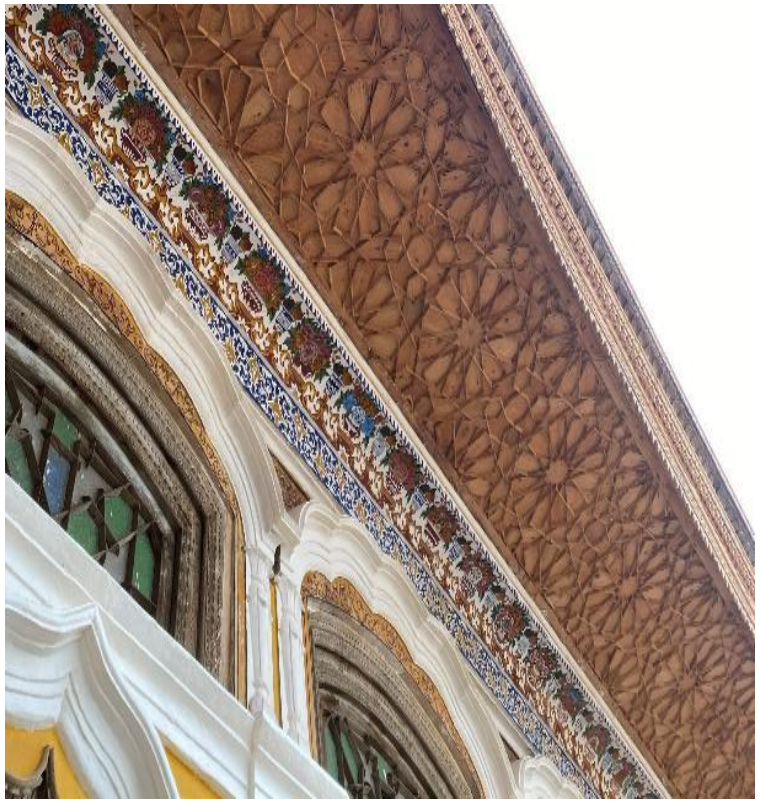

Before

After

UMAR HAYAT MAHAL

Wood , Glass , Stucco and Fresco Work

Physical Progress: 80 %
Completion date: 31-10-2026

Before

After

UMAR HAYAT MAHAL

Physical Progress: 80 %
Completion date: 31-10-2026

Wood , Glass , Stucco and Fresco Work

Before

Current

UMAR HAYAT MAHAL

Restoration of Floors

Physical Progress: 90 %
Completion date: 30-09-2026

Current

UMAR HAYAT MAHAL

Top roof

Physical Progress: 75%
Completion date: Delyed

Before

After

UMAR HAYAT MAHAL

Wood work Glass work

Completion date: Delyed

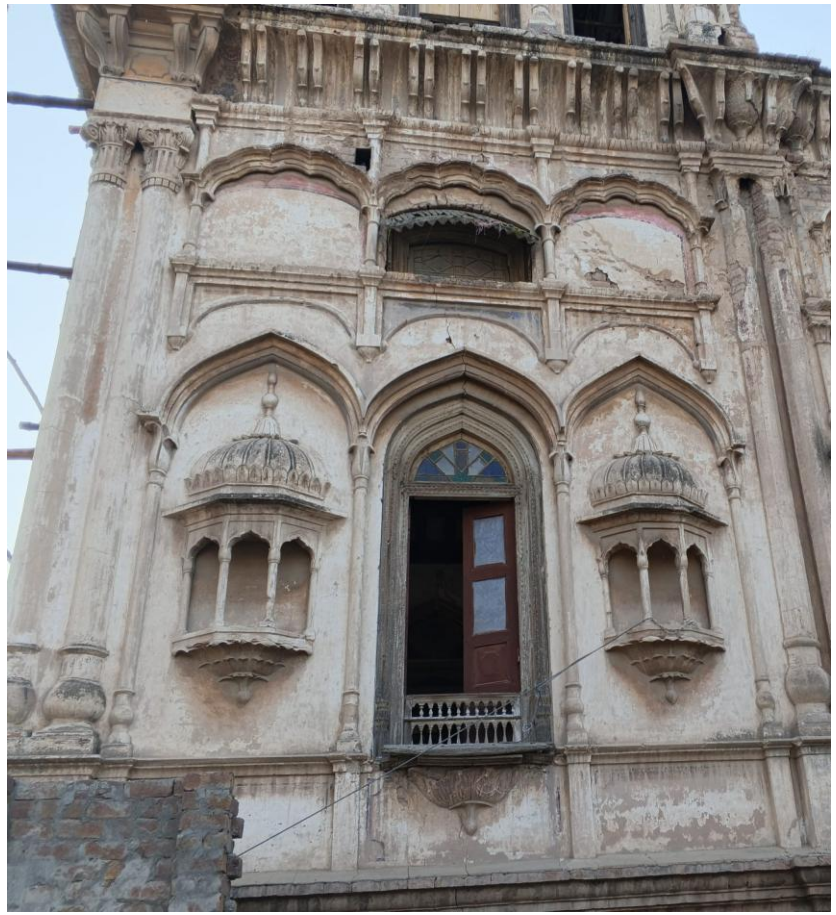

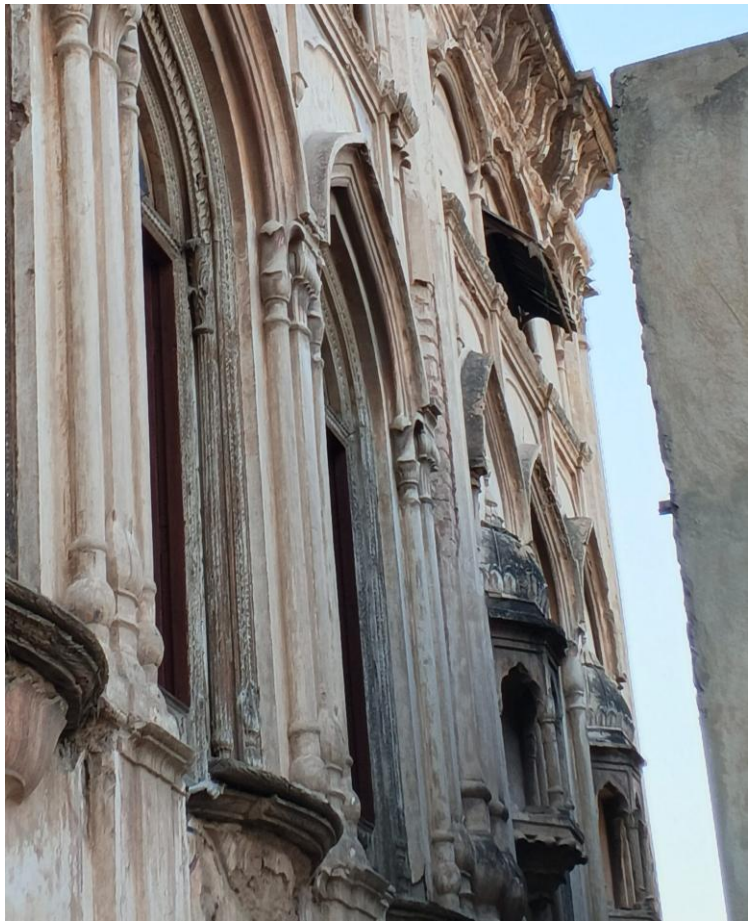

Current

Project Status & Reasons for Delay

- **Tenders in process**

1. development work
2. furniture
3. illumination

Site Focal Person	Phone Number
Tehreem Baber	03364270349

Heritage Conservation of Old Town Bhera for the Promotion of Tourism

Responsibility: TAM / TDCP
Cost: PKR **737.631** million

Physical Progress	45%
Financial Progress	6 %
Allocation (2026-27)	20 Million
Additional Funds Demand	250 Million

Scope of work
Conservation, restoration and rehabilitation of: 1. Sher Shah Suri Mosque 2. Historic Gates 3. Railway Station 4. Irrigation Resthouse 5. Bauli Mandir

Progress so far
Conservation, restoration and rehabilitation of: 1. Sher Shah Suri Mosque: 50% completed 2. Historic Gates: 2 out of 6 gates are 80% completed 3. Railway Station: 45% completed 4. Irrigation Resthouse:60% completed 5. Mandir:35% completed

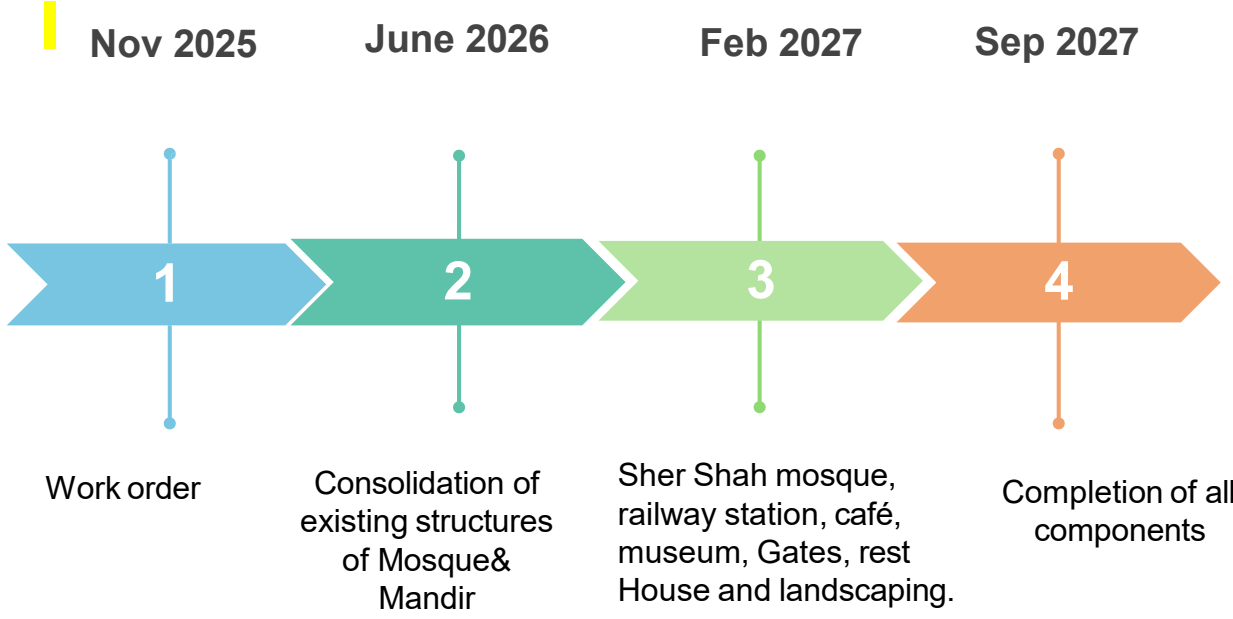

Project Start Date:	20 Oct 2025
Completion Date As Per PC1:	30 Jun 2027
Completion Date As Per TAM:	30 Sep 2027

Next 30 Days Plans:

- Continuation of Work on Lahori & Kashmiri Gate and Irrigation rest House Revamping
- Mosque Plaster Work and Railway Station Museum & Cafe

Back

Components of the Project-Bhera Railway Station

Component	Progress	Completion	Status
Removal of Cement	100%	Completed	On Track
Consolidation of existing structures	100 %	Completed	On Track
Conservation of existing structures	70%	31-08-2026	On Track
Earth Filling	50%	31-08-2026	On Track
Boundary Wall	20%	31-12-2026	On Track
Museum & Cafeteria	40%	30-01-2027	On Track
Illumination / Electrification	--	28-02-2027	On Track
Land scaping and External Development	--	31-03-2027	On Track
Kids Play Area	--	31-03-2027	On Track

● = On Track
● = Delayed
● = Critical

Components of the Project-Sher Shah Suri Mosque

Component	Progress	Completion	Status
Removal of Cement	100%	Completed	On Track
Consolidation of existing structures	100%	Completed	On Track
Water Proofing	100%	Completed	On Track
Restoration of Architectural Features	100%	Completed	On Track
Removal of structures	100%	30-09-2027	On Track
Electricity & Plumbing Work	20%	30-11-2026	On Track
Conservation of existing structures	60%	31-12-2026	On Track
Ablution Area and Residences	--	31-12-2026	On Track
Remodeling of conference hall	--	28-02-2027	On Track
Relocation of museum	--	28-02-2027	On Track
Landscaping	--	31-03-2027	On Track

● = On Track
● = Delayed
● = Critical

Components of the Project-Mandir Bhera

Component	Progress	Completion	Status
Consolidation of existing structures	100%	Completed	On Track
Conservation of existing structures	30%	31-03-2027	On Track
Boundary Wall	--	28-02-2027	On Track
Landscaping	--	31-03-2027	On Track
Parking Area	--	31-03-2027	On Track
Security Office	--	31-03-2027	On Track
Electricity & Illumination	--	31-03-2027	On Track

● = **On Track**
● = **Delayed**
● = **Critical**

Components of the Project-Irrigation Rest House

Component	Progress	Completion	Status
Removal of Cement	100%	Completed	On Track
Consolidation of existing structures	100%	Completed	On Track
Removal of Paint	100%	Completed	On Track
Conservation of existing structures	60%	31-12-2026	On Track
Flooring	--	31-12-2026	On Track
Electricity and Plumbing	30%	31-01-2027	On Track
Kankar lime Plaster	20%	31-03-2027	On Track
Boundary Wall	30%	31-03-2027	On Track
Landscape and External Development	--	31-03-2027	On Track

● = **On Track**
● = **Delayed**
● = **Critical**

Components of the Project-Historical Gates

Component	Progress	Completion	Status
1.Lahori Gate			
Removal of Cement	100%	Completed	On Track
Consolidation of existing structures	85 %	Completed	On Track
Removal of alien architecture features	100%	Completed	On Track
Conservation of existing structures	100%	30-10-2026	On Track
Shifting of Electrical Pole	--	30-10-2026	On Track
Illumination	--	30-10-2026	On Track

● = On Track
● = Delayed
● = Critical

Components of the Project-Historical Gates

2. Kashmiri Gate			
Removal of Cement	100%	Completed	On Track
Consolidation of existing structures	80%	Completed	On Track
Conservation of existing structures	80%	Completed	On Track
Removal of alien architecture features	80%	Completed	On Track
Illumination		30-10-2026	On Track

● = **On Track**
● = **Delayed**
● = **Critical**

Components of the Project-Historical Gates

Component	Progress	Completion	Status
3. Chinioti Gate			
Removal of Cement	--	30-09-2027	Delayed
Consolidation of existing structures	--	30-09-2027	Delayed
Conservation of existing structures	--	30-09-2027	Delayed
Removal of alien architecture features	--	30-09-2027	Delayed
Illumination		30-09-2027	Delayed

● = On Track
● = Delayed
● = Critical

Components of the Project-Historical Gates

4. Kabli Gate			
Removal of Cement	--	30-09-2027	Delayed
Consolidation of existing structures	--	30-09-2027	Delayed
Removal of alien architecture features	--	30-09-2027	Delayed
Illumination	--	30-09-2027	Delayed

● = On Track
● = Delayed
● = Critical

Components of the Project-Historical Gates

Component	Progress	Completion	Status
5. Multani Gate			
Removal of Cement	--	30-09-2027	Delayed
Consolidation of existing structures	--	30-09-2027	Delayed
Conservation of existing structures	--	30-09-2027	Delayed
Removal of alien architecture features	--	30-09-2027	Delayed
Illumination	--	30-09-2027	Delayed
6. Lahori Gate			
Removal of Cement	--	30-09-2027	Delayed
Consolidation of existing structures	--	30-09-2027	Delayed
Conservation of existing structures	--	30-09-2027	Delayed
Removal of alien architecture features	--	30-09-2027	Delayed
Illumination	--	30-09-2027	Delayed

● = On Track
● = Delayed
● = Critical

Heritage Conservation of Old Town Bhera for the Promotion of Tourism

Sher Shah Suri Mosque



Heritage Conservation of Old Town Bhera for the Promotion of Tourism

Conservation of Lahori Gate

Physical progress: 70%
Completion: 30.10.2026

Before

Work in Progress

Heritage Conservation of Old Town Bhera for the Promotion of Tourism

Conservation of Kashmiri Gate

Physical progress: 60%
Completion: 30.10.2026

Before

Work in Progress

Heritage Conservation of Old Town Bhera for the Promotion of Tourism

Conservation of Mandir

Physical progress: 40%
Completion Date: 31-03-2027

Work in Progress

Heritage Conservation of Old Town Bhera for the Promotion of Tourism

Drone Video

Heritage Conservation of Old Town Bhera for the Promotion of Tourism

Conservation of Irrigation Rest House

Physical progress:25%
Completion: 31.03.2027

3D Render

Work in Progress

Heritage Conservation of Old Town Bhera for the Promotion of Tourism

Conservation of Irrigation Rest House

Physical progress:25%
Completion: 31.03.2027

Before

Work in Progress

Heritage Conservation of Old Town Bhera for the Promotion of Tourism

Railway Station Bhera

Back

MOUJ GARH FORT

Responsibility: TAM / Archaeology
Cost: PKR **798.25** million

Physical Progress	25%
Financial Progress	15%
Allocation (2026-27)	30 Million
Additional Funds Demand	250 Million

Scope of work
1. Archaeological Excavation 2. Consolidation of existing special size Sun dried masonry 3. Conservation and Preservation of Fortification Walls Bastions 4. Conservation of entrance gateway 5. External Development, public Facilities, landscape and illumination

Progress SO far
1. Eastern Fortification Wall & Corner Bastions — 15% 2. Northern Fortification Wall & Northwest Bastions — 20% 3. Southern Fortification Wall & Southwest Bastions — 27%

Project Start Date:	**01 Jul 2025**
Completion Date As Per PC1:	**30 Jun 2028**
Completion Date As Per TAM:	**31 Dec 2027**

Next 30 Days Plans:

- Preparation of Sun Dried bricks
- Underpinning work of fortification walls

Back

Components of the Project

Component Name	Physical Progress	Expected Completion	Status
Conservation and Preservation of: • Eastern Fortification Wall • Northeast Corner Bastion • Southeast Corner Bastions	15%	30-03-2027	On Track
Conservation and Preservation of: • Northern Fortification Wall • Northwest Corner Bastions	20%	30-03-2027	On Track
Conservation and Preservation of: • Southern Fortification Wall • Southwest Corner Bastions	27%	30-03-2027	On Track
Exterior/Finishing Work and Illumination	---	30-12-2027	On Track

= On Track
= Delayed
= Critical

Mouj Garh Fort

Conservation of Fortification wall and Bastion

Physical Progress: 21%
Date Completed: 30-12-27

Before

Work in Progress

Mouj Garh Fort

Conservation of Fortification wall and Bastion

Physical Progress: 21%
Date Completed: 30-12-27

Before

Work in Progress

Mouj Garh Fort

Conservation of Fortification wall and Bastion

Physical Progress: 21%
Date Completed: 30-12-27

Before

Work in Progress

Mouj Garh Fort

Conservation of Fortification wall and Bastion

Physical Progress: 21%
Date Completed: 30-12-27

Before

Work in Progress

Mouj Garh Fort

Conservation of Fortification wall

Physical Progress: 21%
Date Completed: 30-12-27

Before

Work in Progress

Mouj Garh Fort

Currently work

Mouj Garh Fort

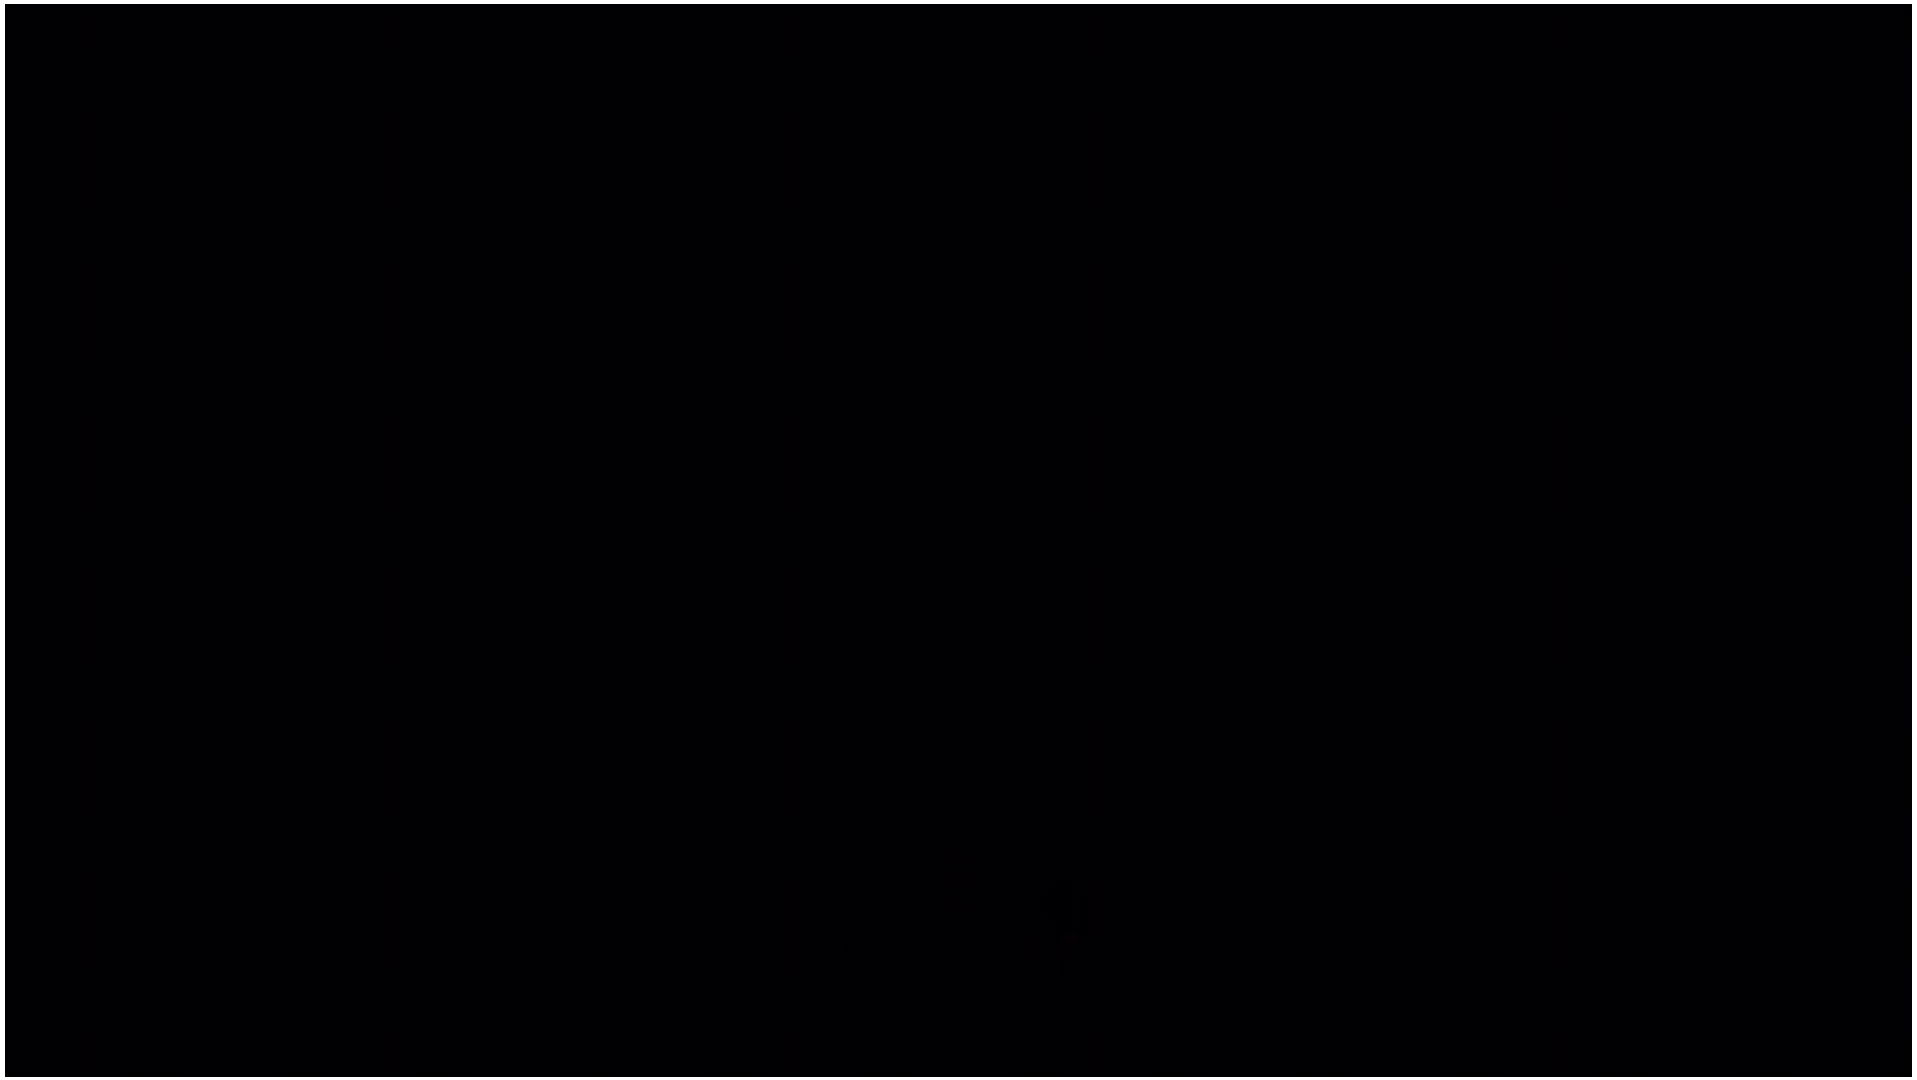

Showcase Video

Mouj Garh Fort (09-Aug-2026)

Back

Conservation and Preservation of Din Garh Fort, District Bahawalpur

Responsibility: TAM / ARCHAEOLOGY
Cost: PKR **618.848** million

Physical Progress	31%
Financial Progress	20%
Allocation (2026-27)	30 Million
Additional Funds Demand	300 Million

Scope of work

1. Conservation of Fortification walls and Bastions of the Fort
2. Conservation of Entrance gateway
3. External Development, landscape and Illumination

Progress so far

1. Conservation of Fortification Wall and Bastion of the Fort — 30%
2. Conservation of Entrance Gateway — 35%

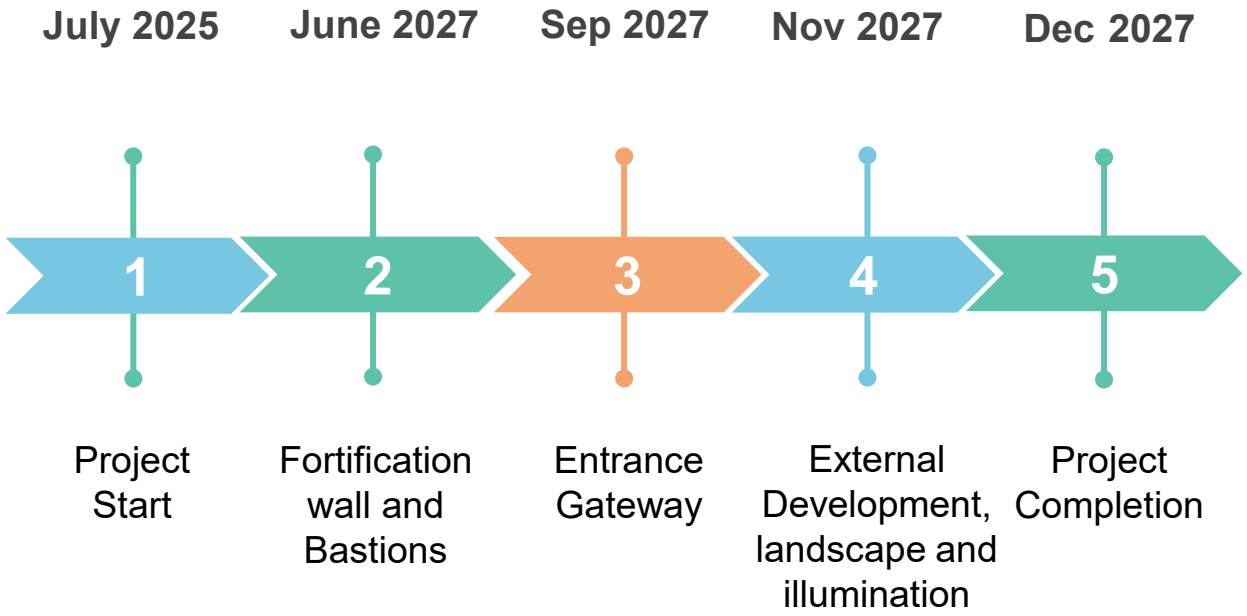

Project Start Date:	**01 July 2025**
Completion Date by PC1:	**30 June 2028**
Completion Date by TAM:	30 December 2027

Next 30 Days Plans:

- Preparation of Sun Dried bricks
- Underpinning work on fortification walls, bastions and gateway.

Components of the Project

Component Name	Physical Progress	Expected Completion	Status
Conservation of Fortification wall and Bastion of the Fort	30%	30-06-2027	On Track
Conservation of Entrance gateway	35%	30-09-2027	On Track
External Development, landscape and Illumination	---	30-09-2027	On Track

= On Trac
= Delayed
= Critical

Din Garh Fort

Conservation of Fortification wall and Bastions

Physical Progress: 30%
Completion date: 30-06-2027

Before

Work in Progress

Din Garh Fort

Physical Progress: 30%
Completion date: 30-09-2027

Conservation of Fortification wall and Entrance Gateway

Before

Work in Progress

Din Garh Fort

Conservation of Fortification wall

Physical Progress: 30%
Completion date: 30-06-2027

Before

Work in Progress

Din Garh Fort

Back

Preservation, Restoration, Improvement, Management and Upgradation of Harappa Archaeological Park

Presented by Hassan

5.Preservation, Restoration, Improvement, Management and Upgradation of Harappa Archaeological Park

Responsibility: TAM / ARCHAEOLOGY
Cost: PKR **1,429.0** million

Scope of Work
1. Conservation of Rest House
2. Conservation of Old Museum & Conversion into Cafeteria
3. Conversion of Existing Canteen into Haddaba
4. Remodelling of Auditorium
5. Construction of Living History Village
6. Harmonisation of Façade – Museum Complex
7. Construction of Parking
8. Conservation of Archaeological Ruins
9. Construction of One Window Facilitation Centre
10. The Citadel Hotel
11. Construction of Indus Valley Decipherment Centre

Progress So far
1. Conservation of Rest House — 98%
2. Conservation of Old Museum & Conversion into Cafeteria — 90%
3. Conversion of Existing Canteen into Haddaba — 75%
4. Remodeling of Auditorium — 80%
5. Construction of Living History Village — 50%
6. Harmonizing of Façade – Museum Complex — 30%
7. Construction of Parking — 35%
8. Conservation of Archaeological Ruins — 52%
9. Construction of One Window Facilitation Centre — 25%

Physical Progress	30%
Financial Progress	16%
Allocation (2026-27)	100 Million
Additional Funds Demand	400 Million

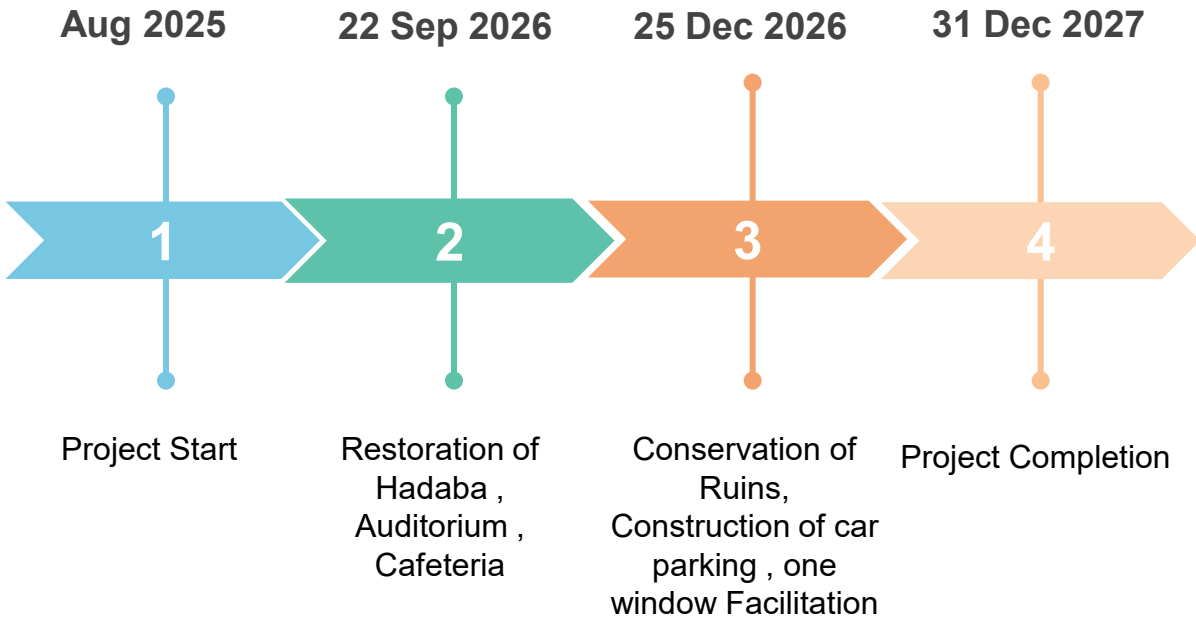

Project Start Date: 13 Aug 2025
Completion Date by PC1: 15 June 2028
Completion Date by TAM: 31 Dec 2027

Next 30 Days Plans:
1. Conservation of Old Museum & Conversion into Cafeteria
2. Conversion of Existing Canteen into Haddaba
3. Remodelling of Auditorium

Components of the Project

Component Name	Physical Progress	Expected Completion	Status
Conservation of Rest House	98 %	Completed	On Track
Conservation of Old Museum & Conversion into Cafeteria	90%	30-09-2026	On Track
Conversion of Existing Canteen into Haddaba	75%	30-09-2026	On Track
Remodelling of Auditorium	80%	30-09-2026	On Track
Construction of Living History Village	50%	30-10-2026	On Track
Harmonizing of Façade – Museum Complex	As per simulation 80%	30-06-2027	On Track
Construction of Parking	35%	30-06-2027	On Track
Conservation of Archaeological Ruins	52% Technical mistake	30-10-2026	Delayed
Construction of One Window Facilitation Centre	25%	30-06-2027	On Track
The Citidal Hotel	Relocation and design phase complete	20-01-2028	Delayed
Construction of Indus Valley Decipherment Center	Relocation and design phase complete	20-01-2028	Delayed

● = On Track
● = Delayed
● = Critical

Harappa Archaeological Park

Harmonisation of Façade – Booking Counter

Physical Progress: 98%
Completion date:30-06-2027

Before

After

Harappa Archaeological Park

Conservation

Physical Progress: 50%
Completion date:30-10-2026

Before

Current

Harappa Archaeological Park

Conservation work at Granary area

Physical Progress: 60%
Completion date:30-10-2026

Current

Harappa Archaeological Park

Harmonisation of Façade – Mosque

Physical Progress: 40%
Completion date:30-06-2027

Before

Work in Progress

Harappa Archaeological Park

Harmonization of Boundary wall

Physical Progress: 100% Complete

Completed

Harappa Archaeological Park

Walkway

Physical Progress: 50%
Completion date:30-06-2027

Before

After

Harappa Archaeological Park

Viewing Tower

Physical Progress: 20%
Completion date:30-06-2027

Proposed

Current

Harappa Archaeological Park

Auditorium

Physical Progress: 80%
Completion date:30-09-2026

Before

After

Harappa Archaeological Park

Rest House Upgradation

Physical Progress: 98% Completed

Proposed

Current

Harappa Archaeological Park

Rest House Upgradation

Physical Progress: 98% completed

Before

After

Harappa Archaeological Park

Physical Progress: 98% completed

Rest House Upgradation

Before

After

Harappa Archaeological Park

Rest House

Physical Progress: 98% completed

During

After

Harappa Archaeological Park

Rest House Upgradation

Physical Progress: 98% completed

After

Harappa Archaeological Park

Rest House Upgradation

Physical Progress: 98%
completed

Current

Harappa Archaeological Park

Physical Progress: 75%
Completion date:30-09-2026

Hadhaba

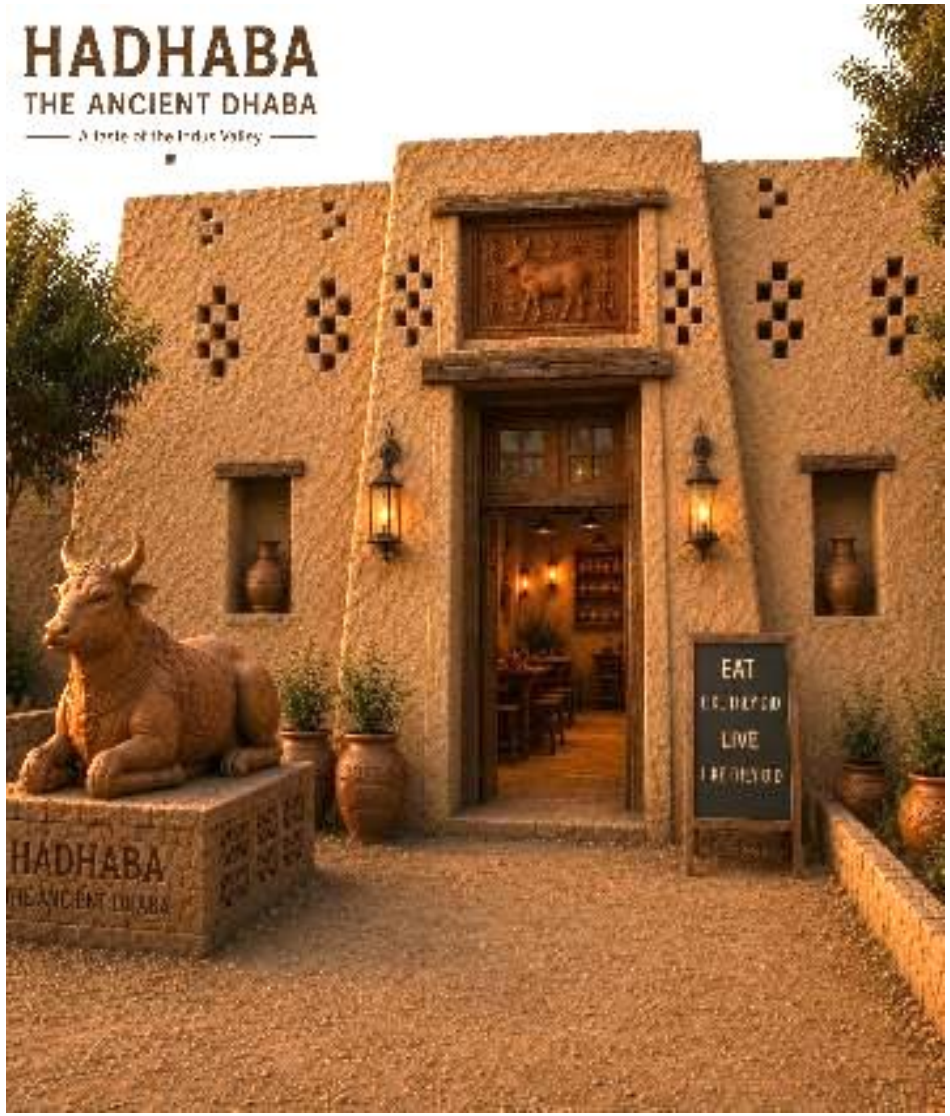

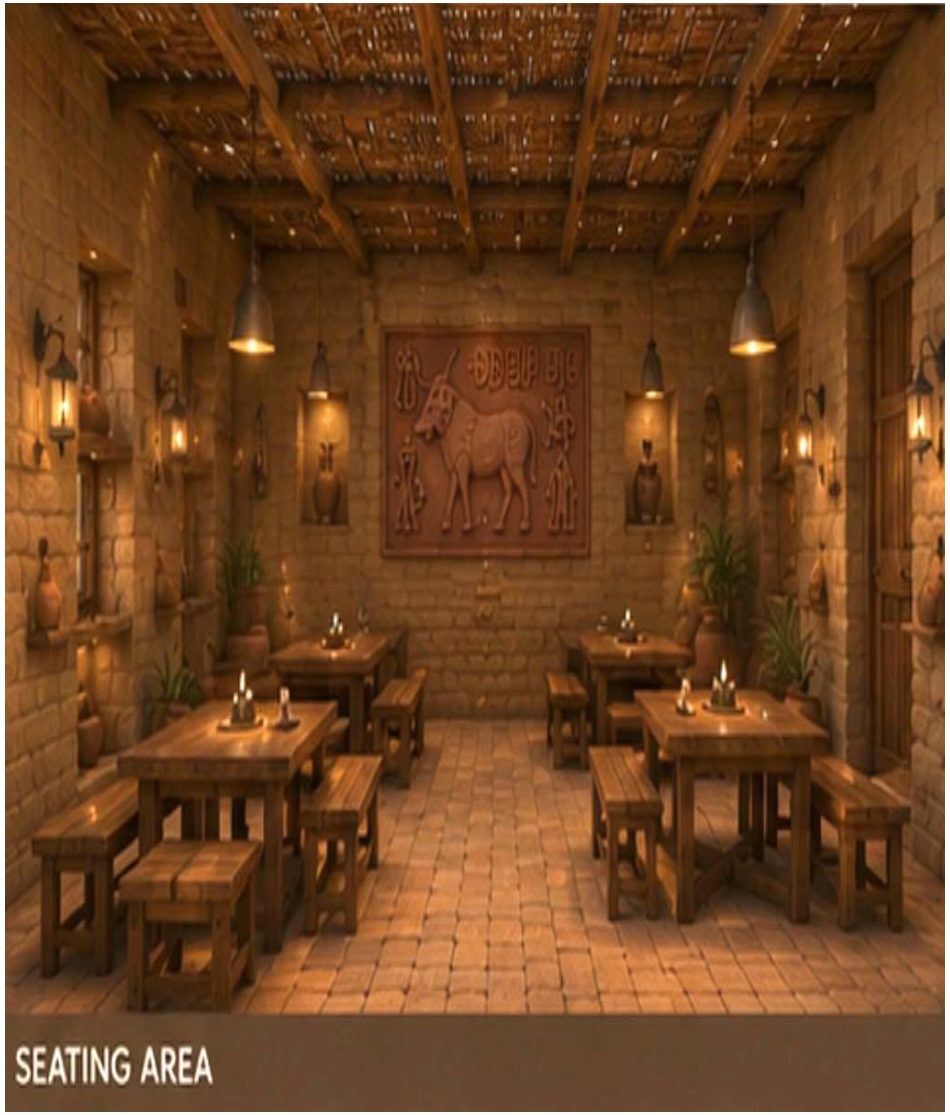

Proposed

Harappa Archaeological Park

Haddaba

Physical Progress: 75 %
Completion date:30-09-2026

Current

Harappa Archaeological Park

Harmonizing of Museum Complex

Physical Progress: 90%
Completion date:30-09-2026

Before

Proposed

Harappa Archaeological Park

Physical Progress: 90%
Completion date:30-09-2026

Conservation of Old Museum & Conversion into Cafeteria

Current

Harappa Archaeological Park

Physical Progress: 90%
Completion date:30-09-2026

Conservation of Old Museum & Conversion into Cafeteria

proposed

Current

Harappa Archaeological Park

Living History Village

Physical Progress: 50%
Completion date:30-10-2026

Proposed

Work in Progress

Harappa Archaeological Park

Village History

Physical Progress: 50%
Completion date:30-10-2026

Before

Current

Harappa Archaeological Park

Camping site

Physical Progress: 20%
Completion date:30-06-2027

Proposed

Current

Harappa Archaeological Park

Parking

Physical Progress: 35%
Completion date:30-06-2027

Proposed

Before

Current

Harappa Archaeological Park

Heritage Gateway Facilitation Hub(research center)

Physical Progress: 20%
Completion date: 30-06-2027

proposed

Current

Project Status & Reasons for Delay

- **The Citadel Hotel:** The work is currently delayed as the relocation and design phase has been completed.
- **Construction of Indus Valley Decipherment Center:** The progress is delayed due to the ongoing completion of the relocation and design phase.
- **Conservation of Archaeological Ruins:** The work is delayed due to a technical mistake made at the time of awarding the contract.

Site Focal Person	Phone Number
Imran Zahid	03324888110

Improvement, Revitalization, and Upgradation of TDCP Tourist Resort Kallar Kahar, District Chakwal

Responsibility: TAM / TDCP/ C&W
Cost: PKR **799.557** million

Scope of work
Construction of Guest House: Ground Floor ,First Floor, Second Floor Third Floor Construction of Boundary Wall (9" thick, 8' high) Construction of Reception Counters Water Supply C Sewerage Line Underground Water Tank Overhead Reservoir (O.H.R.) - 5,000 Gallons Provision of Cutting C Filling Provision of Fountain Construction of Ramp from 8'-0" to 37'-3" Provision of Water Supply System Improvement/Renovation of Existing/New Jetty Construction of Ticketing Booth Construction of Gate House (03 Nos.) Construction of Tuck Shop/Lake Side Restaurant (Ground Floor C First Floor) Construction of Live Kitchen Construction of Coffee Shop Construction of Café Construction of Yoga Meditation Space Construction of Glamping Pods Construction of Boundary Wall (9" thick, 8' high) Construction of Gate C Gate Pillars Construction of Sitting Area No. 1 C 2 Construction of Sitting Steps Provision of Gazebo Provision of Fountain Construction of Toilet Block for Male C Female Provision of Water Supply System Underground Water Tank Overhead Reservoir (O.H.R.) - 5,000 Gallons Provision of Additional Items

Progress so far
1. Scheme approved in DDSC. 2. TS is under progress.

Physical Progress 0%
Financial Progress 0%
Allocation CFY 2026-27: 30.000 M
Additional Funds Demand: 241.000 M

Project Start Date: **01 Jul 2026**
Completion Date as per PC-1: **30 Jun 2028**
Completion Date by TAM: **30 Jun 2028**

Next 30 Days Plans: 30 Aug 2026

Back

Improvement, Revitalization, and Upgradation of TDCP Tourist Resort Kallar Kahar, District Chakwal

Start Point

End Point

Improvement, Revitalization, and Upgradation of TDCP Tourist Resort Kallar Kahar, District Chakwal

PROPOSED DESIGNS

Improvement, Revitalization, and Upgradation of TDCP Tourist Resort Kallar Kahar, District Chakwal

PROPOSED DESIGNS

Back

ESTABLISHMENT OF CHAIR LIFT SYSTEM AND ALLIED INFRASTRUCTURE AT KOTLI SATTIAN, DISTRICT MURREE

Responsibility: TAM / TDCP
Approved Cost: **PKR 3,189 million**,
Revised cost 3,996 million

Physical Progress 00%
Financial Progress 00%
Allocation CFY 2026-27: 20 Mn
Additional Funds Demand: 2,498 Mn

Scope of Work
1. Supply and erection of E & M Chairlift Equipment **2. Civil Works** ▪ Ticket Booth ▪ Guard room ▪ Office Block ▪ Rest Room ▪ Restaurant 3. **External Works** 4.Consultancy (EPC-Owner's Engineer)

Progress So far
1. PDWP Approval: 10 December 2025 2. Tender and retender : 19 January 2026, Apr 1,2026. 3. Financial bid opened on 09.05.2026, **M/s ELITE-AIPEL (Dopplemayr) JV** declared lowest responsive technically qualified bidder. 4. Revised PC 1 sent for the revision of the scheme from 3.1 billion to 3.9 billion in accordance with the received bid.

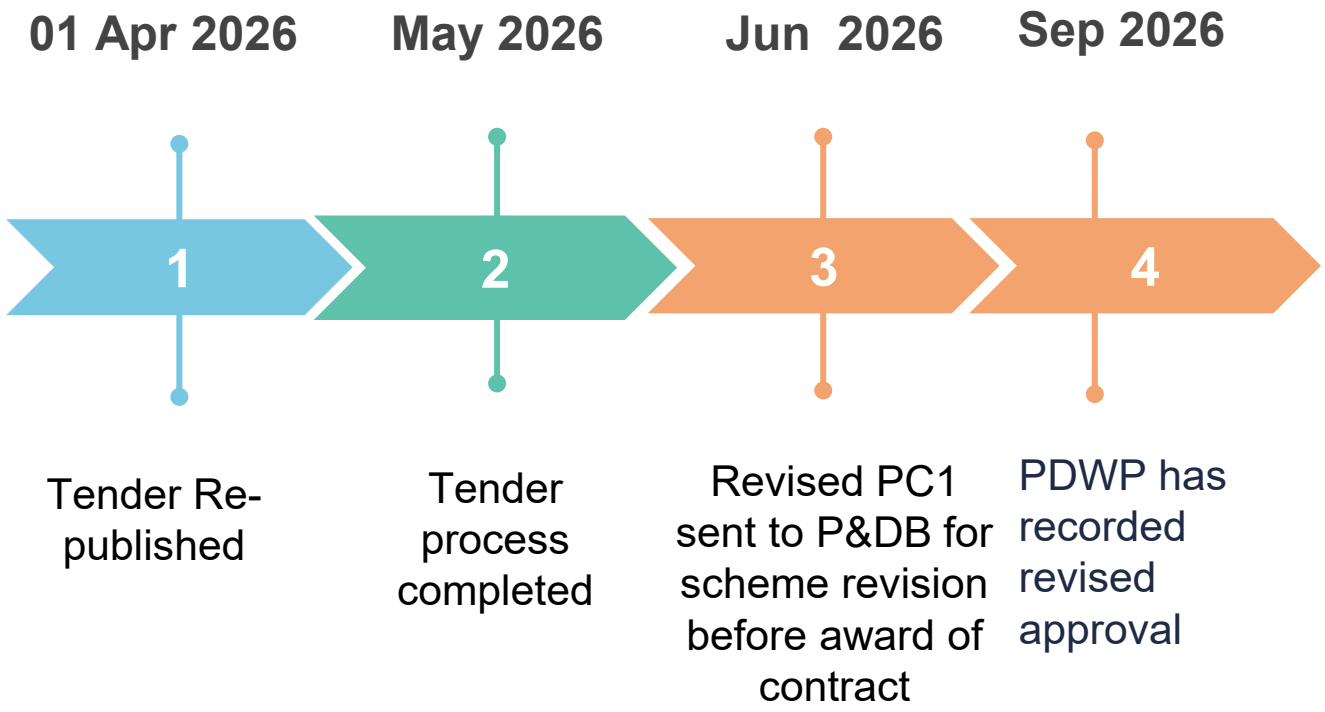

Project Start Date: **10 Dec 2025**
Completion Date as per PC-1: **30 Jun 2028**
Completion Date by TAM: **30 Jun 2028**

Next 30 Days Plans:
Final Award of Contract 30 Aug 2026
Commencement 15 Sep 2026

Back

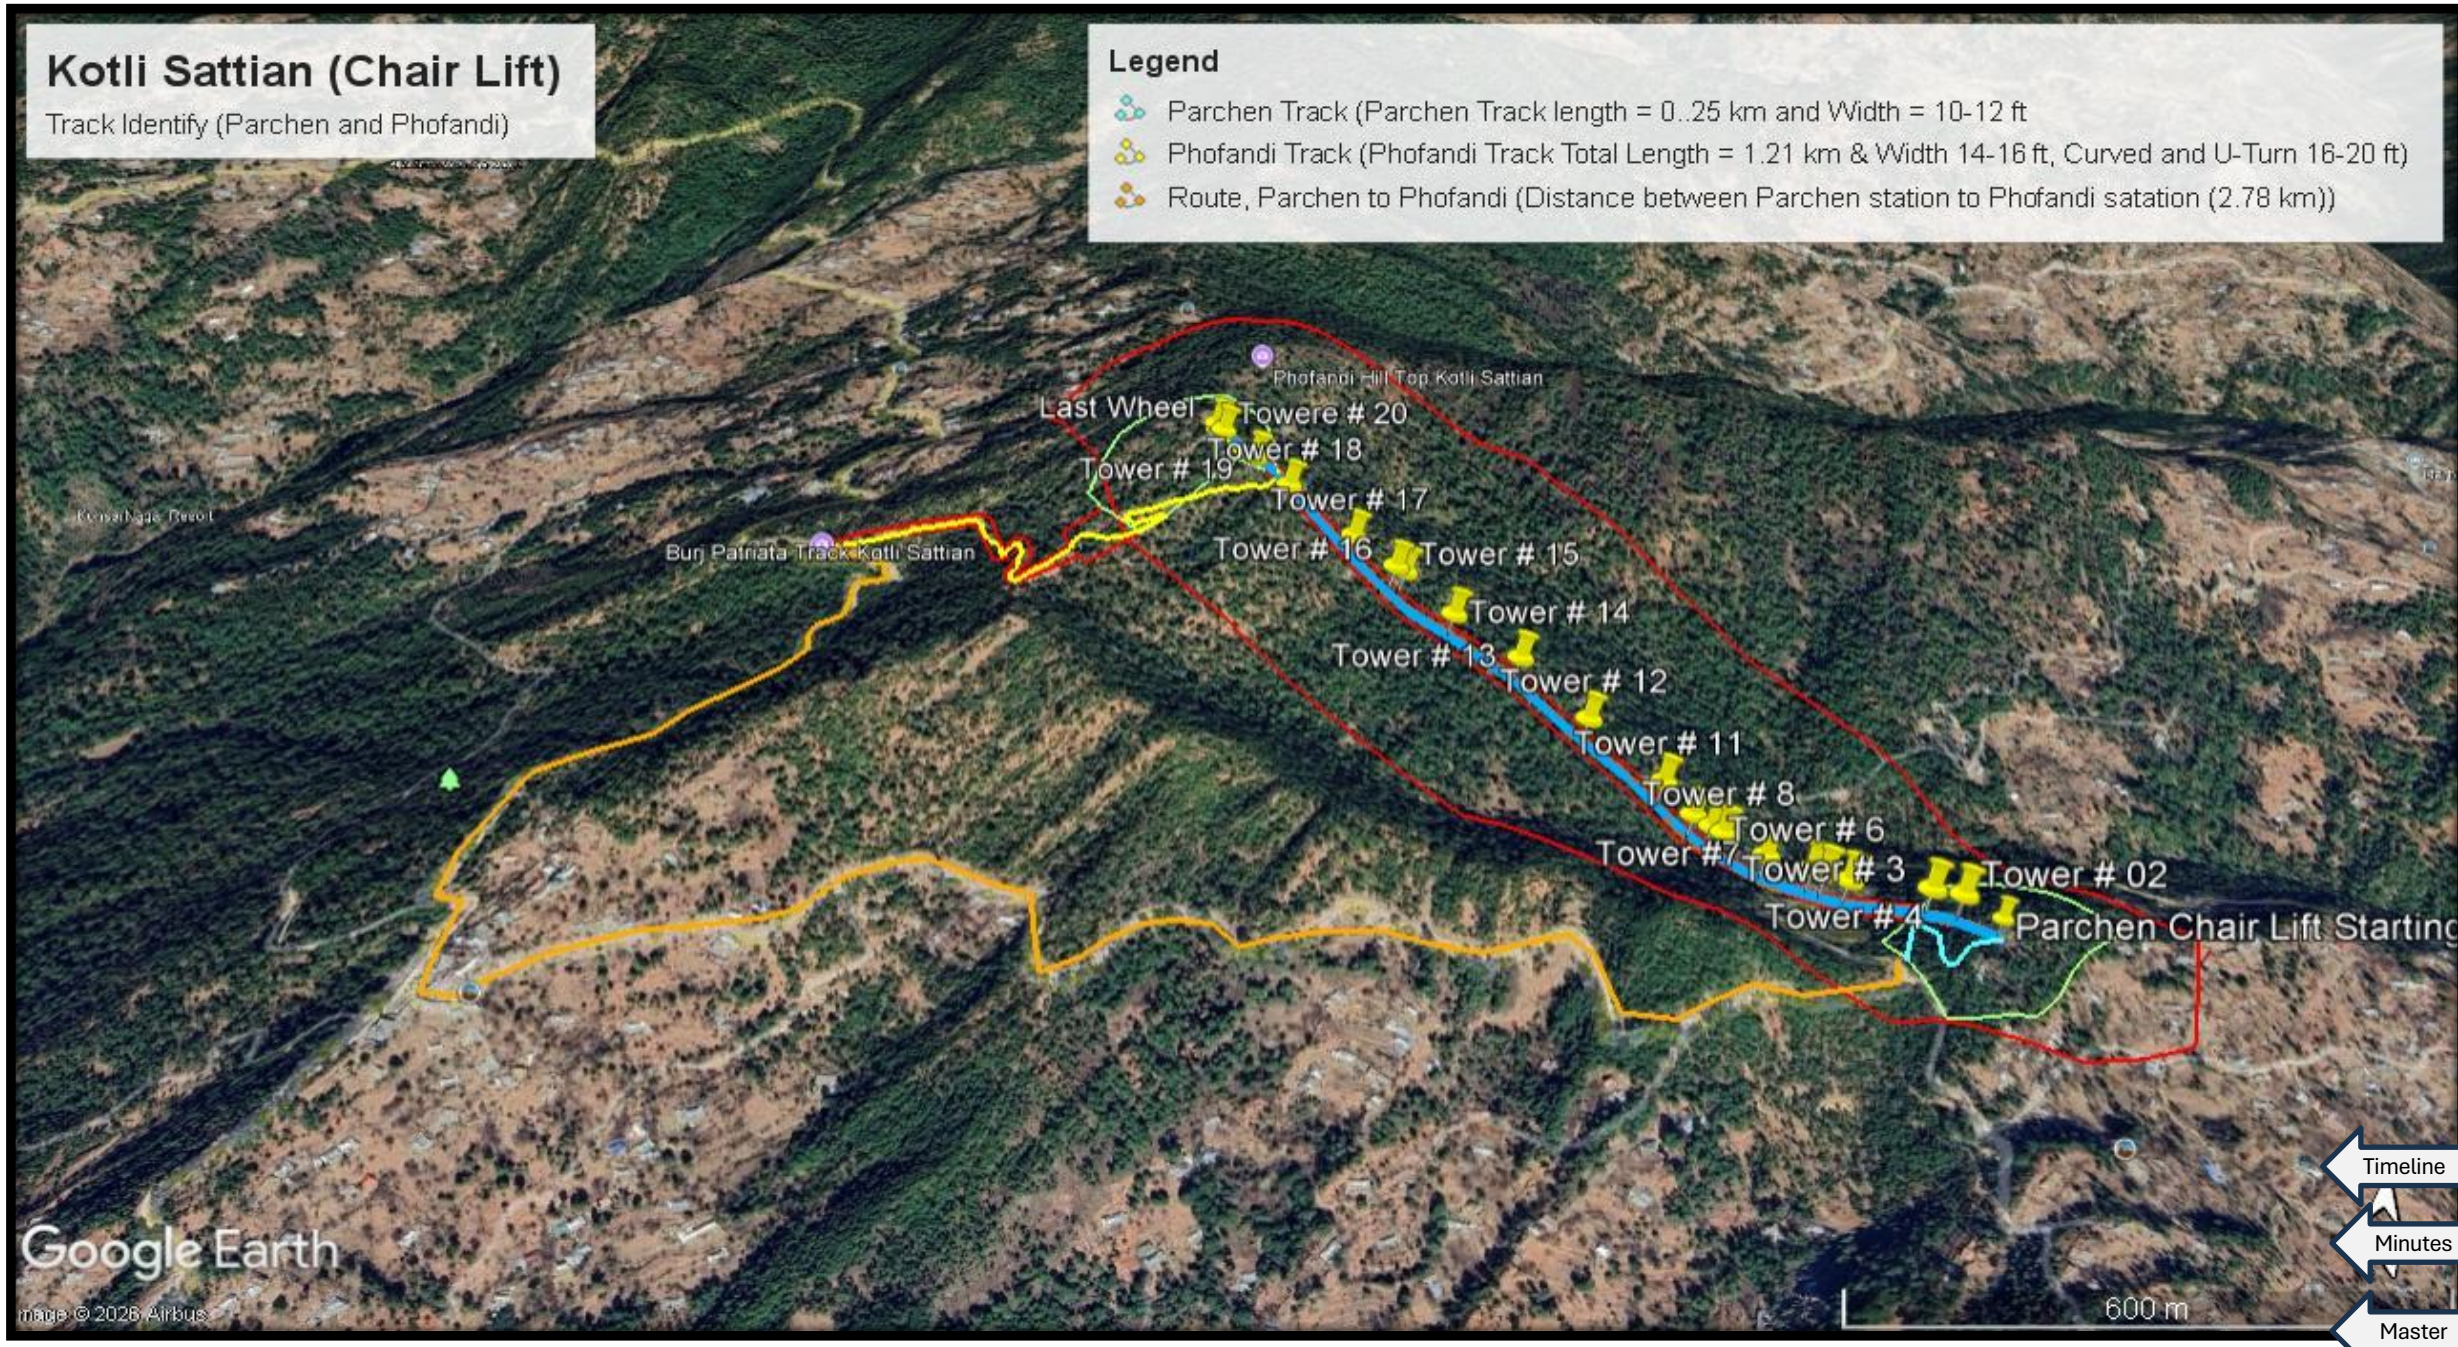
Kotli Sattian (Chair Lift)
Track Identify (Parchen and Phofandi)
Legend
Parchen Track (Parchen Track length = 0..25 km and Width = 10-12 ft
Phofandi Track (Phofandi Track Total Length = 1.21 km & Width 14-16 ft, Curved and U-Turn 16-20 ft)
Route, Parchen to Phofandi (Distance between Parchen station to Phofandi satation (2.78 km))
Phofandi Hill Top Kotli Sattian
Last Wheel
Towere # 20
Tower # 18
Tower # 19
Tower # 17
Bun Patriata Track Kotli Sattian
Tower # 16
Tower # 15
Tower # 14
Tower # 13
Tower # 12
Tower # 11
Tower # 8
Tower # 6
Tower # 7
Tower # 3
Tower # 02
Tower # 4
Parchen Chair Lift Starting
Google Earth
600 m
Timeline
Minutes
Master

Project Status & Reasons for Delay

• Revised PC 1 sent for the revision of the scheme from 3.1 billion to 3.9 billion in accordance with the received bid.

Site Focal Person	Phone Number
Zulfiqar Moin	03044936550

Back

Construction of Sky Glass Bridge at Panjpeer Rocks Tehsil Kotli Sattain District Murree

Responsibility: TAM / TDCP
Estimated Cost: PKR **2.4** billion

Scope of work
• Land Acquisition • Glass Bridge Deck Glass and Fabricated Steel • Architectural Works • Structures • Electrical Works • Plumbing and External Water Supply & Drainage • Road Works • Firefighting • Slope Stabilization

Progress
• Feasibility completed • Scheme stands approved from PDWP and included in ADP-2026-27 • Land Acquisition to start shortly

Physical Progress: 100% (Feasibility)
Financial Progress:
Allocation CFY 2026-27: 20 Mn
Additional Funds Demand: 980 Mn

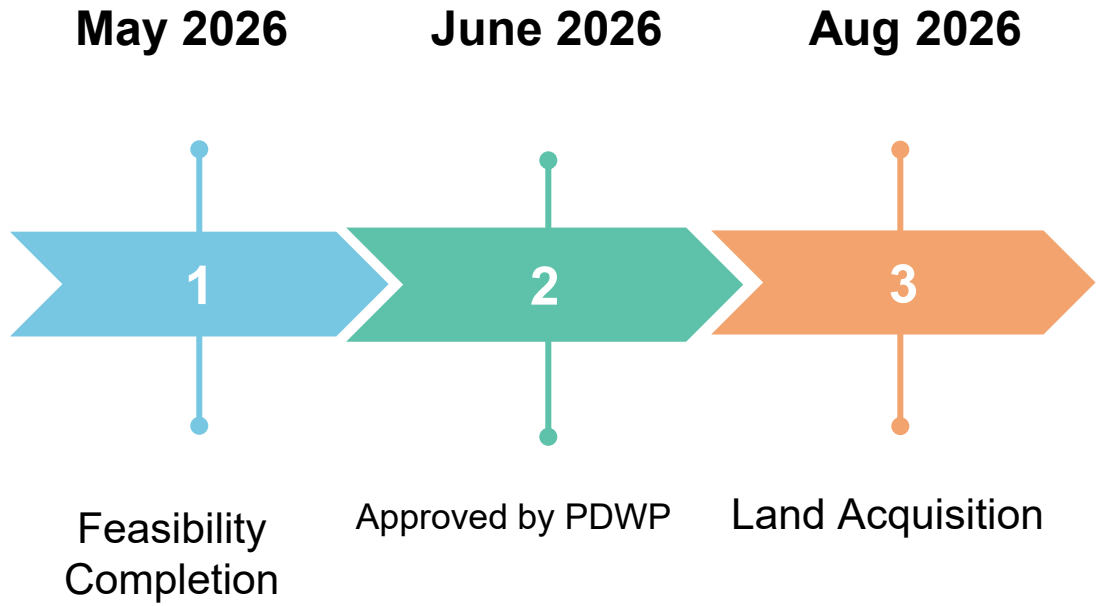

Project Start Date: **16 Feb 2026**
Completion Date as per PC-1: **30 Jun 2027**

Next 30 Days Plans:
Land Acquisition

Back

Construction of Sky Glass Bridge at Panjpeer Rocks Tehsil Kotli Sattain District Murree

Proposed Design

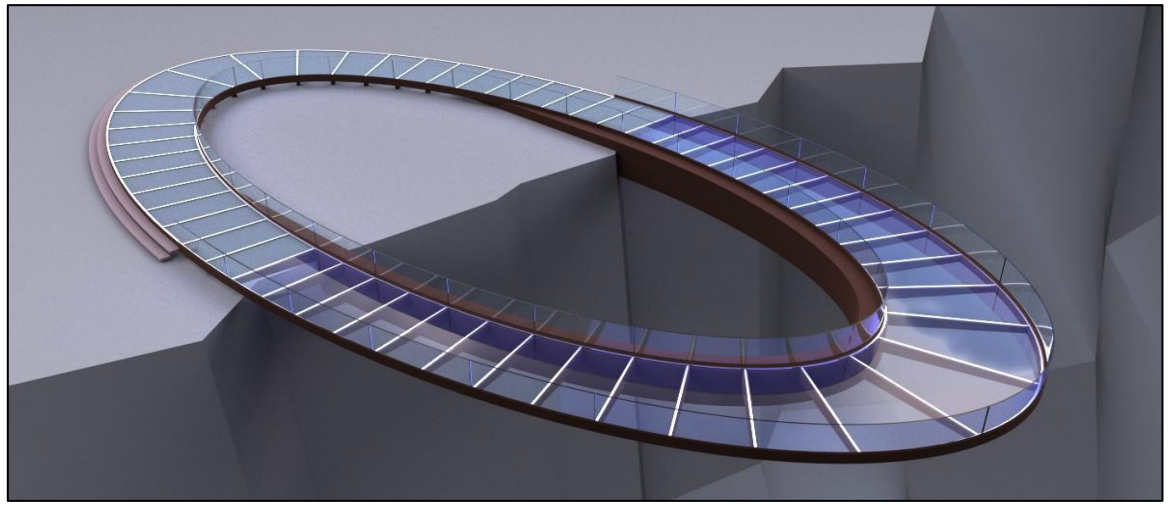

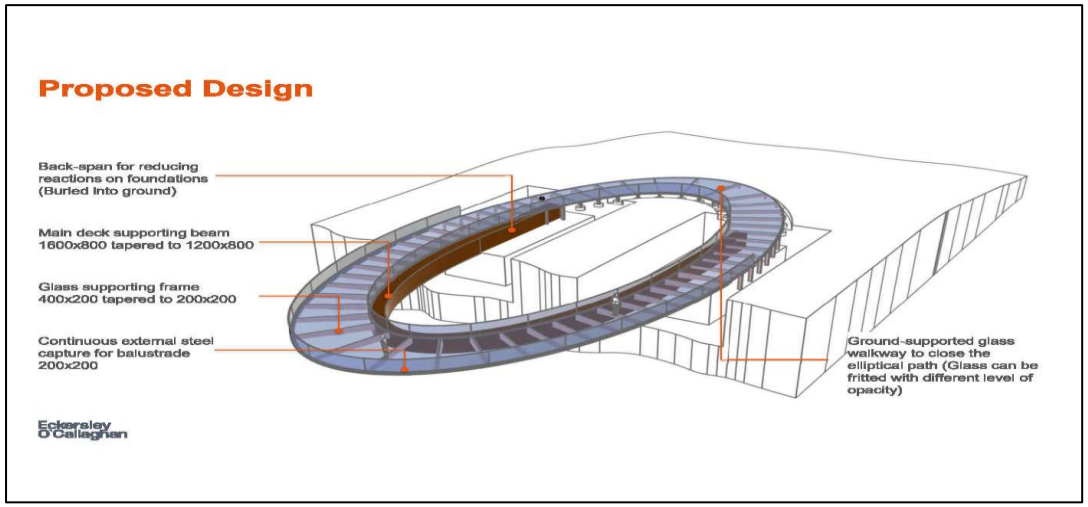

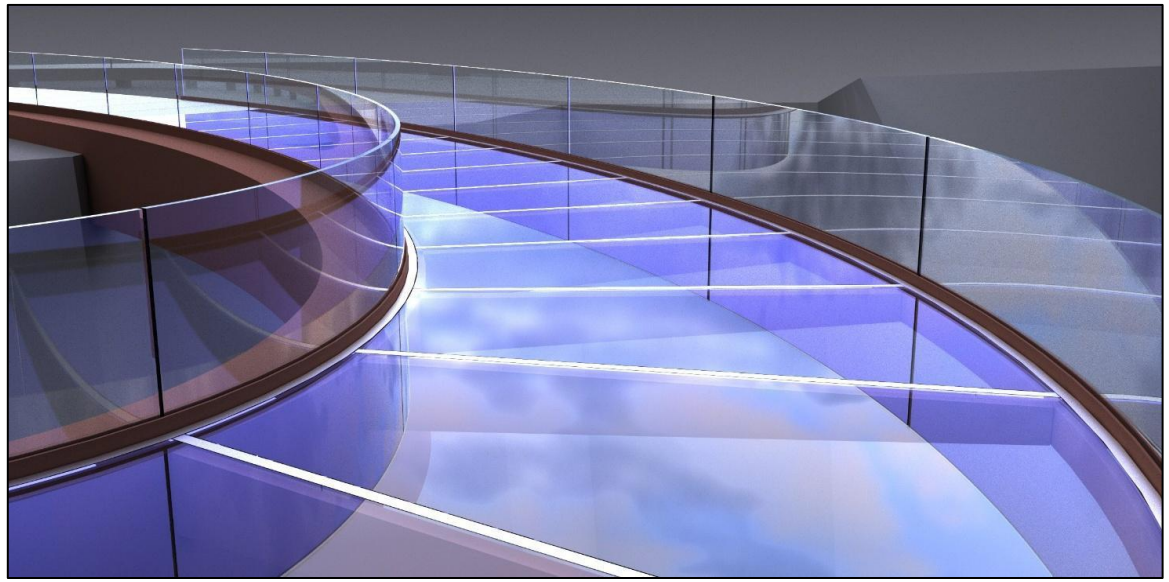

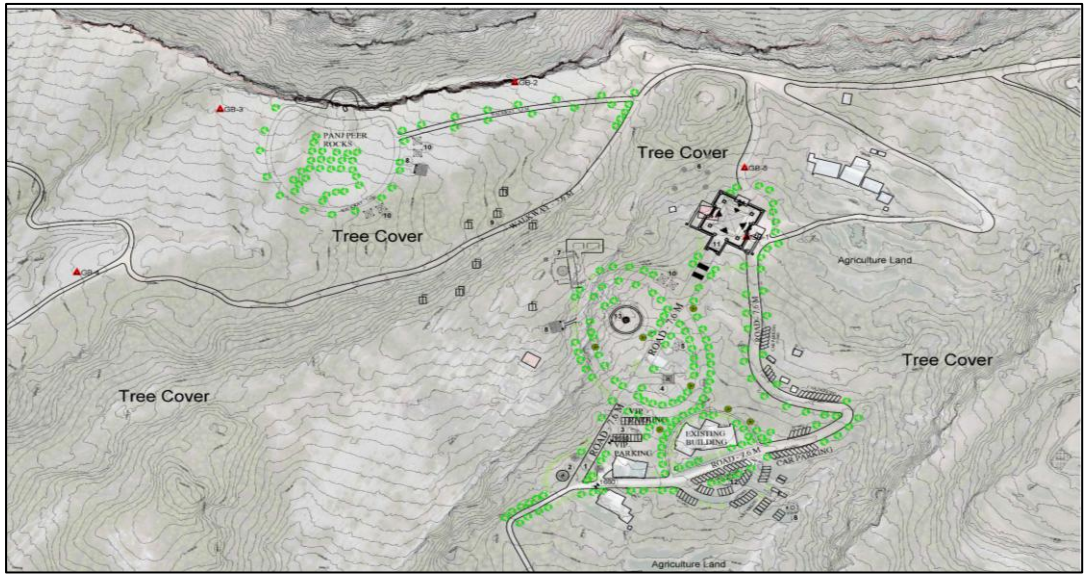

Construction of Sky Glass Bridge at Panjpeer Rocks Tehsil Kotli Sattain District Murree

Selected Site for Sky Walk Glass Bridge

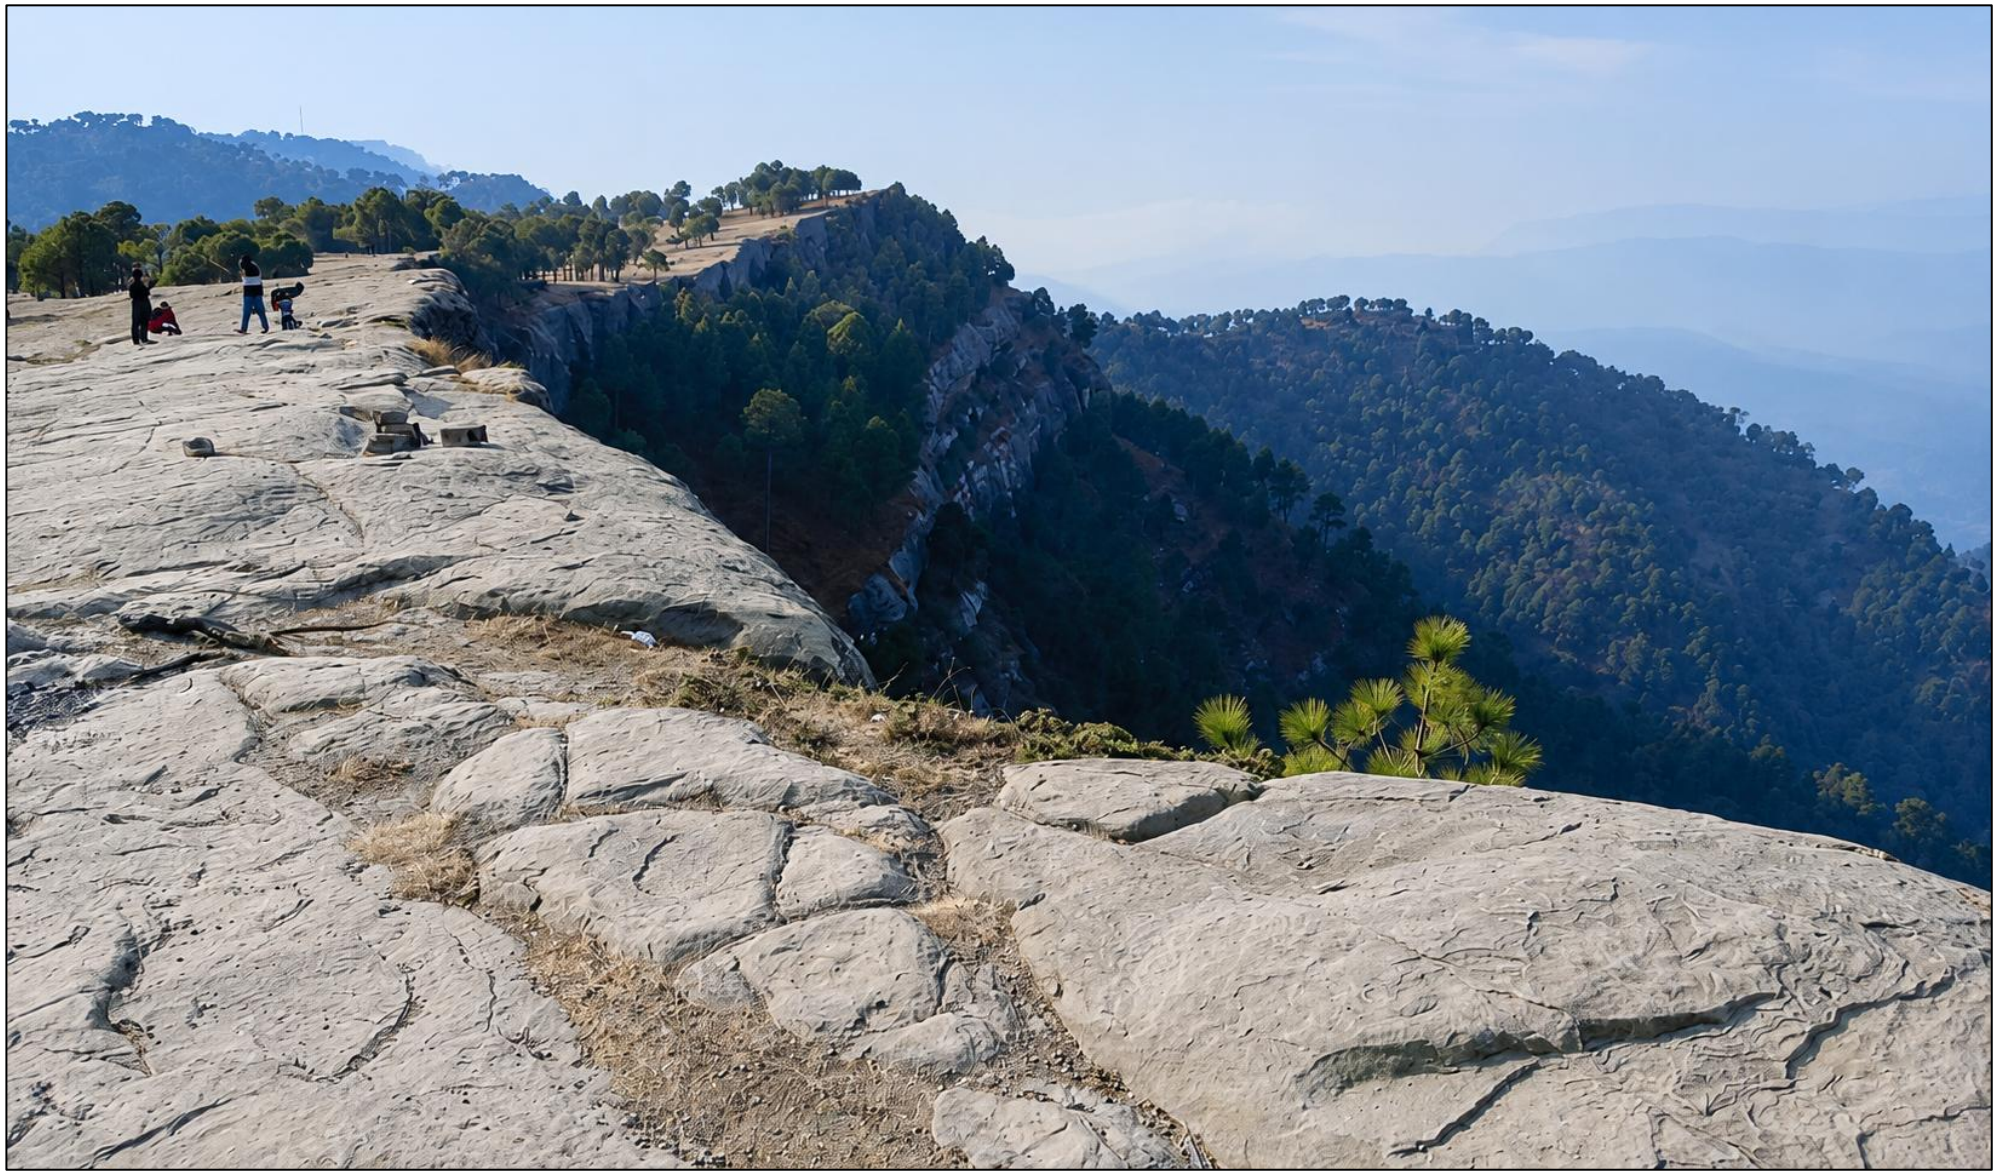

Project Status & Reasons for Delay

- Scheme stands approved from PDWP and included in ADP-2026-27.
- Land Acquisition to start shortly.

Site Focal Person	Phone Number
Unassigned	03000000000

Back

Preservation/Restoration, Improvement, Management and Upgradation of Derawar Fort, District Bahawalpur

Approved Cost: PKR 2490.79
Responsibility: TAM / ARCHAEOLOGY

Scope of work	Progress so far
1. Conservation of Front Fortification Wall	1. Completed 100%
2. Restoration of North Bastion and Baradari	2. Completed 100%
3. Restoration of Nawab's Residence within Civil Building	3. Completed 100%
4. Restoration of Civil Building	4. Completed 100%
5. Revival of Derawar Bazaar	5. Base work and excavation are in progress.11%
6. Conservation of Barracks	6. Debris has been removed, and the area has been cleaned 5%
7. Conservation of Haram	7. Conservation work is in progress on the walls of the Haram 14%
8. Conservation of Nawab's Residence within Haram	8. Debris has been removed, and the area has been cleaned 5%
9. Conservation of Fortification Wall	9. 0%
10. Revival of Toba	10. 0%
11. Conservation of Basement	11. 0%

Physical Progress:	20%
Financial Progress:	7%
Allocation (2026-27)	119.601 Million
Additional Funds Demand	50 Million

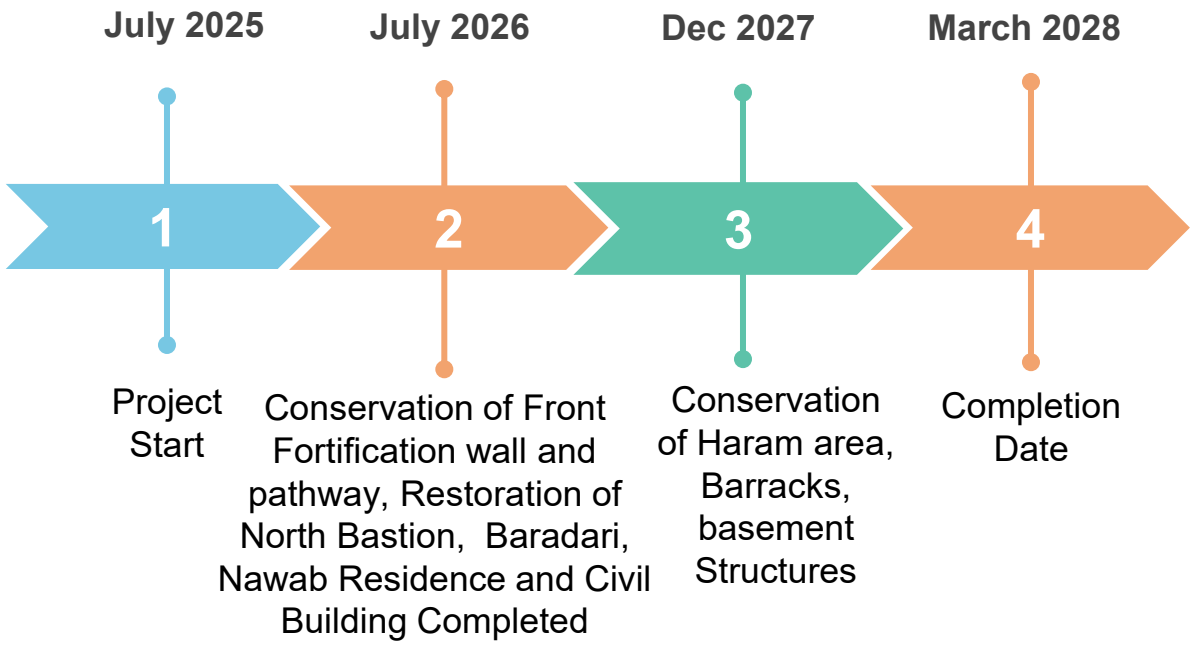

Project Start Date: **01 July 2025**
Completion Date by PC1: **30 July 2028**
Completion Date by TAM: **31 Mar 2028**

Next 30 Days Plans:
- Structural Consolidation of Barracks.
- Underpinning Work for Heritage Bazar
- Revival of Heritage Bazar
- Arrangement for stabilization of basement structure

Components of the Project

Component Name	Physical Progress	Expected Completion	Status
Conservation of Front Fortification Wall and Pathway	100%	Completed	On Track
Restoration of North Bastion and Baradari	100 %	Completed	On Track
Restoration of Nawab's Residence within Civil Building	100 %	Completed	On Track
Restoration of Civil Building	100 %	Completed	On Track
Revival of Derawar Bazaar	11%	15-10-2027	On Track
Conservation of Barracks	10%	31-12-2027	On Track
Conservation of Haram	14%	31-12-2027	On Track
Conservation of Nawab's Residence within Haram	05%	31-12-2027	On Track
Conservation of Fortification Wall	--	31-12-2027	Delayed
Revival of Toba	--	31-12-2027	Delayed
Conservation of Basement	--	31-12-2027	Delayed

● = On Trac
● = Delayed
● = Critical

Derawar Fort

Conservation of Baradari

Physical Progress: 100%
Completion date: 30-12-2025

Before

After

Derawar Fort

Passage to Baradari

Physical Progress: 100%
Completion date: 30-12-2025

Before

After

Derawar Fort

Passage to Baradari

Physical Progress: 100%
Completion date: 30-12-2025

Before

After

Derawar Fort

Civil Building Inside Derawar Fort

Physical Progress: 100%
Completion date: 30-01-2026

Before

After

Derawar Fort

Civil Building Inside Derawar Fort

Physical Progress: 100%
Completion date: 30-01-2026

Before

After

Derawar Fort

Civil Building Inside Derawar Fort

Physical Progress: 100%
Completion date: 30-01-2026

Before

After

Derawar Fort

Civil Building Inside Derawar Fort

Physical Progress: 100%
Completion date: 30-01-2026

Before

After

Derawar Fort

Western Bastion

Physical Progress: 100%
Completion date: 31-12-2025

Before

After

Derawar Fort

Western Bastion

Physical Progress: 100%
Completion date: 31-12-2025

Before

After

Derawar Fort

Nawab’s Residence inside Civil Building

Physical Progress: 100%
Completion date: 31-12-2025

Before

After

Derawar Fort

Nawab’s Residence inside Civil Building

Physical Progress: 100%
Completion date: 31-12-2025

Before

After

Derawar Fort

Physical Progress: 100%
Completion date: 31-12-2025

Before

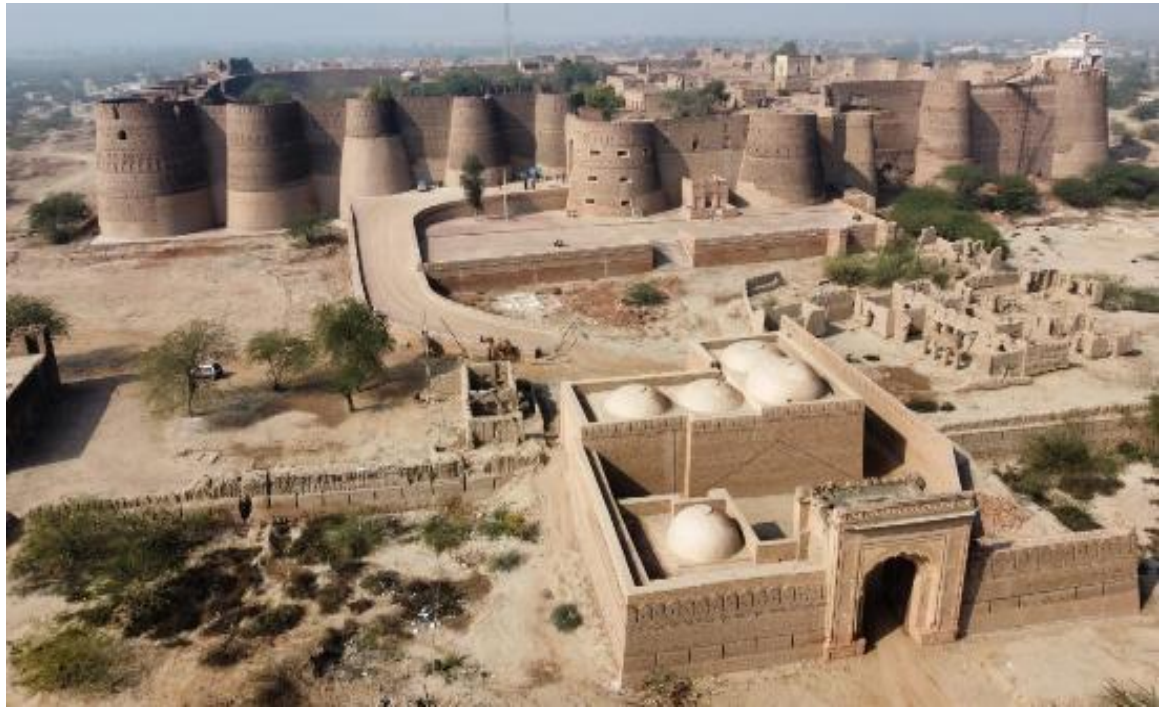

After

Derawar Fort

Revival of Derawar Bazar

Physical Progress: 11%
Completion date: 15-10-2027

Before

Work in Progress

Derawar Fort

Revival of Derawar Bazar

Physical Progress: 10%
Completion date: 15-10-2027

Work in Progress

Work in Progress

Derawar Fort

Conservation Work at Haram Area

Physical Progress: 14%
Completion date: 31-12-2027

Before

Work in Progress

Derawar Fort

Conservation Work at Haram Area

Physical Progress: 14%
Completion date: 31-12-2027

During

In progress

Derawar Fort

Physical Progress: 10%
Completion date: 31-12-2027

Derawar Fort

Back

Project Status

Work in Progress
Work is currently in progress only in the **Haram Area and Derawar Bazaar**.
No work is currently being carried out in the **Barracks Area**.
The pace of work is very slow.
Key Concerns
CCTV cameras have not yet been installed.
No proper system exists for daily progress reporting and monitoring.

Site Focal Person	Phone Number
M Sibtain	03057334649

Back

4.Preservation, Restoration, Improvement, Management and Upgradation of World Heritage Site Taxila, District Rawalpindi

Responsibility: TAM / ARCHAEOLOGY
Cost: PKR **3,972.6** million

Physical Progress	11%
Financial Progress	8.2%
Allocation (2026-27)	150 Million
Additional Funds Demand	120 Million

Scope of work

1. Heritage Gateway
2. Conservation of John Marshall Cottage
3. Cafeteria &Souvenir Shop
4. Lanscape of taxila museum campous
5. Archaeological Excavations Mohra muradu Dharmajika

Progress So far

1. The Gray Structure of the gateway has been completed. Finishing Works are in progress 62%.
2. The Conservation of John Marshall Cottage is in progress. 100%
3. The superstructure of the Souvenir Shop and cafeteria has been completed. Finishing Works in Progress. 70%
4. Dismantling work is in progress.
5. The work on the conservation of Mohra Muradu is in progress. 25%

Dharmajika is in progress.. 5%

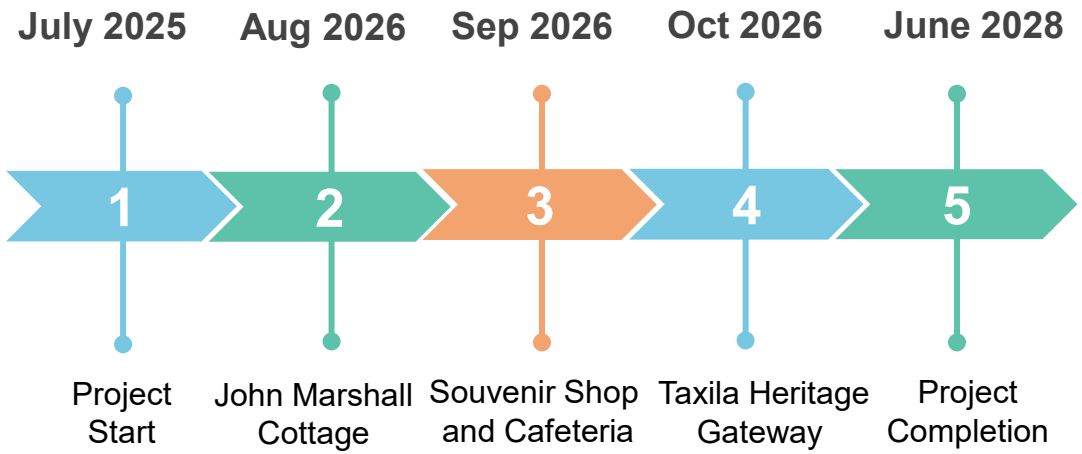

Project Start Date:	July 2025
Completion Date by PC1:	June 2028
Completion Date by TAM:	June 2028

Next 30 Days Plans:

- Start the Diversion Road at the Taxila Gateway.
- Complete Cafeteria grey structure.
- Complete Souvenir Shop remaining works.
- Continue conservation works at Dharmarajika.

Back

Components of the John Marshall Cottage

Component Name	Physical Progress	Expected Completion	Status
Stabilization of existing Structure	100%	Completed	On Track
Water Proofing	100%	Completed	On Track
Plaster and Paint Work	100 %	Completed	On Track
Electrification and Pluming Works	100%	Completed	On Track
Washrooms	100%	Completed	On Track
Wooden Flooring	100%	Completed	On Track
Marble Flooring	100%	Completed	On Track
Illumination	100%	Completed	On Track
Chandelier and Lighting	100%	Completed	On Track
Wooden Paneling	100%	Completed	On Track
Wooden Skirting	100%	Completed	On Track
Furniture	100%	Completed	On Track
Landscape	100%	15-08-2026	On Track
Wooden Doors and Windows	100%	31-08-2026	On Track

● = On Track
● = Delayed
● = Critical

Components of the Souvenir Shop

Component Name	Physical Progress	Expected Completion	Status
Alteration / Extension in Existing Structure	100%	Completed	On Track
Water Proofing	100%	Completed	On Track
Plaster and Paint Work	100 %	Completed	On Track
Electrification and Pluming Wiring	100%	Completed	On Track
Flooring	100%	Completed	On Track
Interior Works	0%	30-09-2026	On Track

= On Track
= Delayed
= Critical

Components of the Heritage Gateway Taxila

Component Name	Physical Progress	Expected Completion	Status
Water Boring and Electric Connection	100%	Completed	On Track
Foundation Work	100%	Completed	On Track
Super Structure Work	100%	Completed	On Track
Pouring of R.C.C Slab (03 Stages)	100%	Completed	On Track
Plaster on Surface	100%	Completed	On Track
Diversion Road	10%	15-08-2026	Delayed
Stone Tile Work	70%	30-10-2026	On Track
Stone Artifacts (Story of Buddha)	30%	30-10-2026	Delayed
Landscape	--	30-10-2026	Delayed
Illumination	--	30-10-2026	Delayed

= On Track
= Delayed
= Critical

Components of the Cafeteria

Component Name	Physical Progress	Expected Completion	Status
Alteration in Existing Structure	100%	Completed	On Track
Water Proofing	100%	Completed	On Track
Plaster and Paint Work	100 %	Completed	On Track
Electrification and Pluming Wiring	100%	Completed	On Track
Flooring	100%	Completed	On Track
Interior Counters	100%	Completed	On Track
Storage and pantry area	80%	15-08-2026	On Track
Front Glass Wall	60%	15-08-2026	On Track
External Verandah Extension	20%	30-09-2026	On Track
Interior Works	--	30-09-2026	On Track
Furniture	--	30-09-2026	On Track

= On Track
= Delayed
= Critical

Components of the Archaeological Sites Taxila

Component Name	Physical Progress	Expected Completion	Status
Conservation of Mohra Moradu Stupa & Monastery	05 %	31-12-2027	Delayed
Conservation of Sirkap Site	05 %	31-12-2027	Delayed
Conservation of Dharmarajika Stupa & Monastery	--	15-06-2028	Delayed
Conservation of Bhir Mound	--	15-06-2028	Delayed
Conservation of Saraikala (Prehistoric Mound)	--	15-06-2028	Delayed
Conservation of Giri Mosque and Tombs		15-06-2028	Delayed
Conservation of Buddhist Remains Around Bhallar Stupa and Monastery	--	15-06-2028	Delayed
Conservation of Kunala Stupa and Monastery	--	15-06-2028	Delayed
Conservation of Giri Complex of Monuments	--	15-06-2028	Delayed
Conservation of Kalawan Monastery	--	15-06-2028	Delayed
Conservation of Khader Mohra	--	15-06-2028	Delayed

= On Track
= Delayed
= Critical

Components of the Heritage BAZAAR

Component Name	Physical Progress	Expected Completion	Status
Tuf tiles	100%	15.06.2026	Delayed
Benches	0 %	15.06.2026	Delayed
Electric Work	0%	15-06-2028	Delayed

= On Track
= Delayed
= Critical

Components of the Heritage BAZAAR

Component Name	Physical Progress	Expected Completion	Status
Landscape of Taxila Museum Campus	5%	15.06.2026	= On Track

= On Track
= Delayed
= Critical

World Heritage Site Taxila

John Marshall Cottage

Physical Progress: 100%
Completion Date: 31.08.2026

Proposed

Work in Progress

World Heritage Site Taxila

Taxila Gate

Physical Progress: 62%
Completion Date: 30.10.2026

Proposed

Work in Progress

World Heritage Site Taxila

Diversion Road

Physical Progress: 90%
Completion Date: 30.10.2026

Proposed

Work in Progress

World Heritage Site Taxila

Souvenir Shop

Physical Progress: 60 %
Completion Date: 30.09.2026

Proposed

Work in Progress

World Heritage Site Taxila

Cafeteria

Physical Progress: 60 %
Completion Date: 30.09.2026

Proposed

Work in Progress

World Heritage Site Taxila

Cafeteria

Physical Progress: 60 %
Completion Date: 30.09.2026

Work in Progress

Work in Progress

World Heritage Site Taxila

Archaeological Excavations

Physical Progress: 10%
Completion Date: 15.06.2028

Before

After

World Heritage Site Taxila

facade

Proposed

Work in Progress

World Heritage Site Taxila

Heritage BAZAAR

Physical Progress: 90 %
Completion Date: 15.06.2026

● Delayed

Work in Progress

Work in Progress

World Heritage Site Taxila

MOHRA MURADU

Physical Progress: 5 %
Completion Date: 31.12.2027

Work in Progress

Work in Progress

World Heritage Site Taxila

Dharmajika

Physical Progress: 5 %
Completion Date: 15.06.2028

Work in progress

Work in Progress

World Heritage Site Taxila

Landscape of Taxila Museum Campus

Physical Progress: 5 %
Completion Date: 15.06.2028

Before

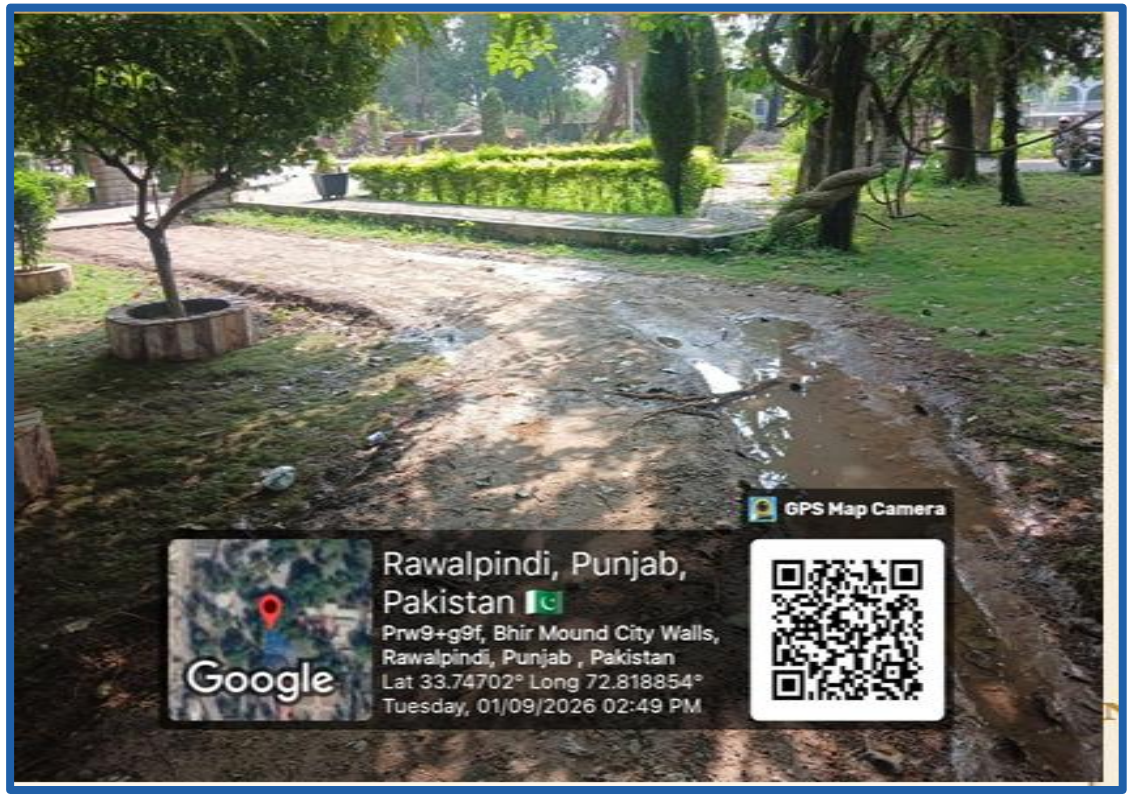

After

Project Status & Reasons for Delay

Work Progress

Mohra Muradu & Dharmarajika: Work is **stopped by UNESCO**.
Taxila Gate: Work was previously on hold due to the **Diversion Road**; the **Diversion Road is now approximately 90% complete**, and work in progressing.
Rest Area: 100% complete.
Cafeteria & Souvenir Shop: Grey structure is complete; **interior and exterior works**, including tiling, are currently in progress.
Craft Bazaar: 90% complete; remaining works include **benches and electrical work**.
Landscape of Taxila Museum Campus: Only **dismantling work has been carried out so far**.
Facade: Tender has not yet been received.
Overall Progress: The **pace of work is quite slow**.

Site Focal Person	Phone Number
Asfaq	+92 335 4409497

Back

Master Plan for Conservation, Rehabilitation, Improvement, and Upgradation of Lahore Museum

Presented by: Mehreen Maher

Master Plan for Conservation, Rehabilitation, Improvement, and Upgradation of Lahore Museum

Responsibility: TAM / IDAP Cost: PKR **4,391.53** million

Physical Progress	5%
Financial Progress	14%

Scope of work

Phase 1

1. Demolition work 17,936 SFT
2. Construction of East & West Wings (New Block) 34,924 SFT
3. Construction of Facilitation Center & Gazebos 3,188 SFT
4. External Works 7,500 SFT

Phase 1

1. Conservation of Existing Museum Building (Left Flank)
2. Artifacts Packing & Shifting
3. External Works 7,500 SFT
4. Content Development

Phase 3

1. Conservation of Existing Museum Building (Right & Central Flank)
2. External Work 7,500 SFT

Progress So Far

1. Building Assessment Report Completed. Assessment included Conservation as well as Museological aspects of the existing Building
1. Topographic survey done and reconciliation of the UNESCO report completed.
1. IDAP has devised execution plan in 3 phases. The same is going to be incorporated in the PC-1 Revision.
2. PC-1 revision with revised cost of **7,021.62 million** is being submitted to P&D

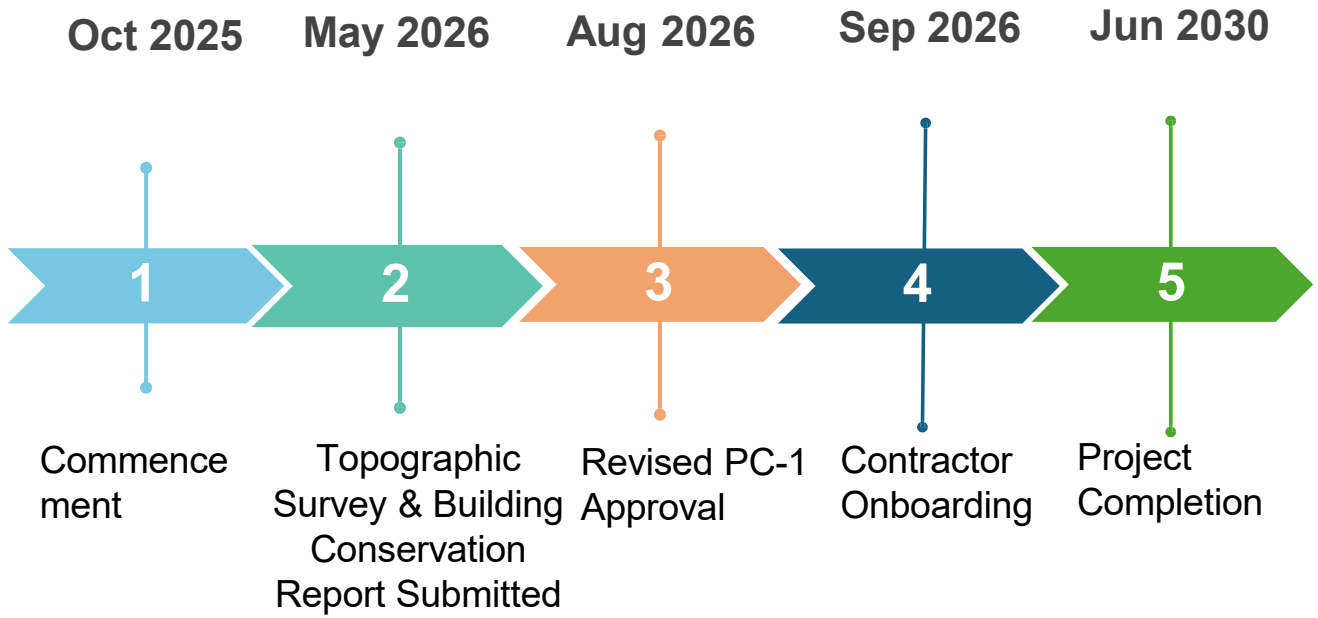

Project Start Date:	**20 Oct 2025**
Completion Date as per PC-I:	**30 Jun 2030**

Next 30 Days Plans:

Revised PC-1 Approval	31 Aug 2026
Bidding Process Initiated	30 Sep 2026

Components of the Project

Component Name (As per the PC-1 Revision Draft)	Physical Progress	Expected Completion	Status
Building Assessment Report submission	100%	30-05-2026	Completed
Demolition work 17,936 SFT	0%	30-11-2026	*-Phase 1* • On Track
Construction of East & West Wings (New Block) 34,924 SFT	0%	31-12-2027	*-Phase 1* • On Track
Construction of Facilitation Center & Gazebos 3,188 SFT	0%	30-12-2027	*-Phase 1* • On Track
Conservation of Existing Museum Building (Left Flank)	0%	30-06-2029	*-Phase 2* • On Track
Artifacts Packing & Shifting	0%	31-03-2029	*-Phase 2* • On Track
Content Development	0%	31-03-2029	*-Phase 2* • On Track
Conservation of Existing Museum Building (Right & Central Flank)	0 %	30-06-2030	*-Phase 3* • On Track
External Work 22,500 SFT	0%	30-06-2030	*-Phase 2 & 3*

● = On Track
● = Delayed
● = Critical

Master Plan for Conservation, Rehabilitation, Improvement, & Upgradation of Lahore Museum

Building Topographic Survey & Building Assessment Report Submitted

Physical Progress:100%
Completion Date: 30.05.2026

Survey Completed Renders:

Master Plan for Conservation, Rehabilitation, Improvement, & Upgradation of Lahore Museum Existing Building

Physical Progress:0%
Completion Date: 30.06.2030

Proposed

Master Plan for Conservation, Rehabilitation, Improvement, & Upgradation of Lahore Museum Existing Building

PROPOSED ELEVATION

Master Plan for Conservation, Rehabilitation, Improvement, & Upgradation of Lahore Museum Existing Building

PROPOSED ELEVATION

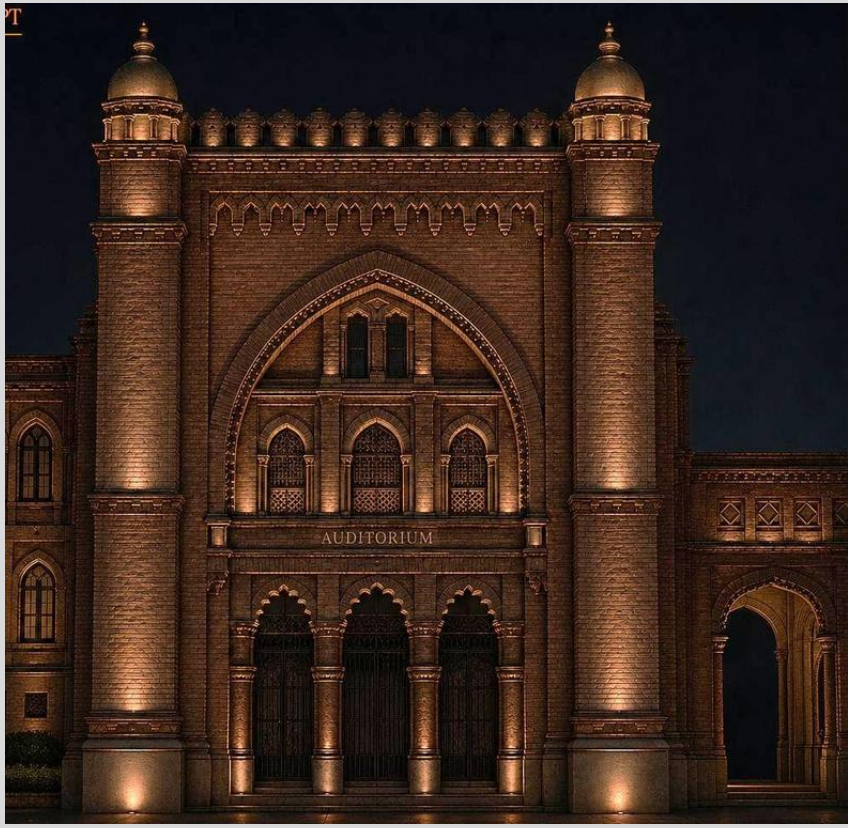

Master Plan for Conservation, Rehabilitation, Improvement, & Upgradation of Lahore Museum Existing Building

PROPOSED INTERIOR VIEW

Master Plan for Conservation, Rehabilitation, Improvement, & Upgradation of Lahore Museum Existing Building

PROPOSED EXTERIOR VIEWS

Master Plan for Conservation, Rehabilitation, Improvement, & Upgradation of Lahore Museum Existing Building

PROPOSED EASTERN & WESTERN BLOCKS

Master Plan for Conservation, Rehabilitation, Improvement, & Upgradation of Lahore Museum Existing Building

PROPOSED INTERIOR VIEWS

Progress & Coordination Remarks

MASTER PLAN

- Scheme under revision:
- Proposed revised cost: 7,021.62 million.
- Revision based on detailed studies and surveys conducted by Conservation and Museologist Consultants engaged by IDAP (Executing Agency).
- Pre-PDWP meeting on the revised PC-1 held on 11 August 2026.
- Annotated responses to Technical Appraisal comments and P&D Board observations have been submitted.
- Sr. Chief YAST scheduled a meeting on Sep 01, 2026 with consultant and IDAP to discuss cost and finalization of the working papers for the PDWP meeting.
- Deliberation held on IDAP's PC-1 regarding the Master Plan.
- As suggested by Kamil Khan Mumtaz Sb, it was decided that the PC-1 will first be vetted by the BoGs and subsequently placed before P&D/PDWP for approval.
- The Master plan has been approved.
- IDAP team is having a meeting with the Chief Technical at P&D today to sort out any repetitions, if identified.

Construction of Lahore Museum (New Block)

Responsibility: TAM / IDAP
Cost: PKR **5,605.65** million

Physical Progress	0%
Financial Progress	0%

Scope of work

1.Construction of New Museum Block with seven galleries and offices (2B+G+3) - 87,328 SFT
2.Shops + Prayer Hall (for 150) (G+1) – 12,132 SFT
1. External sitting shed – 2,978 SFT
1. Vehicular Parking (86 cars, 200 bikes)
2. Underground Connecting Corridor to connect with existing museum site: 3,456 SFT
3. Water feature (Pond)
4. Food & Souvenir shops
5. UGWT, Transformer & Generator Pads
6. Provision of 12 quarters and shifting of labs for the Irrigation Dept. 7,488 SFT

Progress So Far

1. Transfer of parcel land measuring 4.81 Kanal from the adjacent Irrigation building for construction of New Block under process
2. BRS Report on the Irrigation Structure for Demolition completed
3. PC-1 Revision Draft submitted in light of change in scope and designs of the Project. Revised project cost is **Rs.8,365.563 Million**
4. IDAP Floated Tender for Pre-Qualification of firms/consultants
1. Pre-PDWP meetings held and observations of the P&D Board Addressed

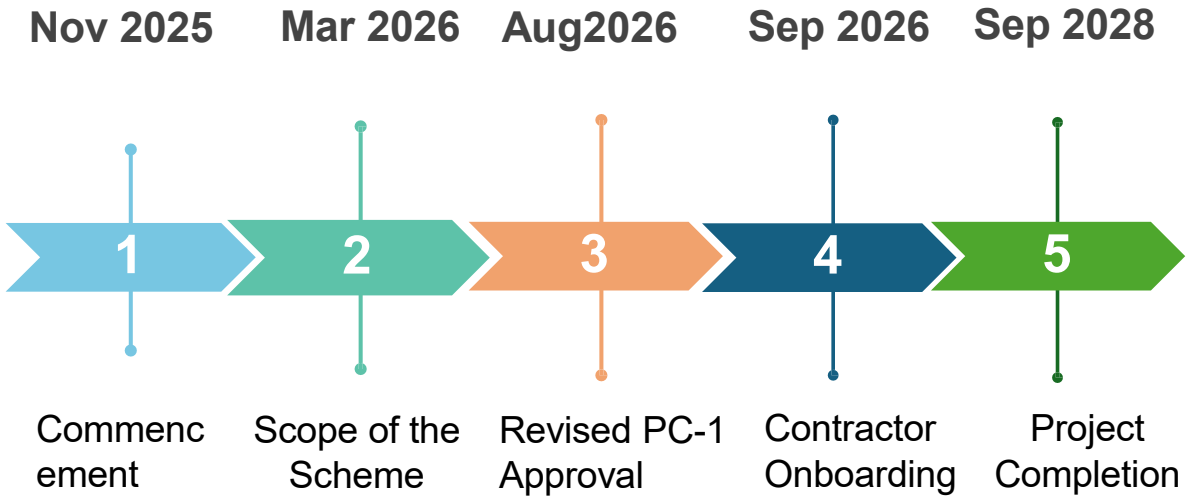

Project Start Date: 21 Nov 2025
Completion Date as per PC-I: 30 Sep 2028
Completion Date by TAM: **30 Sep 2028**

Next 30 Days Plans:

Approval of the Revised PC-1	31 Aug 2026
Bidding Process Initiated	30 Sep 2026

Components of the Project

Component Name (As per the PC-1 Revision Draft)	Physical Progress	Expected Completion	Status
Shops + Prayer Hall (for 150) (G+1) – 12,132 SFT	0%	30-09-2027	• On Track
External sitting shed – 2,978 SFT	0%	30-09-2027	• On Track
Water feature (Pond)	0%	30-09-2027	• On Track
Food & Souvenir shops	0%	30-09-2027	• On Track
Provision of 12 quarters for the Irrigation Dept. 7,488 SFT	0 %	30-09-2027	• On Track
Underground Connecting Corridor to connect with existing museum site: 3,456 SFT	0%	30-06-2028	• On Track
Construction of New Museum Block with seven galleries and offices (2B+G+3) - 87,328 SFT	0%	30-09-2028	• On Track
Vehicular Parking (86 cars, 200 bikes)	0%	30-09-2028	• On Track

● = On Track
● = Delayed
● = Critical

Renders:

Construction of Lahore Museum (NEW BLOCK)

CONSTRUCTION OF NEW BLOCK

Physical Progress: 0%
Completion Date: 30.09.2028

Proposed

Present

Construction of Lahore Museum (NEW BLOCK)

PROPOSED EXTERIOR VIEWS – MUSEUM

Construction of Lahore Museum (NEW BLOCK)

PROPOSED EXTERIOR VIEWS – MUSEUM

Construction of Lahore Museum (NEW BLOCK)

PROPOSED EXTERIOR VIEWS – MUSEUM

Construction of Lahore Museum (NEW BLOCK)

PROPOSED EXTERIOR VIEWS - SHOPS

Construction of Lahore Museum (NEW BLOCK)

PROPOSED INTERIOR VIEWS - ENTRANCE LOBBY/ RECEPTION/ WAITING

Construction of Lahore Museum (NEW BLOCK)

PROPOSED INTERIOR VIEWS - ARMS & ARMORY GALLERY

Construction of Lahore Museum (NEW BLOCK)

PROPOSED INTERIOR VIEWS - COINS & STAMPS GALLERY

Construction of Lahore Museum (NEW BLOCK)

PROPOSED INTERIOR VIEWS – CHINESE GALLERY

Construction of Lahore Museum (NEW BLOCK)

INTERIOR VIEWS - SIKH GALLERY

Construction of Lahore Museum (NEW BLOCK)

PROPOSED INTERIOR VIEWS – FREEDOM MOVEMENT

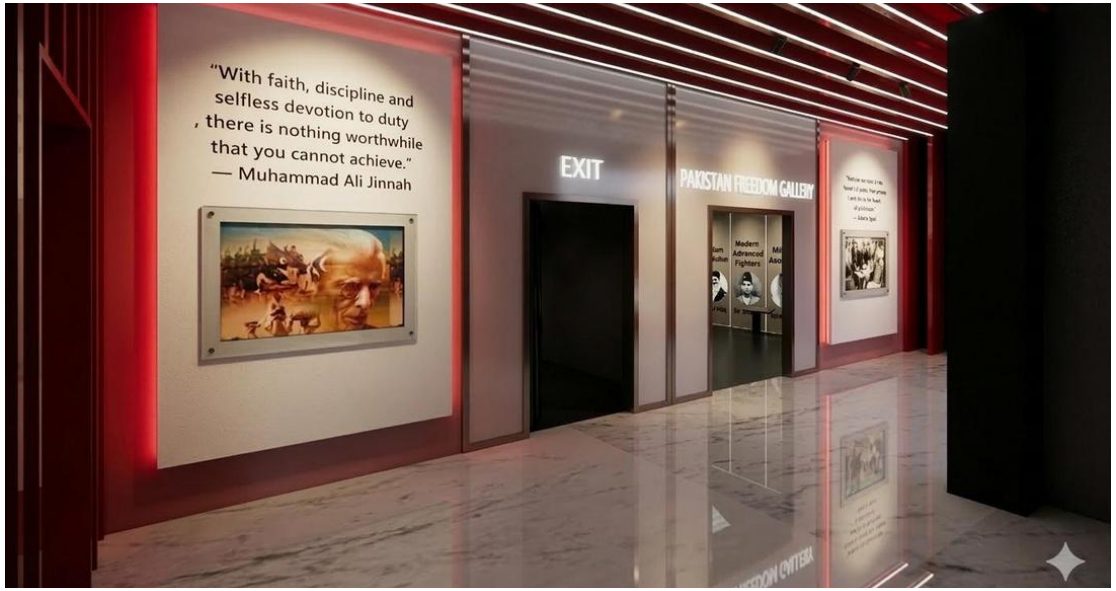

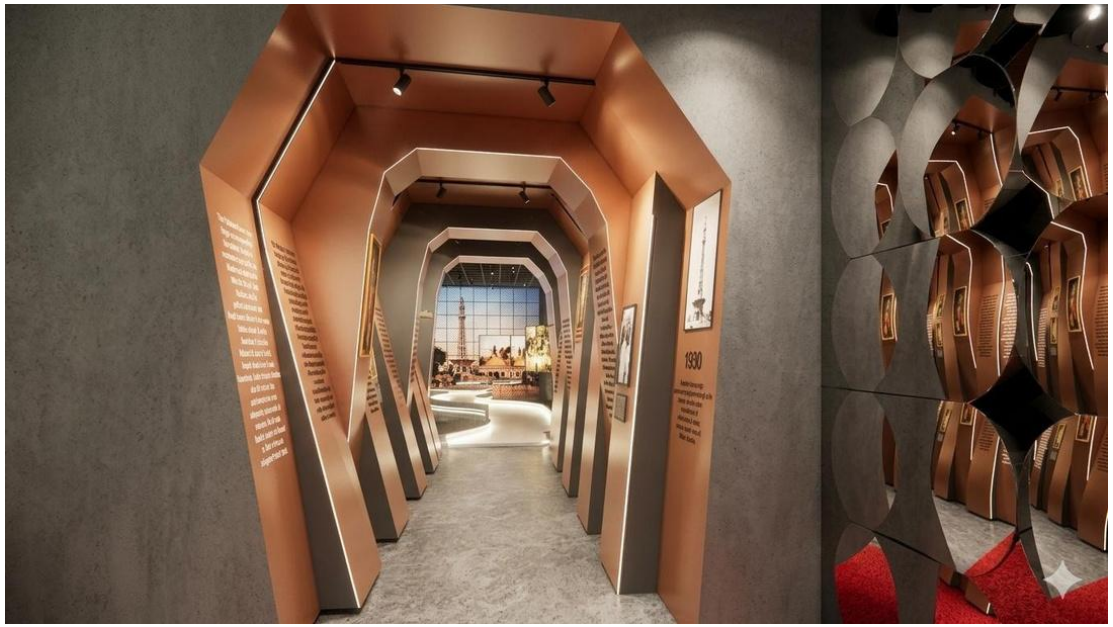

Construction of Lahore Museum (NEW BLOCK)

PROPOSED INTERIOR VIEWS - MOSQUE

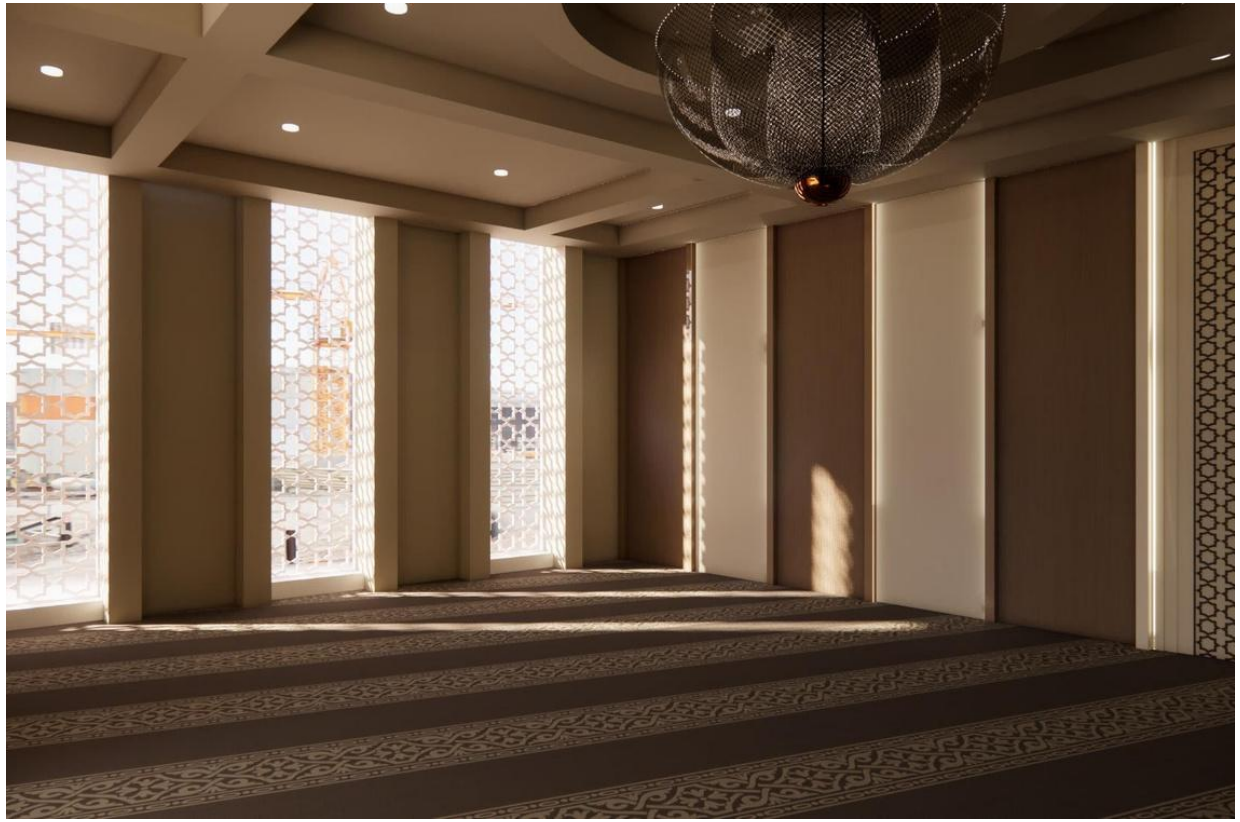

Progress & Coordination Remarks

NEW BLOCK

- Proposed revised cost: 8,365.563 million.
- P&D conducted two Pre-PDWP meetings on the revised PC-1
- Land transfer is in progress; expected to be completed within the next month.
- Tender for work award to be floated by IDAP (Executing Agency) in September 2026.
- PDWP meeting for approval expected soon.
- Rationalization of the proposed New Block is required.

Site Focal Person	Phone Number
Muhammad Umair	03224847017
